
From:

To:

Cc:

Bcc:

Subject:

(b) (7)(E)

(b)(6);(b)(7)(C)

RE: URGENT - DHS Contract Notification W9126G-17-F-0179 /

(b) (7)(E)

Date:

Thu Oct 05 2017 14:51:25 EDT

Attachments:

Check points IAA 1015X00161 (1).msg

HSBP1015X00161 Checkpoint Award sig 092615.pdf

HSBP1015X00161.1.pdf

HSBP1015X00161.2.pdf

See attached.

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, October 05, 2017 2:12 PM

To:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: URGENT - DHS Contract Notification W9126G-17-F-0179 / (b) (7)(E)

(b) (7)(E)

When the original IAA was obligated, when any mods were done and when plans changed to fund (b) (7)(E) design due to (b)(7)(E) cost being more than originally estimated.

(b)(6);(b)(7)(C)

OFAM Budget Officer

Business Operations Div. - Financial Mgmt. Branch

U.S. Customs & Border Protection

Phone: (b)(6);(b)(7)(C)

Mobile:

From: (b)(6);(b)(7)(C)

Sent: Thursday, October 05, 2017 2:05:59 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: RE: URGENT - DHS Contract Notification W9126G-17-F-0179 / (b) (7)(E)

(b) (7)(E)

(b)(6);(b)(7)(C) Can you specify what dates you are looking for?

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, October 05, 2017 2:03 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: URGENT - DHS Contract Notification W9126G-17-F-0179 /

(b) (7)(E)

(b) (7)(E)

I see that the separate SOW attachment is different than the SOW included in the IAA .pdf file for projects identified and POP and option year's, as well as overall cost. When was this separate SOW submitted, if ever.

The Word document file name indicated this is an IAA, but only contains an SOW, so we'll need the original IAA .pdf document.

The .pdf file appears to be the mod that was processed on 09/28 and signed by (b)(6);(b)(7)(C) (b) (5), (b) (7)(E), so I'll speak with her to better understand this from a Procurement perspective.

We still need dates provided in the summary document.

Thanks,

(b)(6);(b)(7)(C)

OFAM Budget Officer
Business Operations Div. - Financial Mgmt. Branch
U.S. Customs & Border Protection
Phone: (b)(6);(b)(7)(C)
Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, October 05, 2017 1:18:31 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: RE: URGENT - DHS Contract Notification W9126G-17-F-0179 /

(b) (7)(E)

(b) (7)(E)

Original IAA and mod attached.

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, October 05, 2017 12:51 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

gov>

Subject: RE: URGENT - DHS Contract Notification W9126G-17-F-0179 / (b) (7)(E)

(b) (7)(E)

All,

(b)(6);(b)(7)(C) is heading to the airport so I am passing along her comments/concern....

Based on the meeting that we had with DHS and CBP, we will need to be a bit more specific with providing dates in the history section to really get them a timeline of what was submitted when starting with the IAA.

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, October 5, 2017 12:32 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: URGENT - DHS Contract Notification W9126G-17-F-0179 /

(b) (7)(E)

(b) (7)(E)

See below for write up. We are pulling the other requested docs now – wanted to get this over you now though. Stay tuned.

IAA Synopsis:

(b) (5), (b) (7)(E)

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

-----Original Appointment-----

From: (b)(6);(b)(7)(C)

Sent: Thursday, October 05, 2017 10:31 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: URGENT - DHS Contract Notification W9126G-17-F-0179 / (b) (7)(E)

(b) (7)(E)

When: Thursday, September 28, 2017 10:30 AM-11:00 AM (UTC-05:00) Eastern Time (US & Canada).

Where: NP Rm. 737 - (b) (7)(E) PIN (b) (7)(E) (Host Code: (b) (7)(E))

To: Check po
From: (b)(6);(b)(7)(C)
Sent: Thur 10/5/2017 6:46:35 PM
Subject: Check points IAA 1015X00161
[HSBP1015X00161.2.pdf](#)
[HSBP1015X00161.1.pdf](#)
[HSBP1015X00161 Checkpoint Award sig 092615.pdf](#)

Attached is the initial IAA and 2 mods

The initial IAA was signed by the CO on 9/26/15

Mod # 1 was signed by the CO on 8/01/2016

Mod # 2 was signed by the CO on 9/28/2017

(b)(6);(b)(7)(C)

Chief, Financial Management Branch

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facility Management & Engineering

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (7)(E)

**DEPARTMENT OF HOMELAND SECURITY
U.S. CUSTOMS AND BORDER PROTECTION
INTERAGENCY AGREEMENT
(IAA)**

1. Agreement No. HSBP1015X00161	2. Modification No.	3. Order No.	4. Requisition No. 0020084839				
5. Period of Performance From 09/24/2015 To 09/24/2018		6. Statutory Authority	7. Date IAA Prepared 09/22/2015				
8. Requesting Agency Agency Name: DHS - Customs & Border Protection Office/Division: Customs and Border Protection POC: (b)(6);(b)(7)(C) Address: 24000 Avila Road Laguna Niguel CA 92677 POC Phone No.: (b)(6);(b)(7)(C)		9. Servicing Agency Agency Name: ARMY CORPS OF ENGINEERS Office/Division: POC: Address: 819 TAYLOR ST RM 3A14 FT WORTH TX 76102-0300 POC Phone No.:					
10. Scope of Work USACB to perform an assisted acquisition (as the Servicing Agency) for the DHS CBP (Requesting Agency) U.S. Border Patrol Texas Checkpoints Improvement Project.							
11. Delivery/Shipping Schedule See Attached Delivery Schedule							
12. IAA Amount		13. Billing and Payment					
Base Price of IAA	\$ (b) (4)	<table border="1" style="width: 100%; border-collapse: collapse;"> <thead> <tr> <th style="width: 50%;">Requesting Agency</th> <th style="width: 50%;">Servicing Agency</th> </tr> </thead> <tbody> <tr> <td> Locator Code: 70050800 DUNS #: DUNS# 879824324 Address: DHS - Customs & Border Protection Commercial Accounts Sect. 6650 Telecom Drive, Suite 100 Indianapolis IN 46278 POC: (b)(6);(b)(7)(C) POC Phone #: POC Fax #: POC Email: </td> <td> Locator Code: 00008736 DUNS #: 068112791 Address: USACE Attn: CBPC-PP 5722 Integrity Drive Millington TX38054 POC: POC Phone #: POC Fax #: POC Email: </td> </tr> </tbody> </table>		Requesting Agency	Servicing Agency	Locator Code: 70050800 DUNS #: DUNS# 879824324 Address: DHS - Customs & Border Protection Commercial Accounts Sect. 6650 Telecom Drive, Suite 100 Indianapolis IN 46278 POC: (b)(6);(b)(7)(C) POC Phone #: POC Fax #: POC Email:	Locator Code: 00008736 DUNS #: 068112791 Address: USACE Attn: CBPC-PP 5722 Integrity Drive Millington TX38054 POC: POC Phone #: POC Fax #: POC Email:
Requesting Agency	Servicing Agency						
Locator Code: 70050800 DUNS #: DUNS# 879824324 Address: DHS - Customs & Border Protection Commercial Accounts Sect. 6650 Telecom Drive, Suite 100 Indianapolis IN 46278 POC: (b)(6);(b)(7)(C) POC Phone #: POC Fax #: POC Email:	Locator Code: 00008736 DUNS #: 068112791 Address: USACE Attn: CBPC-PP 5722 Integrity Drive Millington TX38054 POC: POC Phone #: POC Fax #: POC Email:						
Modification Amount	\$0.00						
Assisted Acquisition Servicing Fee	\$0.00						
Total IAA Price	\$8,250,150.00						
14. Requesting Agency TAS No.		15. Servicing Agency TAS No.					
10	070 X0532000	10	00000000_3122				
20	070 X0532000	20	00000000_3122				
30	07020132017_0532000	30	00000000_3122				

16. Invoice/Payment Method

- ☐ Requesting Agency Initiate IPAC
☒ Servicing Agency Initiate IPAC
☐ Credit Card
☐ Other (explain below)

17. Billing Frequency

- ☐ Monthly
☐ Quarterly
☐ Semi-annually
☐ Annual
☐ Advanced Payment (explain below)
☐ Other (explain below)

18. Requesting Agency Accounting and Appropriation Data

10 6999.3221USCSGLCS0928040500Z1ST11139FM011602ALFQ 105203221
 TAS# 070 X0532000
 20 6999.3221USCSGLCS0928040500Z1ST11139FM011602ALFQ 105203221
 TAS# 070 X0532000
 30 6999.3221USCSGLCS0928040500Z1ST13461FM011602ALFQ 105203221
 TAS# 07020132017 0832

19. Approvals			
Program Officials		Requesting Agency	Servicing Agency
Name	(b)(6);(b)(7)(C)		(b)(6)
Title	BPFTT PMO Director		ECSC Director
Telephone No.	(b)(6);(b)(7)(C)		(b)(6);(b)(7)(C)
Fax No.			(b)(6);(b)(7)(C)
Email	(b)(6); (b)(7)(C)		(b)(6)
Signature On behalf of (b)(6); (b)(7)(C)	(b)(6);(b)(7)(C) (b)(6); (b)(7)(C) Date:		FOR (b)(6) Date: 09/25/2015
Funding Officials			
Name	(b)(6);(b)(7)(C)		(b)(6)
Title	Principal Management Branch Chief		Budget Officer
Telephone No.	(b)(6);(b)(7)(C)		(b)(6)
Fax No.			(b)(6)
Email	(b)(6);(b)(7)(C)		(b)(6)
Signature	(b)(6);(b)(7)(C) (b)(6); (b)(7)(C) Date:		(b)(6) Date:
Contracting Officials			
Name	(b)(6);(b)(7)(C)		
Title	Contracting Officer		
Telephone No.	(b)(6);(b)(7)(C)		
Fax No.			
Email	(b)(6); (b)(7)(C)		
Signature	(b)(6);(b)(7)(C) (b)(6); (b)(7)(C) Date: 9/26/15		Date:

DEPARTMENT OF HOMELAND SECURITY
U.S. CUSTOMS AND BORDER PROTECTION

INTERAGENCY AGREEMENT
(IAA)

INSTRUCTIONS

Block 1: Insert IAA number (automatic system populated).

Block 2: Insert modification number of the IAA (automatic system populated).

Block 3: Insert IAA order number (automatic system populated).

Block 4: Insert IAA requisition number (automatic system populated).

Block 5: Insert period of performance for the IAA.

Block 6: Insert statutory authority for the IAA.

Block 7: Insert date the IAA was prepared (automatic system populated).

Block 8: Insert requesting agency information.

Block 9: Insert servicing agency information.

Block 10: Insert a brief description of the IAA requirements (scope of work) and list the applicable attachments in this block. At a minimum, the attachments should include the IAA terms and conditions, statement of work, and analysis of alternative, if applicable.

Block 11: Insert the delivery and/or shipping schedule for the IAA or indicate where the delivery/shipping schedule may be found.

Block 12: Insert the base price of the IAA, modification amount, assisted acquisition servicing fee, and total IAA price--automatic system populated.

Block 13: Insert the billing and payment information for the requesting and servicing agency (requesting agency information automatic system populated).

Block 14: Insert the requesting agency TAS number for each line item (automatic system populated).

Block 15: Insert the servicing agency TAS number for each line item (automatic system populated).

Block 16: Check the invoice/payment method for the IAA and explain if "other" is selected.

Block 17: Check the billing frequency for the IAA and explain if "advanced payment" or "other" is selected.

Block 18: Insert the requesting agency accounting and appropriation data per line item (automatic system populated).

Block 19: Insert IAA approval information for the requesting and servicing agency pertaining to program officials, funding officials, and contracting officers. Include the date for each signature.

HSBP1015X00161

**ITEMS AND PRICES, DELIVERY SCHEDULE AND ACCOUNTING DATA
FOR
INTERAGENCY AGREEMENT: HSBP1015X00161**

I.1 SCHEDULE OF SUPPLIES/SERVICES

ITEM #	DESCRIPTION	QTY	UNIT	UNIT PRICE	EXT. PRICE
10	CMR, Check Points	1,000	AU	(b) (4)	
20	Check Point Study Phase II	1,000	AU		
30	(b)(7)(E) (b) (7)(E) Checkpoint	1,000	AU		

Total Funded Value of Award:

\$5,250,150.00

I.2 ACCOUNTING and APPROPRIATION DATA

ITEM #	ACCOUNTING and APPROPRIATION DATA	AMOUNT
10	6999.3221USCSGLCS0928040600Z1ST11139FM011602ALFQ 105203221 TAS# 070 X0632000	(b) (4)
20	6999.3221USCSGLCS0928040600Z1ST11139FM011602ALFQ 105203221 TAS# 070 X0632000	
30	6999.3221USCSGLCS0928040600Z1ST13461FM011602ALFQ 105203221 TAS# 07020132017 0632000	

I.3 DELIVERY SCHEDULE

DELIVER TO:	ITEM #	QTY	DELIVERY DATE
Customs and Border Protection (b)(7)(E)	10	1,000	09/24/2015 9/24/2018
	20	1,000	09/24/2015 9/24/2018
	30	1,000	09/24/2015 9/24/2018

Checkpoint IA-USACB

Terms and Conditions for Assisted Acquisitions

1 Purpose

- 1.1 The terms and conditions of this Interagency Agreement (IA) govern the acquisition assistance provided to the U.S. Customs and Border Protection (CBP), the Requesting Agency, by the U.S. Army Corps of Engineers (USACE), the Servicing Agency.
- 1.2 The Servicing Agency's obligation to provide supplies or services under this IA and the Requesting Agency's obligation to provide funding does not arise until all applicable requirements are satisfied and the IA is signed by the required parties at CBP and USACE.

2 Authority

CBP and USACE are executing this IA that supports an Interagency acquisition under the authority of Economy Act, 31 U.S.C. 1535.

3 Scope

3.1.1 Organizations Authorized to Request Acquisition Assistance

The following organizations within the Requesting Agency are authorized to obtain assistance from USACE:

Border Patrol Facilities and Tactical Infrastructure Program Management Office (BPFTI PMO), Facilities Management and Engineering (FM&E)

3.1.2 Organizations Authorized to Provide Acquisition Assistance

The following organizations within the Servicing Agency are authorized to provide acquisition assistance to the Requesting Agency:

Fort Worth District, Southwestern Division
Engineering, Construction Support Office (ECSO)
USACE Supporting Districts, as required by the work in the Statement of Work (SOW), through the ECSO

3.1.3 Limitation(s): The following restrictions apply: None

4 Description of Products or Services to be Acquired

See Statement of Work for Texas Checkpoints Improvement Project.

5 Period of Agreement

This IA becomes effective when signed by the Contracting Officer (CO) and Program Manager (PM)/Requirements Official (RO) of the Requesting Agency and the authorized

Checkpoint III (IA) - USACE

official of the Servicing Agency and remains in effect until May 31, 2022 unless agreed to and amended by both the Servicing and Requesting Agencies. The countersigned IA must be returned to the CBP CO or this IA may be subject to cancellation.

6 Roles, Responsibilities of Servicing Agency and Requesting Agency

The effective management and use of IAs is a shared responsibility of the Requesting Agency and the Servicing Agency. The parties hereby agree to the following roles and responsibilities, which are derived from guidance issued by the Office of Management and Budget's Office of Federal Procurement Policy (OfPP), available at:

http://www.whitehouse.gov/sites/default/files/omb/assets/procurement/iaoc_revised.pdf

6.1 Requesting Agency

- Work closely with the Servicing Agency to establish requirements that are clear and complete.
- Be a good steward of the agency's funds by ensuring appropriate internal controls are in place to ensure interagency acquisition activities are consistent with sound project management, contracting, and fiscal practices.
- Work in close collaboration with the Servicing Agency throughout the project lifecycle. Make trained and qualified personnel available to support key activities, including the timely preparation and execution of funding documents, compliance with customer-unique laws and policies, acquisition planning, source selection evaluation, and contract administration.
- Provide accurate and timely information to support the Servicing Agency in effectively awarding and managing the contract, including evaluation of contractor performance and prompt payment.
- Review the general terms and conditions of the IA with the Servicing Agency no less than annually and make amendments as necessary.

6.2 Servicing Agency

- Be a good steward of the Requesting Agency's funds by ensuring appropriate internal controls, and applying sound project management, contracting, and fiscal practices.
- Manage all phases of the project lifecycle from requirements development through contract closeout, as agreed in the IA.
- Work in close collaboration with the Requesting Agency throughout the project lifecycle, responding promptly to inquiries from the Requesting Agency, which may include matters regarding process, project status, and funds balance, among others. Ensure timely delivery of acceptable goods and services.
- Maintain accurate records and files associated with acquisition assistance activities. Review the general terms and conditions of the IA with the Requesting Agency no less than annually and make amendments as necessary.
- Help the Requesting Agency comply with the bona fide needs rule by:
 - o managing funds according to the Requesting Agency's guidance; o
 - o recording transactions in a timely fashion; and

CheckpointIAA-USACB

- o implementing and exercising controls to ensure compliance with all applicable statutory and regulatory fiscal requirements.

7 Billing and Payment

- 7.1 The Requesting Agency will pay the Servicing Agency for the reimbursement of overhead costs as identified in the specific project requirement documents and costs of each contract or task/delivery order. Billings may include the amounts due under the contract or order plus any identified assisted acquisition service costs. CBP reimbursement of costs incurred in the performance of work described in the Statement of Work (SOW) will be made via the U.S. Treasury Intra-Government Payment and Collection (IPAC) System.
- 7.2 Payments are delinquent when they are pending sixty (60) or more calendar days from the date of the billing. When billings remain delinquent and the Requesting Agency has not indicated a problem regarding the services, the Servicing Agency will not award any new contract/orders or modifications to existing contracts or orders on behalf of the Requesting Agency.

8 IA Funding

The Servicing Agency is limited to recovery of only actual costs incurred. The Servicing Agency shall notify the Requesting Agency's Contracting Officer's Representative (COR) when the costs incurred, together with costs of any outstanding commitments, total 80 percent (%) of the obligated estimated cost ceiling of this IA. The Servicing Agency shall make no other commitments or expenditures beyond 100% of the funds obligated and shall be excused from further performance of the work unless, and until, the Requesting Agency CO, or other authorized official, increases the total obligation by modification to the IA.

- 8.1 Special Terms for One-year Funding. The total amount to be reimbursed shall not exceed the total amount obligated for the current fiscal year. If this IA is issued under the authority of the Economy Act (31 U.S.C. 1535) and the Servicing Agency uses in-house resources to perform part or all of the agreement, in-house work must stop on September 30th of the current fiscal year, and any unexpended funds for work to be performed in-house must be de-obligated. In-house work that will continue in the next fiscal year must be funded, effective October 1st, with the new fiscal year's funds. If the Servicing Agency obligates the fiscal year funds by awarding a contract or an order prior to the expiration of the fiscal year, the funds obligated by such award do not need to be de-obligated after September 30.
- 8.2 Special Terms for Greater Than One-year Funding. For longer than one-year (e.g. two-year, no-year) funding availability, the dates are extended appropriately.

9 Contract Termination, Disputes and Protests

CheckpointIAA-USACE

- 9.1 If a contract or order awarded pursuant to this IA is terminated or cancelled or a protest or dispute arises from specifications, solicitation, award, performance or termination of a contract, appropriate action will be taken in accordance with the terms of the contract and applicable laws and regulations.
- 9.2 The Servicing Agency shall consult with and seek concurrence from the Requesting Agency before agreeing to a settlement or payments to ensure that the Requesting Agency has adequate time in which to raise any objections or address any fiscal or budgetary concerns arising from the proposed payment or settlement. If concurrence is not obtained, the parties agree to refer the matter to the District Engineer, of the applicable USACE District where the Contracting Officer resides, and the CBP FM&E Director for resolution before the Servicing Agency agrees to any settlements or payments. The Servicing Agency Contracting Officer will delay any decision for settlement and payment until no sooner than thirty (30) calendar days after the issue is referred to the District Engineer and CBP FM&E Director.

10 Amendments

Any amendments to the terms and conditions to this IA must be made in writing and signed by both the Servicing Agency and the Requesting Agency. The party proposing the amendment must allow the other party a minimum of seven (7) calendar days to review and accept any proposed changes before they can take effect. At its discretion, the reviewing agency may agree to allow the change to take effect before the reviewing period expires. If the parties cannot agree regarding the proposed amendment, the disagreement is subject to the provisions on IA interpretation of this agreement.

11 IA Termination

This IA may be terminated upon one hundred eighty (180) calendar days' written notice by either party as a unilateral agreement. A bilateral agreement from both parties to terminate can be issued at any time during the course of this agreement. If this IA is cancelled, any implementing contract/order may also be cancelled. If the IA is terminated, the agencies must agree to the terms of the termination, including costs attributable to each party and the disposition of awarded and pending actions.

12 Interpretation of the IA

- 12.1 If the Servicing Agency and Requesting Agency are unable to agree about a material aspect of the IA, the parties agree to engage in an effort to reach mutual agreement in the proper interpretation of this IA, including amendment of this IA, as necessary, by escalating the dispute within their respective organizations.
- 12.2 If a dispute related to funding cannot be resolved under 12.1, the parties agree to refer the matter expeditiously to their respective Chief Financial Officers (CFO) with a recommendation that the dispute be resolved in accordance with Appendix 10, *Intragovernmental Transaction (IGT) Guide*, of Chapter 4700 of Volume I, *Federal Agencies*, of the Treasury Financial Manual, or subsequent guidance.

CheckpointIAA-USACB

13 Small Business Credit

- 13.1 CBP, as the Requesting Agency, must supply the Servicing Agency with the lowest and most specific FIPS 95-2 office code to ensure that the CBP receives the small business credit.
- 13.2 The Servicing Agency is responsible for entering the specific CBP code into RPDS- NG for the award.

14 Congressional Notification Requirements

In accordance with HSAM 3005.303-70, Congressional Notifications are required for:

- Any contract award including new contract actions being awarded on behalf of DHS by a Servicing Agency through an assisted acquisition in excess of \$1 million (including the base value and all options).
- Any modification in excess of \$1 million for additional supplies or services that were not covered in the Congressional notification for the award of the contract or task or delivery order.
- Any task or delivery order using FY 2012, FY 2013 or FY 2014 multi-year DHS funds in excess of \$10 million.
- Any task or delivery order, in any amount, that causes cumulative obligations in a single FY 2012, FY 2013 or FY 2014 multi-year account to exceed 50 percent of the total amount appropriated.

Failure to properly make Congressional notification may result in a violation of the Anti-Deficiency Act. Additional details on Congressional notification requirements and the required DHS Form 2140-01 are available in Appendix A of these terms and conditions.

The CO of the Servicing Agency shall prepare and submit DHS Form 2140-01 and the SOW/PWS at least six (6) full business days prior to the planned award of the contract action via electronic mail to cbppgad@dhs.gov. The subject line must state "Congressional Notification for Contract No. [insert]."

The business day begins at 9:00 a.m. Eastern Time (ET). For notifications received after 9:00 a.m. ET, the first full business day will be the day following receipt. For example, if a contract or order is to be awarded on a Friday, DHS Form 2140-01 must be received by no later than 9:00 a.m. the previous Friday. CBP will submit the Congressional notification information and will send notice via email of the earliest award date to the Servicing Agency CO. NOTE: The contract award or order issuance cannot take place prior to notice from CBP.

15 Review of Terms and Conditions

Checkpoint IAA - USACE

If the period of performance of this IA exceeds one (1) year, the parties agree to jointly review the terms and conditions of the IA at least annually. Appropriate changes will be made by amendment to this IA.

16 Signatures

By signing the Terms and Conditions document, the Requesting Agency confirms that a bona fide need exists and that funds are for the designated purpose, meet time limitations, and are legally available for the acquisition described in the IA; that all unique funding and procurement requirements, including all statutory and regulatory requirements applicable to the funding being provided, have been disclosed to the Servicing Agency; and all internal reviews and approvals required prior to transferring funds to the Servicing Agency have been completed. Further, both the Requesting Agency and the Servicing Agency agree to the terms and conditions as set forth herein.

Requesting Agency Contracting Officer:

(b)(6);(b)(7)(C) (b)(6); (b)(7)(C)

(b)(6);(b)(7)(C)

Contracting Officer

9/26/15

Date

Requesting Agency PMO Director:

(b)(6);(b)(7)(C) (b)(6); (b)(7)(C)

(b)(6);(b)(7)(C)

BPFTI PMO Director

August 27, 2015

Date

Servicing Agency Program Director:

(b) (6)

(b)(6);(b)(7)(C)

ECSSO Director

Date

Checkpoint IA

STATEMENT OF WORK

INTERAGENCY AGREEMENT (IA) BETWEEN U.S. CUSTOMS AND BORDER PROTECTION AND U.S. ARMY CORPS OF ENGINEERS

TEXAS CHECKPOINTS IMPROVEMENTS PROJECT

I. AUTHORITY

This IA is authorized pursuant to the provisions of the Economy Act of 1932 (31 U.S.C. 1535) with additional requirements for this Act contained in the Federal Acquisition Regulation (FAR) 17.5, Interagency Acquisitions.

II. OBJECTIVE/PURPOSE

This IA between the U.S. Army Corps of Engineers (USACE) and the Department of Homeland Security (DHS), U.S. Customs and Border Protection (CBP), Office of Administration, Facilities Management and Engineering (FM&E) Border Patrol Facilities & Tactical Infrastructure (BPFTI) Program Management Office (PMO) is for the purpose of obtaining the planning, acquisition, environmental assessment, programming design and construction activities for renovations to existing Border Patrol checkpoints. Due to increased trade and traffic patterns, many of the existing checkpoints are hazardous to both agents and the general public.

III. SCOPE

Texas checkpoint safety improvements may include, but not necessarily be limited to, providing separate commercial deceleration lanes, moving primary inspections areas out of roadway/highway thoroughfares; improving lighting and signage; and constructing protective barriers and canopies. Condition improvements may include: major repairs; minor construction and alterations; and new construction. Specific details on each project are documented in Project Requirement Documents (PRD) agreed to by both the project team members from the servicing and requesting agencies. PRDs will be included in the IA file, but all changes within scope of the PRDs and this IA will be executed via the BPFTI Change Management Process.

During the Base Period, the USACE will use its best efforts to provide the following services either by contract or by in-house efforts:

- a. Provide **program and project management support and expertise** (using either in-house or contractor resources), including but not limited to:
 - 1) Support overarching program management requirements and reporting needs.
 - 2) Provide complete project management services to include, cost, schedule, and scope management.

Checkpoint IA

- 3) Development of PRDs, preparation of rough order of magnitude cost estimates and preliminary schedules, risk identification, risk analyses, and mitigation strategies, project monitoring and control, and performance of other preparatory work.
- 4) Track project progress and provide progress reporting and updated schedules through regular reporting, periodic reviews, and maintaining current data in the Facilities and Infrastructure Tracking Tool (FITT) database.
- b. Provide **planning phase** support to include the completion of an acquisition plan in support of CBP projects.
- c. Provide technical, contractual, and project management experience to develop and execute **acquisition strategies**.
- d. Provide program management, real estate, environmental, and Architect/Engineering (A/E) support and expertise during the **design phase** that encompasses the preparation of designs including plans, drawings, design analyses, specifications and cost estimates required to execute a site-specific construction project (including studies and surveys).
- e. Provide support during the **construction phase** of projects.
- f. Provide support during the **post-construction phase** of projects.
- 1) Supporting project closeout activities to ensure that all obligations, expenditures, and vouchers are finalized and executed, excess funds are deobligated, and financial records for the project are properly closed out.
- 2) Assisting in resolving warranty issues should the contractor refuse to address these items, as applicable.
- 3) Submitting closeout and project documentation through FITT.

IV. REQUIREMENTS/TASKS:

- a. Checkpoint Study: Evaluate the feasibility of improving the safety and overall physical condition of checkpoints throughout the United States. Safety improvements may include but not necessarily be limited to providing separate commercial deceleration lanes, moving primary inspections areas out of roadway/highway thoroughfares; improving lighting and signage; and constructing protective barriers and canopies. Results will indicate condition improvements which may include: major repairs; minor construction and alterations; and new construction.
- b. (b)(7)(E) Checkpoint: This project involves the planning, land acquisition, design, and construction of (b)(7)(E) Checkpoint renovation to meet the required capacity of operations. The project includes building one (1) to three (3) lanes for primary inspection for commercial trucks and passenger vehicles, with deceleration lanes, (b)(7)(E) booth, canopies, lighting and signage. It will also require a small one (1) lane secondary inspection, one (1) (b)(7)(E) (b)(7)(E) parking and inspection area, a main building with operations and cell detention areas, a vehicle impound lot, a fire suppression sprinkler system, parking for government vehicles, a kennel, adequate potable water, new concrete approaches and departures (some on Texas Department of Transportation (TXDOT) land), new utilities, security fence and cameras to

Checkpoint IA

complete renovations. (b)(7)(E)

(b)(7)(E) The reconfiguration of the checkpoint will require the acquisition of four (4) to five (5) acres of additional land. The project will require a new CBP/TXDOT land use agreement. The new Small Checkpoint Standards will be the guide.

The objective of the project is to alleviate the safety risks and deficient facility conditions that exist at the current (b)(7)(E) Checkpoint on (b)(7)(E). The current checkpoint was built in 2001. The capacity of the current checkpoint became inadequate due the increase of traffic flow. The new renovations to this checkpoint will reduce overcrowding, provide adequate space for inspection, equipment storage and vehicle parking, as well as provide a safe environment for border patrol personnel and visitors.

c. (b)(7)(E) (b)(7)(E) Checkpoint: Renovate the (b)(7)(E) (b)(7)(E) Border Patrol Checkpoint to improve the safety of the agents and the public. The renovation will include reconfiguration of the checkpoint, installation of traffic barriers and protection features and replacement of structures as necessary to accommodate the reconfiguration and provide for operational capability of the checkpoint. The project will include all planning, acquisition, environmental assessment, programming design and construction activities for the project which will be executed through the USACE. The renovation will adopt the configuration and features defined in the U.S. Border Patrol Facility Design Standard – Checkpoint.

The (b)(7)(E) Checkpoint is located on (b)(7)(E) northeast of the town of (b)(7)(E) Texas. The checkpoint is located on approximately (b)(7)(E) acres of TXDOT right-of-way. The current checkpoint configuration requires agents to conduct enforcement (b)(7)(E)

d. (b)(7)(E) (b)(7)(E) Checkpoint: Renovate the (b)(7)(E) (b)(7)(E) Border Patrol Checkpoint to improve the safety of the agents and the public. The renovation will include reconfiguration of the checkpoint, installation of traffic barriers and protection features and replacement of structures as necessary to accommodate the reconfiguration and provide for operational capability of the checkpoint. The project will include all planning, acquisition, environmental assessment, programming design and construction activities for the project which will be executed through the USACE. The renovation will adopt the configuration and features defined in the U.S. Border Patrol Facility Design Standard – Checkpoint.

The (b)(7)(E) Checkpoint is located on (b)(7)(E) north of the town of (b)(7)(E) Texas. The checkpoint is located on approximately (b)(7)(E) acres of TXDOT right-of-way. The current checkpoint configuration requires agents to conduct enforcement (b)(7)(E)

e. (b)(7)(E) (b)(7)(E) Checkpoint: Renovate the (b)(7)(E) (b)(7)(E) Border Patrol Checkpoint to improve the safety of the agents and the public. The renovation will include reconfiguration of the checkpoint, installation of traffic barriers and protection features and replacement of structures as necessary to accommodate the reconfiguration and provide for operational capability of the checkpoint. The project will include all planning, acquisition, environmental assessment, programming design and construction activities for the project which

Checkpoint 1A

will be executed through the USACE. The renovation will adopt the configuration and features defined in the U.S. Border Patrol Facility Design Standard – Checkpoint.

The (b) (7)(E) Checkpoint is located on (b)(7)(E) southwest of the town of (b) (7)(E) Texas. The checkpoint is located on approximately (b)(7)(E) acres of TXDOT right-of-way. The current checkpoint configuration requires agents to conduct enforcement (b) (7)(E)

f. (b)(7)(E) (b)(7)(E) Checkpoint: Renovate the (b)(7)(E) (b)(7)(E) Border Patrol Checkpoint to improve the safety of the agents and the public. The renovation will include reconfiguration of the checkpoint, installation of traffic barriers and protection features and replacement of structures as necessary to accommodate the reconfiguration and provide for operational capability of the checkpoint. The project will include all planning, acquisition, environmental assessment, programming design and construction activities for the project which will be executed through the USACE. The renovation will adopt the configuration and features defined in the U.S. Border Patrol Facility Design Standard – Checkpoint.

The (b)(7)(E) Checkpoint is located on (b)(7)(E) at an intersection west of the town of (b)(7)(E) Texas. The checkpoint is located on approximately (b)(7)(E) of TXDOT right-of-way. The current checkpoint configuration requires agents to conduct enforcement (b) (7)(E)

g. (b)(7)(E) (b)(7)(E) Checkpoint: Renovate the (b)(7)(E) (b)(7)(E) Border Patrol Checkpoint to improve the safety of the agents and the public. The renovation will include reconfiguration of the checkpoint, installation of traffic barriers and protection features and replacement of structures as necessary to accommodate the reconfiguration and provide for operational capability of the checkpoint. The project will include all planning, acquisition, environmental assessment, programming design and construction activities for the project which will be executed through the USACE. The renovation will adopt the configuration and features defined in the U.S. Border Patrol Facility Design Standard – Checkpoint.

The (b) (7)(E) Checkpoint is located on (b)(7)(E) east of the (b)(7)(E) Texas. The checkpoint is located on approximately (b)(7)(E) acres of TXDOT right-of-way. The current checkpoint configuration requires agents to conduct enforcement (b) (7)(E)

Checkpoint IA

V. ESTIMATED COST BREAKOUT (INCLUDING APPLICABLE FEES):

Table 1: Project Cost Estimate

Checkpoint Item	Base Period Cost Estimate	Fixed Cost Estimate	Fixed Cost Percentage
10 - Change Management Reserve			
20 - Checkpoint Study Phase II			
30 - (b)(7)(E) (b)(7)(E) Checkpoint			
Base Period Subtotal			
40 - (b)(7)(E) (b)(7)(E) Checkpoint*			
50 - (b)(7)(E) (b)(7)(E) Checkpoint*			
60 - (b)(7)(E) (b)(7)(E) Checkpoint*			
70 - (b)(7)(E) (b)(7)(E) Checkpoint*			
80 - (b)(7)(E) (b)(7)(E) Checkpoint*			
Base Period Subtotal			
Total			

Additional supporting documentation on the basis of the cost estimates is available in the Project Requirement Documents (PRD).

The Base Period amount includes all costs for all work included in the scope of this IAA plus the project management costs charged by the USACE for the Base Period. Actual costs are dependent on the work performed. This budgetary estimate is based on a summation of all the labor, contract and other direct costs assumed to be required to fund the portfolio of projects executed during the Base Period through contract closeout. Change Management Reserve (CMR) funding is set aside based on specific risks that are expected for the projects in this IA. Risk analysis is conducted monthly to quantify the expected budgetary impact of potential foreseen issues. Additional detail on the value for the CMR funds will be included in the IA file.

Options will be executed as funding for each project is made available and the supporting PRD is completed. Option executions will be executed with agreements from both organizations.

VI. DELIVERABLES:

The Texas Checkpoint Projects must provide an electronic version of the following:

- * Monthly expense burn rate report (USACE Detail Reports)
- * Monthly updates in the FITT systems
- * Monthly Project Delivery Schedule (Primavera Schedule)

Checkpoint IA

VII. PLACE OF PERFORMANCE:

The place of performance for this requirement shall include:

1. Checkpoint Study Phase II (Texas)
2. (b)(7)(E) (Del Rio Sector)
3. (b)(7)(E) (Del Rio Sector)
4. (b)(7)(E) (Del Rio Sector)
5. (b)(7)(E) (Laredo Sector)
6. (b)(7)(E) (Laredo Sector)
7. (b)(7)(E) (Rio Grande Valley Sector)

VIII. PERIOD OF PERFORMANCE

This Agreement is effective on September 25, 2015 through September 24, 2018 with four (4) 1-Year Options:

- Option 1: September 25, 2018 through September 24, 2019
- Option 2: September 25, 2019 through September 24, 2020
- Option 3: September 25, 2020 through September 24, 2021
- Option 4: September 25, 2021 through September 24, 2022

IX. FUNDING

\$5,250,150.00

The initial value of the IA base year is \$5,250,150.00. Any modifications resulting from a CBP approved change request will be funded from the change management reserve contract line item number (CLIN) 10. Use of the change management reserve funding CLIN 10 is only authorized after receipt of a CBP approved change request. Funding will be provided by CBP BPFTI PMO to the USACE.

The funding to be used under this agreement is FC&S.

Checkpoint IA

Specific funding information is as follows:

LI 10 (CMR, Check Points) and LI 20 (Check Point Study Phase II)

Fund: 11139

FC: 10520

Cost Center: 928040500

Order: Z1ST

Functional Area: FM011602ALFQ

OCC: 3221

LI 30 (b)(7)(E) Checkpoint)

Fund: 13461

FC: 10520

Cost Center: 928040500

Order: Z1ST

Functional Area: FM011602ALFQ

OCC: 3221

X. APPLICABLE DOCUMENTS

U.S. Border Patrol Facility Design Standard – Checkpoint
Small Checkpoint Standards

XI. POINTS OF CONTACT

CBP:

Contracting Officer's Representative COR:

(b)(6);(b)(7)(C)

Border Patrol Facilities and Tactical Infrastructure

Program Management Office

Phone: (b)(6);(b)(7)(C)

E-mail: (b)(6);(b)(7)(C)

CBP Acquisitions:

(b)(6);(b)(7)(C)

Contracting Officer

US Customs and Border Protection

Phone: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

Checkpoint IA

USACE:

(b) (6)

Director, Engineering and Construction Support for Others

USACE, Ft Worth

Phone: (b)(6);(b)(7)(C)

E-mail: (b)(6);(b)(7)(C)

(b) (6)

Chief, Facilities Branch

USACE, Ft Worth

Phone: (b)(6);(b)(7)(C)

E-mail: (b)(6);(b)(7)(C)

(b) (6)

Chief, Planning, Program & Technical Branch

USACE, Ft Worth

Phone: (b)(6);(b)(7)(C)

E-mail: (b)(6);(b)(7)(C)

(b) (6)

Chief, Program Control Section

USACE, Ft Worth

Phone: (b)(6);(b)(7)(C)

E-mail: (b)(6);(b)(7)(C)

(b) (6)

Budget Analyst

USACE, Ft Worth

Phone: (b)(6);(b)(7)(C)

E-mail: (b)(6);(b)(7)(C)

(b) (6)

Budget Analyst

USACE, Ft Worth

Phone: (b)(6);(b)(7)(C)

E-mail: (b)(6);(b)(7)(C)

XII. PARTICIPATING AGENCY INFORMATION

Specific Agency information is as follows:

Full Agency Name: U.S. Army Corps of Engineers, Fort Worth District

Full Agency Address: 819 Taylor St, Rm 3A14, Fort Worth, TX 76102

Telephone Number: 817-886-1510

Checkpoint IA

Fax Number: 817-886-6440

Tax Identification Number: 62-1642142

DUNS Number: 068112791

Agency Locator Code: 00008736

(END OF STATEMENT OF WORK)

Checkpoint IAA - USACE

Interagency Acquisitions Supplement

Determination and Findings

Authority to Enter into an Interagency Acquisition Under the Economy Act

Based on the following determination and findings, in accordance with the authority of the Economy Act (31 U.S.C. 1535), as implemented in subpart 17.5 of the Federal Acquisition Regulation (FAR), the Requesting Agency, Department of Homeland Security, U.S. Customs and Border Protection (CBP), intends to enter into an Interagency Acquisition (IA) with the Servicing Agency, U.S. Army Corps of Engineers (USACE).

FINDINGS

1. The Requesting Agency needs a Servicing Agency to execute checkpoint safety improvements through an assisted acquisition. Texas checkpoint safety improvements are required to ensure the safety of CBP Agents. Improvements include commercial deceleration lanes, moving primary inspections areas out of roadway/highway thoroughfares; improving lighting and signage; and constructing protective barriers and canopies. Condition improvements may include: major repairs; minor construction and alterations; and new construction. The total cost of the interagency acquisition (IA) is estimated to be \$ (b) (5)

Breakdown of Total Cost

CBP Project Title	ONLY COST ESTIMATE	Total Cost Labor	Total Cost Contract/Overhead
10 - Change Management Reserve	(b) (5)		
20 - Checkpoint Study Phase II			
30 - (b) (7)(E) (b) (7)(E) Checkpoint			
Base Period Subtotal			
40 - (b) (7)(E) (b) (7)(E) Checkpoint*			
50 - (b) (7)(E) (b) (7)(E) Checkpoint*			
60 - (b) (7)(E) (b) (7)(E) Checkpoint*			
70 - (b) (7)(E) (b) (7)(E) Checkpoint*			
80 - (b) (7)(E) (b) (7)(E) Checkpoint*			
Base Period Subtotal			
Total			

Checkpoint IAA - USACE

Date: 9/26/15

Checkpoint IAA - USACE

2. The U.S. Army Corps of Engineers routinely provides facility construction support to CBP utilizing support from the Fort Worth District and the Galveston District. The USACE has the resources, knowledge and experience to complete the work required, on time and within budget as requested by CBP. To date, USACE has been responsive and provided CBP with the desired support on schedule and within budget. Specifically, USACE has construction field support stationed in both Fort Worth and Galveston District field offices which are local to the checkpoints under this project. This will reduce the travel costs for on-site construction oversight and also will reduce the time it takes for someone to be on-site if there are any issues. Additionally, USACE has the in-house staff to complete design reviews and monitor the contract through closeout. Nothing in this requirement conflicts with the authority of the servicing agency. The services cannot be obtained as conveniently, economically, or with minimum risk by contracting directly with a private source.
3. Nothing in this requirement conflicts with the authority of the servicing agency. The servicing agency has capabilities or expertise to enter into a contract for such supplies or services which is not available within the requesting agency.
4. It is in the best interest of the Government to issue an IA since the supplies or services cannot be obtained as conveniently or economically by contracting directly with a private source for the reason(s) stated in Block 2 above.
5. The requesting agency shall furnish a copy of the D&F to the servicing agency with the order.

DETERMINATION

Based on the above findings, I hereby determine that it is in the best interest of the Government to enter into an IA with the servicing agency.

(b)(6); (b)(7)(C)

CBP Requirements Official:

Signature: (b)(6);(b)(7)(C)(b)(6); (b)(7)(C)

Date: 9/24/2015

(b)(6);(b)(7)(C)

CBP Contracting Officer:

Signature: (b)(6);(b)(7)(C)(b)(6); (b)(7)(C)

Checkpoint IAA

DETERMINATION AND FINDINGS Determination of Best Procurement Approach for Assisted Acquisition For Texas Checkpoints Improvement Project

Based on the following Determination of Best Procurement Approach, in accordance with the Federal Acquisition Regulation (FAR) Subpart 17.5 Department of Homeland Security (DHS), U.S. Customs and Border Protection (CBP), intends to enter into an Interagency Acquisition (IAA) with the servicing agency the U.S. Army Corps of Engineers (USACE).

FINDINGS

1. The Requesting Agency needs a Servicing Agency to execute checkpoint safety improvements through an assisted acquisition. Texas checkpoint safety improvements are required to ensure the safety of CBP Agents. Improvements include commercial deceleration lanes, moving primary inspections areas out of roadway/highway thoroughfares; improving lighting and signage; and constructing protective barriers and canopies. Condition improvements may include: major repairs; minor construction and alterations; and new construction. The total cost of the interagency acquisition (IA) is estimated to be \$ (b) (5)
2. As a basis for determining that an IAA was the optimal and most cost effective strategy, various alternatives' benefits and risks were considered and then quantified in a customized risk matrix. These alternatives included:

(b) (5)

A detailed description of the advantages and disadvantages of each alternative are shown in the table below.

Alternative	Benefits	Risks
1. USACE	(b) (5)	
2. CBP In-House		

Checkpoint IAA

Alternative	Benefits	Risks
<p>3. Commercial Service Provider</p>	<p>(b) (5)</p>	

(b) (5)

Checkpoint IAA

Category	Subcategory	Score
	Contracting/Procurement Services	(b) (5)
	Available Expertise	
	Past Experience	
	Initial Cost	
	Project Mgt. Resources	
	Overall Project Failure	
	Total Weighted Risk Score	
	Risk Adjustment (%)	

(b) (5)

4. DHS/CBP funds used to acquire these services comply with applicable DHS/CBP appropriation limitations, and all applicable laws and policies.
5. The Servicing Agency is able to comply with the requesting agency's statutes, regulations, and policies, including any unique acquisition and fiscal requirements.

DETERMINATION

Based on the above findings, I hereby determine that entering into an interagency acquisition with the servicing agency, USACE, is the best procurement approach for the agency's requirement.

Signed:

(b)(6);(b)(7)(C) (b)(6); (b)(7)(C)

Signature of Program Manager

9/24/2015

Date

Checkpoint IAA

(b)(6);(b)(7)(C) (b)(6); (b)(7)(C)

Signature of Contracting Officer

9/26/15

Date



Rec'd 2 Aug 16

**DEPARTMENT OF HOMELAND SECURITY
U.S. CUSTOMS AND BORDER PROTECTION
INTERAGENCY AGREEMENT
(IAA)**

1. Agreement No. HSBP1015X00161		2. Modification No. P00001		3. Order No.		4. Requisition No. 0020084859	
5. Period of Performance From 09/24/2015 To 09/24/2018				6. Statutory Authority		7. Date IAA Prepared 07/27/2016	
8. Requesting Agency Agency Name: DHS - Customs & Border Protection Office/Division: Customs and Border Protection POC: (b)(6);(b)(7)(C) Address: 24000 Avila Road Laguna Niguel CA 92677 POC Phone No.: (b)(6);(b)(7)(C)				9. Servicing Agency Agency Name: ARMY CORPS OF ENGINEERS Office/Division: POC: Address: 819 TAYLOR ST RM 3A14 FT WORTH TX 76102-0300 POC Phone No.:			
10. Scope of Work This IAA modification provides funding for Line Item 40 - Renovate DRT (b)(7)(E) CKPT and Line Item 50 - CMR, Checkpoints. The Statement of Work (SOW), Revision 1 dated 7/25/2016 is incorporated herein by reference. IAA funding is increased by \$ (b)(4) from \$ (b)(4) to \$14,922,632.61. All other IAA terms and conditions remain unchanged.							
11. Delivery/Shipping Schedule See Attached Delivery Schedule							
12. IAA Amount				13. Billing and Payment			
Base Price of IAA		\$ (b)(4)		Requesting Agency		Servicing Agency	
Modification Amount	\$ (b)(4)	Locator Code: 70050800 DUNS #: DUNS# 879824324 Address: DHS - Customs & Border Protection Commercial Accounts Sect. 6650 Telecom Drive, Suite 100 Indianapolis IN 46278 POC: (b)(6);(b)(7)(C) POC Phone #: (b)(6);(b)(7)(C) POC Fax #: (b)(6);(b)(7)(C) POC Email:		Locator Code: 00008736 DUNS #: 068112791 Address: USACE Attn: CBPC-PP 5722 Integrity Drive Millington TX38054 POC: POC Phone #: POC Fax #: POC Email:			
Assisted Acquisition Servicing Fee	\$0.00						
Total IAA Price	\$14,922,632.61						
14. Requesting Agency TAS No.				15. Servicing Agency TAS No.			
10	070	X0532000		10	00000000_3122		
20	070	X0532000		20	00000000_3122		
30	07020132017	0532000		30	00000000_3122		
40	07020152019	0532000		40	00000000_3122		

CBP Form 236 (10/13)

BW23 FOIA CBP 011252

14. Requesting Agency TAS No. (Continued)	15. Servicing Agency TAS No. (Continued)
50 070 X0532000	50 00000000_3122

16. Invoice/Payment Method

- ☐ Requesting Agency Initiate IPAC
☒ Servicing Agency Initiate IPAC
☐ Credit Card
☐ Other (explain below)

17. Billing Frequency

- ☐ Monthly
☐ Quarterly
☐ Semi-annually
☐ Annual
☐ Advanced Payment (explain below)
☐ Other (explain below)

18. Requesting Agency Accounting and Appropriation Data

10	6999.3221USCSGLCS0928040500Z1ST11139FM011602ALFQ 105203221 TAS# 070 X0532000
20	6999.3221USCSGLCS0928040500Z1ST11139FM011602ALFQ 105203221 TAS# 070 X0532000
30	6999.3221USCSGLCS0928040500Z1ST13461FM011602ALFQ 105203221 TAS# 07020132017 0532
40	6999.3221USCSGLCS0928040500Z2HD15461FM011602ALFQ 105203221 TAS# 07020152019 0532
50	6999.3221USCSGLCS0928040500Z2JY11139FM011602ALFQ 105203221 TAS# 070 X0532000

19. Approvals			
Program Officials	Requesting Agency		Servicing Agency
Name	(b)(6);(b)(7)(C)		(b) (6)
Title	BPFTI PMO Director		ECSO Director
Telephone No.	(b)(6);(b)(7)(C)		(b)(6);(b)(7)(C)
Fax No.			(b)(6);(b)(7)(C)
Email	(b)(6);(b)(7)(C)		(b) (6)
Signature	(b)(6);(b)(7)(C)	(b)(6); (b)(7)(C) Date: 7/29/2016	(b) (6) Date:
Funding Officials			
Name	(b)(6);(b)(7)(C) for		(b) (6)
Title	Financial Management Branch Chief		Budget Officer
Telephone No.	(b)(6);(b)(7)(C)		(b)(6);(b)(7)(C)
Fax No.			(b)(6);(b)(7)(C)
Email	(b)(6);(b)(7)(C)		(b) (6)
Signature	(b)(6);(b)(7)(C)	(b)(6); (b)(7)(C) Date: 7/29/16	(b) (6) Date: 2 Aug 2016
Contracting Officials			
Name	(b)(6);(b)(7)(C)		
Title	Contracting Officer		
Telephone No.	(b)(6);(b)(7)(C)		
Fax No.	(b)(6);(b)(7)(C)		
Email	(b)(6);(b)(7)(C)		
Signature	(b)(6);(b)(7)(C) Date: 8/1/2016		Date:

DEPARTMENT OF HOMELAND SECURITY
U.S. CUSTOMS AND BORDER PROTECTION

INTERAGENCY AGREEMENT
(IAA)

INSTRUCTIONS

- Block 1:** Insert IAA number (automatic system populated).
- Block 2:** Insert modification number of the IAA (automatic system populated).
- Block 3:** Insert IAA order number (automatic system populated).
- Block 4:** Insert IAA requisition number (automatic system populated).
- Block 5:** Insert period of performance for the IAA.
- Block 6:** Insert statutory authority for the IAA.
- Block 7:** Insert date the IAA was prepared (automatic system populated).
- Block 8:** Insert requesting agency information.
- Block 9:** Insert servicing agency information.
- Block 10:** Insert a brief description of the IAA requirements (scope of work) and list the applicable attachments in this block. At a minimum, the attachments should include the IAA terms and conditions, statement of work, and analysis of alternative, if applicable.
- Block 11:** Insert the delivery and/or shipping schedule for the IAA or indicate where the delivery/shipping schedule may be found.
- Block 12:** Insert the base price of the IAA, modification amount, assisted acquisition servicing fee, and total IAA price--automatic system populated.
- Block 13:** Insert the billing and payment information for the requesting and servicing agency (requesting agency information automatic system populated).
- Block 14:** Insert the requesting agency TAS number for each line item (automatic system populated).
- Block 15:** Insert the servicing agency TAS number for each line item (automatic system populated).
- Block 16:** Check the invoice/payment method for the IAA and explain if "other" is selected.
- Block 17:** Check the billing frequency for the IAA and explain if "advanced payment" or "other" is selected.
- Block 18:** Insert the requesting agency accounting and appropriation data per line item (automatic system populated).
- Block 19:** Insert IAA approval information for the requesting and servicing agency pertaining to program officials, funding officials, and contracting officers. Include the date for each signature.

HSBP1015X00161P00001

**ATTACHMENT INFORMATION
FOR
AWARD/ORDER/IA MODIFICATION: HSBP1015X00161P00001**

I.1 SCHEDULE OF SUPPLIES/SERVICES

ITEM #	DESCRIPTION	QTY	UNIT	UNIT PRICE	EXT. PRICE
10	CMR, Check Points	1.000	AU	(b) (4)	
20	Check Point Study Phase II	1.000	AU		
30	(b)(7)(E) (b)(6);(b)(7)(C) Checkpoint	1.000	AU		
40	Renovate DRT (b)(7)(E) CKPT	1.000	AU		
50	CMR, Checkpoints	1.000	AU		

Total Funded Value of Award:**\$14,922,632.61****I.2 ACCOUNTING and APPROPRIATION DATA**

ITEM #	ACCOUNTING and APPROPRIATION DATA	AMOUNT
10	6999.3221USCSGLCS0928040500Z1ST11139FM011602ALFQ 105203221 TAS# 070 X0532000	\$500,000.00
20	6999.3221USCSGLCS0928040500Z1ST11139FM011602ALFQ 105203221 TAS# 070 X0532000	\$70,000.00
30	6999.3221USCSGLCS0928040500Z1ST13461FM011602ALFQ 105203221 TAS# 07020132017 0532000	\$4,680,150.00
40	6999.3221USCSGLCS0928040500Z2HD15461FM011602ALFQ 105203221 TAS# 07020152019 0532000	\$7,694,515.83
50	6999.3221USCSGLCS0928040500Z2JY11139FM011602ALFQ 105203221 TAS# 070 X0532000	\$1,977,966.78

I.3 DELIVERY SCHEDULE

DELIVER TO:	ITEM #	QTY	DELIVERY DATE
Customs and Border Protection (b)(7)(E)	10	1.000	09/24/2018
	20	1.000	09/24/2018
	30	1.000	09/24/2018
	40	1.000	09/24/2018
	50	1.000	09/24/2018

Checkpoint IA
Mod P00001, Rev 1 – 7-25-16

STATEMENT OF WORK
INTERAGENCY AGREEMENT (IA)
BETWEEN
U.S. CUSTOMS AND BORDER PROTECTION AND
U.S. ARMY CORPS OF ENGINEERS
TEXAS CHECKPOINTS IMPROVEMENTS PROJECT

I. AUTHORITY

This IA is authorized pursuant to the provisions of the Economy Act of 1932 (31 U.S.C. 1535) with additional requirements for this Act contained in the Federal Acquisition Regulation (FAR) 17.5, Interagency Acquisitions.

II. OBJECTIVE/PURPOSE

This IA between the U.S. Army Corps of Engineers (USACE) and the Department of Homeland Security (DHS), U.S. Customs and Border Protection (CBP), Office of Administration, Facilities Management and Engineering (FM&E) Border Patrol Facilities & Tactical Infrastructure (BPFTI) Program Management Office (PMO) is for the purpose of obtaining the planning, acquisition, environmental assessment, programming design and construction activities for renovations to existing Border Patrol checkpoints. Due to increased trade and traffic patterns, many of the existing checkpoints are hazardous to both agents and the general public.

III. SCOPE

Texas checkpoint safety improvements may include, but not necessarily be limited to, providing separate commercial deceleration lanes, moving primary inspections areas out of roadway/highway thoroughfares; improving lighting and signage; and constructing protective barriers and canopies. Condition improvements may include: major repairs; minor construction and alterations; and new construction. Specific details on each project are documented in Project Requirement Documents (PRD) agreed to by both the project team members from the servicing and requesting agencies. PRDs will be included in the IA file, but all changes within scope of the PRDs and this IA will be executed via the BPFTI Change Management Process.

During the Base Period, the USACE will use its best efforts to provide the following services either by contract or by in-house efforts:

- a. Provide **program and project management support and expertise** (using either in-house or contractor resources), including but not limited to:
 - 1) Support overarching program management requirements and reporting needs.
 - 2) Provide complete project management services to include, cost, schedule, and scope management.

Checkpoint IA
Mod P00001, Rev 1 – 7-25-16

- 3) Development of PRDs, preparation of rough order of magnitude cost estimates and preliminary schedules, risk identification, risk analyses, and mitigation strategies, project monitoring and control, and performance of other preparatory work.
- 4) Track project progress and provide progress reporting and updated schedules through regular reporting, periodic reviews, and maintaining current data in the Facilities and Infrastructure Tracking Tool (FITT) database.
- b. Provide **planning phase support** to include the completion of an acquisition plan in support of CBP projects.
- c. Provide technical, contractual, and project management experience to develop and execute **acquisition strategies**.
- d. Provide program management, real estate, environmental, and Architect/Engineering (A/E) support and expertise during the **design phase** that encompasses the preparation of designs including plans, drawings, design analyses, specifications and cost estimates required to execute a site-specific construction project (including studies and surveys).
- e. Provide support during the **construction phase** of projects.
- f. Provide support during the **post-construction** phase of projects.
- 1) Supporting project closeout activities to ensure that all obligations, expenditures, and vouchers are finalized and executed, excess funds are deobligated, and financial records for the project are properly closed out.
- 2) Assisting in resolving warranty issues should the contractor refuse to address these items, as applicable.
- 3) Submitting closeout and project documentation through FITT.

IV. REQUIREMENTS/TASKS:

- a. Checkpoint Study: Evaluate the feasibility of improving the safety and overall physical condition of checkpoints throughout the United States. Safety improvements may include but not necessarily be limited to providing separate commercial deceleration lanes, moving primary inspections areas out of roadway/highway thoroughfares; improving lighting and signage; and constructing protective barriers and canopies. Results will indicate condition improvements which may include: major repairs; minor construction and alterations; and new construction.
- b. (b)(7)(E) Checkpoint: This project involves the planning, land acquisition, design, and construction of (b)(7)(E) Checkpoint renovation to meet the required capacity of operations. The project includes building one (1) to three (3) lanes for primary inspection for commercial trucks and passenger vehicles, with deceleration lanes, (b)(7)(E) booth, canopies, lighting and signage. It will also require a small one (1) lane secondary inspection, one (1) (b)(7)(E) (b)(7)(E) parking and inspection area, a main building with operations and cell detention areas, a vehicle impound lot, a fire suppression sprinkler system, parking for government vehicles, a kennel, adequate potable water, new concrete approaches and departures (some on Texas Department of Transportation (TXDOT) land), new utilities, security fence and cameras to

Checkpoint IAA
Mod P00001, Rev 1 – 7-25-16

complete renovations.

(b)(7)(E)

(b)(7)(E)

The reconfiguration of the checkpoint will require the acquisition of four (4) to five (5) acres of additional land. The project will require a new CBP/TXDOT land use agreement. The new Small Checkpoint Standards will be the guide.

The objective of the project is to alleviate the safety risks and deficient facility conditions that exist at the current (b)(7)(E) Checkpoint on (b)(7)(E). The current checkpoint was built in 2001. The capacity of the current checkpoint became inadequate due the increase of traffic flow. The new renovations to this checkpoint will reduce overcrowding, provide adequate space for inspection, equipment storage and vehicle parking, as well as provide a safe environment for border patrol personnel and visitors.

c. (b)(7)(E) (b)(7)(E) Checkpoint: Renovate the (b)(7)(E) (b)(7)(E) Border Patrol Checkpoint to improve the safety of the agents and the public. The renovation will include reconfiguration of the checkpoint, installation of traffic barriers and protection features and replacement of structures as necessary to accommodate the reconfiguration and provide for operational capability of the checkpoint. The project will include all planning, acquisition, environmental assessment, programming design and construction activities for the project which will be executed through the USACE. The renovation will adopt the configuration and features defined in the U.S. Border Patrol Facility Design Standard – Checkpoint.

The (b)(7)(E) Checkpoint is located on (b)(7)(E) northeast of the town of (b)(7)(E) Texas. The checkpoint is located on approximately (b)(7)(E) of TXDOT right-of-way. The current checkpoint configuration requires agents to conduct enforcement (b)(7)(E)

V. ESTIMATED COST BREAKOUT (INCLUDING APPLICABLE FEES):

Table 1: Project Cost Estimate

CLIN/Project Title	TOTAL COST ESTIMATE	Total Cost Est. Labor (USACE)	Total Cost Est. Contract/Purchase
Base Period	(b)(5)		
10 - Change Management Reserve			
20 - Checkpoint Study Phase II			
30 - (b)(7)(E) (b)(7)(E) Checkpoint			
Base Period Subtotal			
Options			
40 - Renovate DRT (b)(7)(E) CKPT			
50 - CMR, Checkpoints			
Total	\$14,922,632.61	(b)(5)	

Additional supporting documentation on the basis of the cost estimates is available in the Project Requirement Documents (PRD).

The Base Period amount includes all costs for all work included in the scope of this IAA plus the project management costs charged by the USACE for the Base Period. Actual costs are dependent on the work performed. This budgetary estimate is based on a summation of all the

Checkpoint IA
Mod P00001, Rev 1 – 7-25-16

labor, contract and other direct costs assumed to be required to fund the portfolio of projects executed during the Base Period through contract closeout. Change Management Reserve (CMR) funding is set aside based on specific risks that are expected for the projects in this IA. Risk analysis is conducted monthly to quantify the expected budgetary impact of potential foreseen issues. Additional detail on the value for the CMR funds will be included in the IA file.

Options will be executed as funding for each project is made available and the supporting PRD is completed. Option executions will be executed with agreements from both organizations.

VI. DELIVERABLES:

The Texas Checkpoint Projects must provide an electronic version of the following:

- Monthly expense burn rate report (USACE Detail Reports)
- Monthly updates in the FITT systems
- Monthly Project Delivery Schedule (Primavera Schedule)

VII. PLACE OF PERFORMANCE:

The place of performance for this requirement shall include:

1. Checkpoint Study Phase II (Texas)
2. (b)(7)(E) (Del Rio Sector)
3. (b)(7)(E) (Del Rio Sector)

VIII. PERIOD OF PERFORMANCE

This Agreement is effective on September 25, 2015 through September 24, 2018 with four (4) 1-Year Options:

- Option 1: September 25, 2018 through September 24, 2019
- Option 2: September 25, 2019 through September 24, 2020
- Option 3: September 25, 2020 through September 24, 2021
- Option 4: September 25, 2021 through September 24, 2022

IX. FUNDING

The initial value of the IA base year is \$5,250,150.00. Any modifications resulting from a CBP approved change request will be funded from the change management reserve contract line item

Checkpoint IA
Mod P00001, Rev 1 – 7-25-16

number (CLIN) 10. Use of the change management reserve funding CLIN 10 is only authorized after receipt of a CBP approved change request. Funding will be provided by CBP BPFTI PMO to the USACE.

The funding to be used under this agreement is FC&S.

Specific funding information is as follows:

LI 10 (CMR, Check Points) and LI 20 (Check Point Study Phase II)

Fund: 11139
FC: 10520
Cost Center: 928040500
Order: Z1ST
Functional Area: FM011602ALFQ
OCC: 3221

LI 30 (b)(7)(E) (b)(7)(E) Checkpoint)

Fund: 13461
FC: 10520
Cost Center: 928040500
Order: Z1ST
Functional Area: FM011602ALFQ
OCC: 3221

LI 40 (Renovate DRT (b)(7)(E) CKPT)

***Fund: 15461
FC: 10520
Cost Center: 928040500
Order: Z2HD
Functional Area: FM011602ALFQ
OCC: 3221***

LI 50 (CMR, Checkpoints)

***Fund: 11139
FC: 10520
Cost Center: 928040500
Order: Z2JY
Functional Area: FM011602ALFQ
OCC: 3221***

Checkpoint IA
Mod P00001, Rev 1 – 7-25-16

X. APPLICABLE DOCUMENTS

U.S. Border Patrol Facility Design Standard – Checkpoint
Small Checkpoint Standards

XI. POINTS OF CONTACT

CBP:

Contracting Officer's Representative COR:

(b)(6);(b)(7)(C)

Border Patrol Facilities and Tactical Infrastructure
Program Management Office

Phone: (b)(6);(b)(7)(C)

E-mail: (b)(6);(b)(7)(C)

CBP Acquisitions:

(b)(6);(b)(7)(C)

Contracting Officer

US Customs and Border Protection

Phone: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

USACE:

(b) (6)

Director, Engineering and Construction Support for Others
USACE, Ft Worth

Phone: (b) (6)

E-mail: (b) (6)

(b) (6)

Chief, Facilities Branch

USACE, Ft Worth

Phone: (b) (6)

E-mail: (b) (6)

(b) (6)

Chief, Planning, Program & Technical Branch

USACE, Ft Worth

Phone: (b) (6)

E-mail: (b) (6)

Checkpoint IA
Mod P00001, Rev 1 – 7-25-16

(b) (6)
Chief, Program Control Section
USACE, Ft Worth
Phone: (b) (6)
E-mail: (b) (6)

(b) (6)
Budget Analyst
USACE, Ft Worth
Phone: (b) (6)
E-mail: (b) (6)

(b) (6)
Budget Analyst
USACE, Ft Worth
Phone: (b) (6)
E-mail: (b) (6)

XII. PARTICIPATING AGENCY INFORMATION

Specific Agency information is as follows:

Full Agency Name: U.S. Army Corps of Engineers, Fort Worth District
Full Agency Address: 819 Taylor St, Rm 3A14, Fort Worth, TX 76102
Telephone Number: 817-886-1510

Fax Number: 817-886-6440
Tax Identification Number: 62-1642142
DUNS Number: 068112791
Agency Locator Code: 00008736

(END OF STATEMENT OF WORK)

Date rec'd in ECSO: 2 Aug 16

Date to RM-B: 2 Aug 16

RWA #: HSBP1015X00161.1

Title: CBP Texas Checkpoints Improv Projects

Amt: \$9,672,482.61

Environmental? Y ☐ N ☒

PA/phone #: CS-1598

Remarks: Li-40 (b) (5), (b) (7)(E) Li-50 CMR Checkpoints
\$ (b) (5)

IAA New Total \$14,922,632.61

tech
2 aug 16
CS

P2: 454107/450360

FWI: 20KL1F/25J0HG

Source Appropriation: li-40 70 5/9 0532 expires 30 Sep 2019; li-50 70X0532
no year

**DEPARTMENT OF HOMELAND SECURITY
U.S. CUSTOMS AND BORDER PROTECTION
INTERAGENCY AGREEMENT
(IAA)**

1. Agreement No. HSBP1015X00161		2. Modification No. P00002		3. Order No.		4. Requisition No. 0020084859	
5. Period of Performance From 09/24/2015 To 09/24/2018				6. Statutory Authority		7. Date IAA Prepared 07/27/2016	
8. Requesting Agency Agency Name: DHS - Customs & Border Protection Office/Division: Customs and Border Protection POC: (b)(6);(b)(7)(C) Address: 24000 Avila Road, Suite 1640A Laguna Niguel CA 92677 POC Phone No.: (b)(6);(b)(7)(C)				9. Servicing Agency Agency Name: ARMY CORPS OF ENGINEERS Office/Division: POC: Address: 819 TAYLOR ST RM 3A14 FT WORTH TX 76102-0300 POC Phone No.:			
10. Scope of Work This IAA modification authorizes USACE to use funding for acquisition actions for the projects in the attached SOW. IAA funding remains unchanged at \$14,922,632.61. All other IAA terms and conditions remain unchanged.							
11. Delivery/Shipping Schedule See Attached Delivery Schedule							
12. IAA Amount				13. Billing and Payment			
Base Price of IAA		\$14,922,632.61		Requesting Agency		Servicing Agency	
Modification Amount	\$0.00	Locator Code: 70050800 DUNS #: DUNS# 879824324 Address: DHS - Customs & Border Protection Commercial Accounts Sect. 6650 Telecom Drive, Suite 100 Indianapolis, IN 46278 POC: (b)(6);(b)(7)(C) POC Phone #: POC Fax #: POC Email:		Locator Code: 00008736 DUNS #: 068112791 Address: USACE Attn: CEFC-FP 5722 Integrity Drive Millington TX 38054 POC: POC Phone #: POC Fax #: POC Email:			
Assisted Acquisition Servicing Fee	\$0.00						
Total IAA Price	\$14,922,632.61						
14. Requesting Agency TAS No.				15. Servicing Agency TAS No.			
10	070	X0532000		10	00000000_3122		
20	070	X0532000		20	00000000_3122		
30	07020132017	0532000		30	00000000_3122		
40	07020152019	0532000		40	00000000_3122		

14. Requesting Agency TAS No. (Continued)	15. Servicing Agency TAS No. (Continued)
50 070 X0532000	50 00000000_3122

16. Invoice/Payment Method <input type="checkbox"/> Requesting Agency Initiate IPAC <input checked="" type="checkbox"/> Servicing Agency Initiate IPAC <input type="checkbox"/> Credit Card <input type="checkbox"/> Other (explain below) <hr style="width: 30%; margin-left: 0;"/>	17. Billing Frequency <input type="checkbox"/> Monthly <input type="checkbox"/> Quarterly <input type="checkbox"/> Semi-annually <input type="checkbox"/> Annual <input type="checkbox"/> Advanced Payment (explain below) <input checked="" type="checkbox"/> Other (explain below) <div style="border-bottom: 1px solid black; width: 100%;"></div> As Required
--	---

18. Requesting Agency Accounting and Appropriation Data

10	6999.3221USCSGLCS0928040500Z1ST11139FM011602ALFQ 105203221 TAS# 070 X0532000
20	6999.3221USCSGLCS0928040500Z1ST11139FM011602ALFQ 105203221 TAS# 070 X0532000
30	6999.3221USCSGLCS0928040500Z1ST13461FM011602ALFQ 105203221 TAS# 07020132017 0532
40	6999.3221USCSGLCS0928040500Z2HD15461FM011602ALFQ 105203221 TAS# 07020152019 0532
50	6999.3221USCSGLCS0928040500Z2JY11139FM011602ALFQ 105203221 TAS# 070 X0532000

19. Approvals			
Program Officials	Requesting Agency		Servicing Agency
Name	(b)(6);(b)(7)(C)		For (b) (6)
Title	Eastern Corridors Division Director		Colonel, U.S. Army Commanding
Telephone No.	(b)(6);(b)(7)(C)		817-886-1515
Fax No.			
Email	(b)(6);(b)(7)(C)		(b) (6)
Signature	(b)(6);(b)(7)(C)	(b)(6); (b)(7)(C) Date:	(b) (6) Date: 28 SEP 17
Funding Officials			
Name	(b)(6);(b)(7)(C)		
Title	Chief, Financial Management Branch		Budget Officer
Telephone No.	(b)(6);(b)(7)(C)		(b)(6);(b)(7)(C)
Fax No.			(b)(6);(b)(7)(C)
Email	(b)(6);(b)(7)(C)		(b) (6)
Signature	(b)(6);(b)(7)(C)	(b)(6); (b)(7)(C) Date:	(b) (6) Date:
Contracting Officials			
Name	(b)(6);(b)(7)(C)		
Title	Contracting Officer		
Telephone No.	(b)(6);(b)(7)(C)		
Fax No.			
Email	(b)(6);(b)(7)(C)		
Signature	(b)(6);(b)(7)(C)	(b)(6); (b)(7)(C) Date: 09/28/2017	Date:

DEPARTMENT OF HOMELAND SECURITY
U.S. CUSTOMS AND BORDER PROTECTION

INTERAGENCY AGREEMENT
(IAA)

INSTRUCTIONS

Block 1: Insert IAA number (automatic system populated).

Block 2: Insert modification number of the IAA (automatic system populated).

Block 3: Insert IAA order number (automatic system populated).

Block 4: Insert IAA requisition number (automatic system populated).

Block 5: Insert period of performance for the IAA.

Block 6: Insert statutory authority for the IAA.

Block 7: Insert date the IAA was prepared (automatic system populated).

Block 8: Insert requesting agency information.

Block 9: Insert servicing agency information.

Block 10: Insert a brief description of the IAA requirements (scope of work) and list the applicable attachments in this block. At a minimum, the attachments should include the IAA terms and conditions, statement of work, and analysis of alternative, if applicable.

Block 11: Insert the delivery and/or shipping schedule for the IAA or indicate where the delivery/shipping schedule may be found.

Block 12: Insert the base price of the IAA, modification amount, assisted acquisition servicing fee, and total IAA price--automatic system populated.

Block 13: Insert the billing and payment information for the requesting and servicing agency (requesting agency information automatic system populated).

Block 14: Insert the requesting agency TAS number for each line item (automatic system populated).

Block 15: Insert the servicing agency TAS number for each line item (automatic system populated).

Block 16: Check the invoice/payment method for the IAA and explain if "other" is selected.

Block 17: Check the billing frequency for the IAA and explain if "advanced payment" or "other" is selected.

Block 18: Insert the requesting agency accounting and appropriation data per line item (automatic system populated).

Block 19: Insert IAA approval information for the requesting and servicing agency pertaining to program officials, funding officials, and contracting officers. Include the date for each signature.

HSBP1015X00161P00002

**ATTACHMENT INFORMATION
FOR
AWARD/ORDER/IA MODIFICATION: HSBP1015X00161P00002**

I.1 52.209-10 PROHIBITION ON CONTRACTING WITH INVERTED DOMESTIC CORPORATIONS (NOV 2015)**I.2 SCHEDULE OF SUPPLIES/SERVICES**

ITEM #	DESCRIPTION	QTY	UNIT	UNIT PRICE	EXT. PRICE
10	CMR, Check Points	1.000	AU	(b) (4)	(4)
20	Check Point Study Phase II	1.000	AU		
30	(b)(7)(E) (b) (7)(E) Checkpoint	1.000	AU		
40	Renovate DRT (b)(7)(E) CKPT	1.000	AU		
50	CMR, Checkpoints	1.000	AU		

Total Funded Value of Award:**\$14,922,632.61****I.3 ACCOUNTING and APPROPRIATION DATA**

ITEM #	ACCOUNTING and APPROPRIATION DATA	AMOUNT
10	6999.3221USCSGLCS0928040500Z1ST11139FM011602ALFQ 105203221 TAS# 070 X0532000	(b) (4)
20	6999.3221USCSGLCS0928040500Z1ST11139FM011602ALFQ 105203221 TAS# 070 X0532000	
30	6999.3221USCSGLCS0928040500Z1ST13461FM011602ALFQ 105203221 TAS# 07020132017 0532000	
40	6999.3221USCSGLCS0928040500Z2HD15461FM011602ALFQ 105203221 TAS# 07020152019 0532000	
50	6999.3221USCSGLCS0928040500Z2JY11139FM011602ALFQ 105203221 TAS# 070 X0532000	

I.4 DELIVERY SCHEDULE

DELIVER TO:	ITEM #	QTY	DELIVERY DATE
Customs and Border Protection (b)(7)(E)	10	1.000	09/24/2018
	20	1.000	09/24/2018
	30	1.000	09/24/2018
	40	1.000	09/24/2018
	50	1.000	09/24/2018

Checkpoint IA
Mod P00001, Rev 1 – 7-25-16

SEE ATTACHED REVISION 9/28/2017

STATEMENT OF WORK

INTERAGENCY AGREEMENT (IA) BETWEEN U.S. CUSTOMS AND BORDER PROTECTION AND U.S. ARMY CORPS OF ENGINEERS

TEXAS CHECKPOINTS IMPROVEMENTS PROJECT

I. AUTHORITY

This IA is authorized pursuant to the provisions of the Economy Act of 1932 (31 U.S.C. 1535) with additional requirements for this Act contained in the Federal Acquisition Regulation (FAR) 17.5, Interagency Acquisitions.

II. OBJECTIVE/PURPOSE

This IA between the U.S. Army Corps of Engineers (USACE) and the Department of Homeland Security (DHS), U.S. Customs and Border Protection (CBP), Office of Administration, Facilities Management and Engineering (FM&E) Border Patrol Facilities & Tactical Infrastructure (BPFTI) Program Management Office (PMO) is for the purpose of obtaining the planning, acquisition, environmental assessment, programming design and construction activities for renovations to existing Border Patrol checkpoints. Due to increased trade and traffic patterns, many of the existing checkpoints are hazardous to both agents and the general public.

III. SCOPE

Texas checkpoint safety improvements may include, but not necessarily be limited to, providing separate commercial deceleration lanes, moving primary inspections areas out of roadway/highway thoroughfares; improving lighting and signage; and constructing protective barriers and canopies. Condition improvements may include: major repairs; minor construction and alterations; and new construction. Specific details on each project are documented in Project Requirement Documents (PRD) agreed to by both the project team members from the servicing and requesting agencies. PRDs will be included in the IA file, but all changes within scope of the PRDs and this IA will be executed via the BPFTI Change Management Process.

During the Base Period, the USACE will use its best efforts to provide the following services either by contract or by in-house efforts:

- a. Provide **program and project management support and expertise** (using either in-house or contractor resources), including but not limited to:
 - 1) Support overarching program management requirements and reporting needs.
 - 2) Provide complete project management services to include, cost, schedule, and scope management.

Checkpoint IA
Mod P00001, Rev 1 – 7-25-16

- 3) Development of PRDs, preparation of rough order of magnitude cost estimates and preliminary schedules, risk identification, risk analyses, and mitigation strategies, project monitoring and control, and performance of other preparatory work.
- 4) Track project progress and provide progress reporting and updated schedules through regular reporting, periodic reviews, and maintaining current data in the Facilities and Infrastructure Tracking Tool (FITT) database.
- b. Provide **planning phase support** to include the completion of an acquisition plan in support of CBP projects.
- c. Provide technical, contractual, and project management experience to develop and execute **acquisition strategies**.
- d. Provide program management, real estate, environmental, and Architect/Engineering (A/E) support and expertise during the **design phase** that encompasses the preparation of designs including plans, drawings, design analyses, specifications and cost estimates required to execute a site-specific construction project (including studies and surveys).
- e. Provide support during the **construction phase** of projects.
- f. Provide support during the **post-construction** phase of projects.
- 1) Supporting project closeout activities to ensure that all obligations, expenditures, and vouchers are finalized and executed, excess funds are deobligated, and financial records for the project are properly closed out.
- 2) Assisting in resolving warranty issues should the contractor refuse to address these items, as applicable.
- 3) Submitting closeout and project documentation through FITT.

IV. REQUIREMENTS/TASKS:

- a. Checkpoint Study: Evaluate the feasibility of improving the safety and overall physical condition of checkpoints throughout the United States. Safety improvements may include but not necessarily be limited to providing separate commercial deceleration lanes, moving primary inspections areas out of roadway/highway thoroughfares; improving lighting and signage; and constructing protective barriers and canopies. Results will indicate condition improvements which may include: major repairs; minor construction and alterations; and new construction.
- b. (b)(7)(E) (b)(7)(E) Checkpoint: This project involves the planning, land acquisition, design, and construction of (b)(7)(E) Checkpoint renovation to meet the required capacity of operations. The project includes building one (1) to three (3) lanes for primary inspection for commercial trucks and passenger vehicles, with deceleration lanes, (b)(7)(E) booth, canopies, lighting and signage. It will also require a small one (1) lane secondary inspection, one (1) (b)(7)(E) (b)(7)(E) parking and inspection area, a main building with operations and cell detention areas, a vehicle impound lot, a fire suppression sprinkler system, parking for government vehicles, a kennel, adequate potable water, new concrete approaches and departures (some on Texas Department of Transportation (TXDOT) land), new utilities, security fence and cameras to

Checkpoint IA
Mod P00001, Rev 1 – 7-25-16

complete renovations, (b)(7)(E)
(b)(7)(E) The reconfiguration of the checkpoint will require the acquisition of four (4) to five (5) acres of additional land. The project will require a new CBP/TXDOT land use agreement. The new Small Checkpoint Standards will be the guide.

The objective of the project is to alleviate the safety risks and deficient facility conditions that exist at the current (b)(7)(E) Checkpoint on (b)(7)(E). The current checkpoint was built in 2001. The capacity of the current checkpoint became inadequate due the increase of traffic flow. The new renovations to this checkpoint will reduce overcrowding, provide adequate space for inspection, equipment storage and vehicle parking, as well as provide a safe environment for border patrol personnel and visitors.

c. (b)(7)(E) (b)(7)(E) Checkpoint: Renovate the (b)(7)(E) (b)(7)(E) Border Patrol Checkpoint to improve the safety of the agents and the public. The renovation will include reconfiguration of the checkpoint, installation of traffic barriers and protection features and replacement of structures as necessary to accommodate the reconfiguration and provide for operational capability of the checkpoint. The project will include all planning, acquisition, environmental assessment, programming design and construction activities for the project which will be executed through the USACE. The renovation will adopt the configuration and features defined in the U.S. Border Patrol Facility Design Standard – Checkpoint.

The (b)(7)(E) Checkpoint is located on (b)(7)(E) northeast of the town of (b)(7)(E) Texas. The checkpoint is located on approximately (b)(7)(E) of TXDOT right-of-way. The current checkpoint configuration requires agents to conduct enforcement (b)(7)(E)

V. ESTIMATED COST BREAKOUT (INCLUDING APPLICABLE FEES):

Table 1: Project Cost Estimate

CLIN/Project Title	TOTAL COST ESTIMATE	Total Cost Est. Labor (USACE)	Total Cost Est. Contract/Purchase
Base Period	(b) (5)	(b) (5)	(b) (5)
10 - Change Management Reserve			
20 - Checkpoint Study Phase II			
30 - (b)(7)(E) (b) (7)(E) Checkpoint			
Base Period Subtotal			
Options			
40 - Renovate DRT (b)(7)(E) CKPT			
50 - CMR, Checkpoints	(b) (5)	(b) (5)	(b) (5)
Total			

\$14,922,632.61	(b) (5)
-----------------	---------

Additional supporting documentation on the basis of the cost estimates is available in the Project Requirement Documents (PRD).

The Base Period amount includes all costs for all work included in the scope of this IAA plus the project management costs charged by the USACE for the Base Period. Actual costs are dependent on the work performed. This budgetary estimate is based on a summation of all the

Checkpoint IA
Mod P00001, Rev 1 – 7-25-16

labor, contract and other direct costs assumed to be required to fund the portfolio of projects executed during the Base Period through contract closeout. Change Management Reserve (CMR) funding is set aside based on specific risks that are expected for the projects in this IA. Risk analysis is conducted monthly to quantify the expected budgetary impact of potential foreseen issues. Additional detail on the value for the CMR funds will be included in the IA file.

Options will be executed as funding for each project is made available and the supporting PRD is completed. Option executions will be executed with agreements from both organizations.

VI. DELIVERABLES:

The Texas Checkpoint Projects must provide an electronic version of the following:

- Monthly expense burn rate report (USACE Detail Reports)
- Monthly updates in the FITT systems
- Monthly Project Delivery Schedule (Primavera Schedule)

VII. PLACE OF PERFORMANCE:

The place of performance for this requirement shall include:

1. Checkpoint Study Phase II (Texas)
(b)(7)(E)
2. (b)(7)(E) (Del Rio Sector)
3. (b)(7)(E) (Del Rio Sector)

VIII. PERIOD OF PERFORMANCE

This Agreement is effective on September 25, 2015 through September 24, 2018 with four (4) 1-Year Options:

- Option 1: September 25, 2018 through September 24, 2019
- Option 2: September 25, 2019 through September 24, 2020
- Option 3: September 25, 2020 through September 24, 2021
- Option 4: September 25, 2021 through September 24, 2022

IX. FUNDING

The initial value of the IA base year is \$5,250,150.00. Any modifications resulting from a CBP approved change request will be funded from the change management reserve contract line item

Checkpoint IA

Mod P00001, Rev 1 – 7-25-16

number (CLIN) 10. Use of the change management reserve funding CLIN 10 is only authorized after receipt of a CBP approved change request. Funding will be provided by CBP BPFTI PMO to the USACE.

The funding to be used under this agreement is FC&S.

Specific funding information is as follows:

LI 10 (CMR, Check Points) and LI 20 (Check Point Study Phase II)

Fund: 11139

FC: 10520

Cost Center: 928040500

Order: Z1ST

Functional Area: FM011602ALFQ

OCC: 3221

LI 30 (b)(7)(E) (b)(7)(E) Checkpoint)

Fund: 13461

FC: 10520

Cost Center: 928040500

Order: Z1ST

Functional Area: FM011602ALFQ

OCC: 3221

LI 40 (Renovate DRT (b)(7)(E) CKPT)

Fund: 15461

FC: 10520

Cost Center: 928040500

Order: Z2HD

Functional Area: FM011602ALFQ

OCC: 3221

LI 50 (CMR, Checkpoints)

Fund: 11139

FC: 10520

Cost Center: 928040500

Order: Z2JY

Functional Area: FM011602ALFQ

OCC: 3221

Checkpoint IA
Mod P00001, Rev 1 – 7-25-16

X. APPLICABLE DOCUMENTS

U.S. Border Patrol Facility Design Standard – Checkpoint
Small Checkpoint Standards

XI. POINTS OF CONTACT

CBP:

Contracting Officer's Representative COR:

(b)(6);(b)(7)(C)

Border Patrol Facilities and Tactical Infrastructure
Program Management Office

Phone: **(b)(6);(b)(7)(C)**

E-mail: **(b)(6);(b)(7)(C)**

CBP Acquisitions:

(b)(6);(b)(7)(C)

Contracting Officer
US Customs and Border Protection

Phone: **(b)(6);(b)(7)(C)**

Email: **(b)(6);(b)(7)(C)**

USACE:

(b) (6)

Director, Engineering and Construction Support for Others
USACE, Ft Worth

Phone: **(b)(6);(b)(7)(C)**

E-mail: **(b) (6)**

(b) (6)

Chief, Facilities Branch
USACE, Ft Worth

Phone: **(b)(6);(b)(7)(C)**

E-mail: **(b) (6)**

(b) (6)

Chief, Planning, Program & Technical Branch
USACE, Ft Worth

Phone: **(b)(6);(b)(7)(C)**

E-mail: **(b) (6)**

Checkpoint IA
Mod P00001, Rev 1 – 7-25-16

(b) (6)

Chief, Program Control Section
USACE, Ft Worth
Phone: (b)(6);(b)(7)(C)
E-mail: (b) (6)

(b) (6)

Budget Analyst
USACE, Ft Worth
Phone: (b)(6);(b)(7)(C)
E-mail: (b) (6)

(b) (6)

Budget Analyst
USACE, Ft Worth
Phone: (b)(6);(b)(7)(C)
E-mail: (b) (6)

XII, PARTICIPATING AGENCY INFORMATION

Specific Agency information is as follows:

Full Agency Name: U.S. Army Corps of Engineers, Fort Worth District
Full Agency Address: 819 Taylor St, Rm 3A14, Fort Worth, TX 76102
Telephone Number: 817-886-1510

Fax Number: 817-886-6440
Tax Identification Number: 62-1642142
DUNS Number: 068112791
Agency Locator Code: 00008736

(END OF STATEMENT OF WORK)

Attachment to Scope of Mod HSBP1015X00161.1
For Mod P000002, 9/28/17

**INTERAGENCY AGREEMENT
STATEMENT OF WORK
BETWEEN
U.S. CUSTOMS AND BORDER PROTECTION AND
U.S. ARMY CORPS OF ENGINEERS**

I. AUTHORITY

The authority of the Department of Homeland Security, U.S. Customs and Border Protection and the U.S. Army Corps of Engineers to enter into this Interagency Agreement (IAA) is the Economy Act of 1932 (31 U.S.C. 1535), resulting in an assisted acquisition.

II. OBJECTIVE/PURPOSE

This Interagency Agreement (IAA) between the U.S. Army Corps of Engineers and the Department of Homeland Security, U.S. Customs and Border Protection (CBP), Office of Administration, Facilities Management and Engineering (FM&E) Border Patrol & Air and Marine Facilities (BPAM) Program Management Office (PMO) is for the purpose of obtaining the planning, acquisition, environmental assessment, programming design and construction activities for renovations to existing Border Patrol checkpoints, as well as, a new (b)(7)(E) Border Patrol Station and Border Patrol Checkpoint near (b)(7)(E) in (b)(7)(E) Texas. Due to increased trade and traffic patterns, many of the existing checkpoints and existing (b)(7)(E) Border Patrol Station are hazardous to both agents and the general public.

III. SCOPE

- a. Laredo Sector Border Patrol - New (b)(7)(E) Border Patrol Station (BPS) and Immigration Checkpoint in (b)(7)(E) TX: This project is for the design and construction of a new (b)(7)(E) Border Patrol Station (BPS) and Immigration Checkpoint for Laredo Sector in (b)(7)(E) Texas, similar to the (b)(7)(E) BPS and Co-Located Checkpoint designed and constructed for Del Rio Sector in (b)(7)(E) TX.

The new Border Patrol facilities shall replace existing deficient facilities currently in various leased and temporary buildings and sites. The existing station building(s) are on standstill lease agreement, which will be terminated upon completion of the project. Excessing of the secondary station buildings and property will be executed through GSA excessing program procedures.

The project will include programming, design, real estate market surveys, environmental compliance, site utilization, site acquisition, and construction. The project will include the purchase of approximately (b)(7)(E) site west of the intersection of (b)(7)(E) and (b)(7)(E) in (b)(7)(E) Texas. This project will include comprehensive design and finished construction of all programmed facilities.

The new Laredo Sector - (b)(7)(E) BPS (LRT (b)(7)(E) BPS) shall meet Border Patrol's mission requirements for a new (b)(7)(E) Border Patrol Station and Checkpoint in (b)(7)(E)

Attachment to Scope of Mod HSBP1015X00161.1
For Mod P000002, 9/28/17

(b)(7)(E) Texas, in accordance with the U.S. Border Patrol Facility Design Standard - Border Patrol Station Baseline Design Requirements (Publication Date: July 1, 2014), as agreed upon in the PRD by Border Patrol HQ, Sector and Station officials, BPAM PMO HQ and regional managers, the USACE ECSO HQ and regional district engineers.

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: PR Facilities Evaluations

Date: Thu Oct 05 2017 12:21:48 EDT

Attachments:

Agree with you (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, October 05, 2017 10:44 AM

To:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: PR Facilities Evaluations

The facility evaluation of properties in PR will need to address structural and engineering systems. To understand the deficiencies and be qualified to identify corrective measures, professionals licensed in their area of expertise is required. This is particularly true for structural, electrical and fire protection. Other experts should include registered architects, as well as plumbing, mechanical and civil engineers.

(b) (5)

A/E Technical Services has not been contacted for input on this issue. The evaluation does not have professional architectural/engineering oversight and QC.

(b)(6);(b)(7)(C)

Chief Architect, A/E Services Division

Border Patrol & Air and Marine PMO

Office of Facilities and Asset Management

Office of Administration, U.S. Customs and Border Patrol

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

CBP, 150 Westpark Way, Euless, Texas 76040

Excel as a trusted strategic partner enhancing Border Patrol's proud legacy

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: PR Facilities Evaluations

Date: Thu Oct 05 2017 11:58:16 EDT

Attachments: RE: PR Facilities Evaluations (1).msg

Follow-up call from the PR Facilities Evaluation email attached

<<RE: PR Facilities Evaluations>>

To: RE: PR F (b)(6);(b)(7)(C)
Cc: (b)(6);(b)(7)(C)
From: (b)(6);(b)(7)(C)
Sent: Thur 10/5/2017 3:38:23 PM
Subject: RE: PR Facilities Evaluations

Let's stop the emails and set a call, this doesn't help.

Thanks,

(b)(6);(b)(7)(C) P.E.

PMO Deputy Director
Border Patrol & Air Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering (FM&E)
Office of Enterprise Services
U.S. Customs and Border Protection

24000 Avila Road
Suite 5200
Laguna Niguel, CA

(b)(6);(b)(7)(C) Office
Cell

(b)(6);(b)(7)(C)

(This message is for the designated recipient only and may contain privileged, proprietary, or otherwise private information. If you have received it in error, please notify the sender immediately and delete the original. Any other use of the email by you is prohibited.)

From: (b)(6);(b)(7)(C)

Sent: Thursday, October 5, 2017 8:37 AM

To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: RE: PR Facilities Evaluations

(b) (5)

(b)(6);(b)(7)(C), Chief Architect, CBP BPAM PMO
Office: (b)(6);(b)(7)(C)
Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, October 05, 2017 10:29 AM

To: (b)(6);(b)(7)(C)
Cc: (b)(6);(b)(7)(C)

Subject: RE: PR Facilities Evaluations

My teams will evaluate and then I can determine if more is needed.

Thank You,

(b)(6);(b)(7)(C)

Branch Chief, Facilities
Border Patrol & Air and Marine Program Management Office (BPAM PMO)
Facilities Management and Engineering

Mobile: (b)(6);(b)(7)(C)

Email (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, October 05, 2017 11:26:44 AM

To: (b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: RE: PR Facilities Evaluations

The second hand information I have received is that (b)(6);(b)(7)(C) is organizing three facility evaluation teams (that is beyond the MMs?). (b)(6);(b)(7)(C) has been tasked to go to PR as part of those teams. (b)(5), (b)(6); (b)(7)(C)

(b)(6);(b)(7)(C)

I understand the exigency of the situation. (b)(5)

(b)(6);(b)(7)(C), Chief Architect, CBP BPAM PMO

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, October 05, 2017 9:58 AM

To: (b)(6);(b)(7)(C)

Subject: RE: PR Facilities Evaluations

Good information, but we are not there yet. We only have MM on site at the present and near future time. We will about this soon.

Thanks (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, October 05, 2017 7:43:56 AM

To: (b)(6);(b)(7)(C)

Subject: PR Facilities Evaluations

The facility evaluation of properties in PR will need to address structural and engineering systems. To understand the deficiencies and be qualified to identify corrective measures, professionals licensed in their area of expertise is required. This is particularly true for structural, electrical and fire protection. Other experts should include registered architects, as well as plumbing, mechanical and civil engineers.

(b)(5)

A/E Technical Services has not been contacted for input on this issue. The evaluation does not have professional architectural/engineering oversight and QC.

(b)(6);(b)(7)(C)

Chief Architect, A/E Services Division

Office of Facilities and Asset Management
Office of Administration, U.S. Customs and Border Patrol

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

CBP, 150 Westpark Way, Euless, Texas 76040

Excel as a trusted strategic partner enhancing Border Patrol's proud legacy

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: PR Facilities Evaluations

Date: Thu Oct 05 2017 11:40:11 EDT

Attachments:

agree

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, October 05, 2017 11:38 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: RE: PR Facilities Evaluations

Let's stop the emails an set a call, this doesn't help.

Thanks,

(b)(6);(b)(7)(C) P.E.

PMO Deputy Director

Border Patrol & Air Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering (FM&E)

Office of Enterprise Services

U.S. Customs and Border Protection

24000 Avila Road

Suite 5200

Laguna Niguel, CA

(b)(6);(b)(7)(C) Office

(b)(6);(b)(7)(C) Cell

(b)(6);(b)(7)(C)

(This message is for the designated recipient only and may contain privileged, proprietary, or otherwise private information. If you have received it in error, please notify the sender immediately and delete the original. Any other use of the email by you is prohibited.)

From: (b)(6);(b)(7)(C)

Sent: Thursday, October 5, 2017 8:37 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: RE: PR Facilities Evaluations

(b) (5)

(b)(6);(b)(7)(C) Chief Architect, CBP BPAM PMO

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, October 05, 2017 10:29 AM

To: (b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: RE: PR Facilities Evaluations

My teams will evaluate and then I can determine if more is needed.

Thank You,

(b)(6);(b)(7)(C)

Branch Chief, Facilities

Border Patrol & Air and Marine Program Managent Office (BPAM PMO)

Facilities Management and Engineering

Mobile: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, October 05, 2017 11:26:44 AM

To: (b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: RE: PR Facilities Evaluations

The second hand information I have received is that (b)(6);(b)(7)(C) is organizing three facility evaluation teams (that is beyond the MMs?). (b)(6);(b)(7)(C) has been tasked to go to PR as part of those teams. (b)(6);(b)(7)(C)

I understand the exigency of the situation.

(b) (5)

(b)(6);(b)(7)(C) Chief Architect, CBP BPAM PMO

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, October 05, 2017 9:58 AM

To: (b)(6);(b)(7)(C)

Subject: RE: PR Facilities Evaluations

Good information, but we are not there yet. We only have MM on site at the present and near future time. We will talk about this soon.

Thanks (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, October 05, 2017 7:43:56 AM

To: (b)(6);(b)(7)(C)

Subject: PR Facilities Evaluations

The facility evaluation of properties in PR will need to address structural and engineering systems. To understand the deficiencies and be qualified to identify corrective measures, professionals licensed in their area of expertise is required. This is particularly true for structural, electrical and fire protection. Other experts should include registered architects, as well as plumbing, mechanical and civil engineers.

(b) (5)

A/E Technical Services has not been contacted for input on this issue. The evaluation does not have professional architectural/engineering oversight and QC.

(b)(6);(b)(7)(C)

Chief Architect, A/E Services Division

Border Patrol & Air and Marine PMO

Office of Facilities and Asset Management

Office of Administration, U.S. Customs and Border Patrol

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

CBP, 150 Westpark Way, Euless, Texas 76040

Excel as a trusted strategic partner enhancing Border Patrol's proud legacy

(b) (6)

(b)(6);(b)(7)(C)

Attachments: 465841 RGV [REDACTED] Schedule 20171004.pdf
466411 RGV [REDACTED] Schedule 20171004.pdf
466412 RGV [REDACTED] Schedule 20171004.pdf
466413 RGV [REDACTED] Schedule 20171004.pdf
467742 SDC Secd Schedule 20171004.pdf
468012 RGV [REDACTED] Schedule 20171004.pdf

 V/r

(b) (6)

NOTICE: Do not release under the Freedom of Information Act, 5 U.S.C. § 552 (FOIA). This message [or document] contains personal and confidential information for the intended recipients and contains pre-decisional advice or information which is protected from disclosure under FOIA. Do not copy or release without prior authorization from the originator. Any review or distribution without consent is strictly prohibited. If you have received this information in error, please notify the sender immediately.

(b) (6)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

Page 143 of 1286

All,

Attached are the latest schedules for the FY18 Program.

Thank you,

(b) (6)

Program Specialist

CESWF-PM-PMO

W: (b)(6);(b)(7)(C)

F: (b)(6);(b)(7)(C)

CBP SWBBS RGV			Data Date 04-Oct-17							2018												2019											
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors																								
1	465841	CBP SWBBS RGV (b)(7)(E)	10-Apr-17	04-Jan-19	10-Apr-17 A	09-Jan-19	316d																										
2	465841.01000	Project Management	10-Apr-17	04-Jan-19	10-Apr-17 A	09-Jan-19	316d																										
3	PM1000	Start PMP	10-Apr-17		10-Apr-17 A		0d		PM1020, PM1050, PM1055																								
4	PM1050	Project Management (SWG)	10-Apr-17	31-Aug-18	10-Apr-17 A	05-Sep-18	231d	PM1000	CONS1250																								
5	PM1055	Project Management (SWF)	10-Apr-17	31-Aug-18	10-Apr-17 A	05-Sep-18	231d	PM1000	CONS1250																								
6	PM1020	Draft PMP	25-May-17	01-Aug-17	25-May-17 A	16-Aug-17 A	0d	PM1000	PM1030																								
7	PM1030	Process PMP for Approval	02-Aug-17	14-Aug-17	04-Oct-17	17-Oct-17	9d	PM1020	PM1040																								
8	(b) (5)																																
9	(b) (5)																																
10	465841.01000.01	Planning Phase	10-Apr-17	04-Aug-17	10-Apr-17 A	18-Sep-17 A	0d																										
11	PLAN1000	Planning Funds Received		10-Apr-17		10-Apr-17 A	0d		PLAN1010																								
12	PLAN1010	Kick-off Meeting	10-Apr-17	10-Apr-17	10-Apr-17 A	10-Apr-17 A	0d	PLAN1000	PLAN1020																								
13	PLAN1020	Process PRD	11-Apr-17	04-Aug-17	11-Apr-17 A	18-Sep-17 A	0d	PLAN1010	PLAN1030																								
14	(b) (5)																																
15	465841.95000	Environmental	10-Apr-17	18-Feb-18	10-Apr-17 A	14-Apr-18	131d																										
16	ENV1010	ESPs - Task Order Award	10-Apr-17	16-Jun-17	10-Apr-17 A	16-Jun-17 A	0d		ENV1015																								
17	ENV1015	ESPs - Task Order Award Milestone		16-Jun-17		16-Jun-17 A	0d	ENV1010																									
18	ENV1023	Obtain CATEX Required for Geotech	21-Jun-17	30-Jun-17	21-Jun-17 A	30-Jun-17 A	0d		ENV1025																								
19	ENV1025	CATEX Required for Geotech		30-Jun-17		30-Jun-17 A	0d	ENV1023																									
20	ENV1017	ESP Scope Development	26-Jul-17	22-Aug-17	26-Jul-17 A	16-Oct-17	8d		ENV1019																								
21	ENV1000	Waiver (DOJ, Secretary signature) - All RGV	01-Oct-17	15-Nov-17	04-Oct-17*	18-Nov-17	46d		ENV1005																								
22	(b) (5), (b) (7)(E)																																
23	(b) (5), (b) (7)(E)																																
24	(b) (5), (b) (7)(E)																																
25	(b) (5), (b) (7)(E)																																
26	(b) (5), (b) (7)(E)																																
27	(b) (5), (b) (7)(E)																																
28	(b) (5), (b) (7)(E)																																
29	(b) (5), (b) (7)(E)																																
30	(b) (5), (b) (7)(E)																																
31	(b) (5), (b) (7)(E)																																
32	(b) (5), (b) (7)(E)																																
33	(b) (5), (b) (7)(E)																																
34	(b) (5), (b) (7)(E)																																
35	(b) (5), (b) (7)(E)																																
36	(b) (5), (b) (7)(E)																																
37	(b) (5), (b) (7)(E)																																
38	(b) (5), (b) (7)(E)																																
39	(b) (5), (b) (7)(E)																																
40	465841.40000	Design & Procurement	14-Apr-17	29-Dec-17	14-Apr-17 A	03-Jan-18	61d																										
41	AE-S1060	SWF SOW Prep	14-Apr-17	14-Jun-17	14-Apr-17 A	14-Jun-17 A	0d	AE-S1090	AE-S1140																								
42	AE-S1070	MVK SOW Prep	14-Apr-17	14-Jun-17	14-Apr-17 A	14-Jun-17 A	0d	AE-S1090	AE-S1140																								
43	AE-S1080	SWG SOW Prep	14-Apr-17	14-Jun-17	14-Apr-17 A	14-Jun-17 A	0d	AE-S1090	AE-S1140																								

CBP SWBBS RGV			Data Date 04-Oct-17																		
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors												
44	AE-S1075	MVP SOW Prep (H&H)	20-Apr-17	14-Jun-17	20-Apr-17 A	14-Jun-17 A	0d	AE-S1090	AE-S1140	(b) (5)											
45	PROC1000	SWF CT Support	21-Apr-17	29-Dec-17	21-Apr-17 A	03-Jan-18	61d	AE-S1100	CONS1000												
46	AE-S1150	CBP RGV- XXXX Design Contract (Base) - W9126G17F0015	14-Jun-17	29-Dec-17	14-Jun-17 A	03-Jan-18	92d	AE-S1140	CONS1000												
47	DES1000	Design Support (SWF)	14-Jun-17	29-Dec-17	14-Jun-17 A	03-Jan-18	61d	AE-S1140	CONS1000												
48	DES1001	Design Support (SWG)	14-Jun-17	29-Dec-17	14-Jun-17 A	03-Jan-18	61d	AE-S1140	CONS1000												
49	DES1002	Design Support (MVP)			14-Jun-17 A	03-Jan-18	61d	AE-S1140	CONS1000												
50	465841.40000.01	A/E Solicitation & Award	14-Apr-17	14-Jun-17	14-Apr-17 A	14-Jun-17 A	0d			(b) (5)											
51	AE-S1090	A/E SOW Complete	14-Apr-17	20-Apr-17	14-Apr-17 A	20-Apr-17 A	0d		AE-S1100, AE-S1060, AE-S1110												
52	AE-S1100	A/E RFP Complete	21-Apr-17	12-May-17	21-Apr-17 A	12-May-17 A	0d	AE-S1090	AE-S1110, PROC1000												
53	AE-S1110	A/E Proposal Preparation	13-May-17	24-May-17	13-May-17 A	24-May-17 A	0d	AE-S1100	AE-S1120												
54	AE-S1120	Pre-Award Activities	25-May-17	02-Jun-17	25-May-17 A	02-Jun-17 A	0d	AE-S1110	AE-S1140, AE-S1125												
55	AE-S1125	CBP Congressional Notification	02-Jun-17	14-Jun-17	02-Jun-17 A	14-Jun-17 A	0d	AE-S1120	AE-S1140												
56	AE-S1140	Award		14-Jun-17		14-Jun-17 A	0d	AE-S1120, AE-S1060, AE-S1110	AE-S1150, DES1110, DES1111												
57	465841.40000.02	Design	14-Jun-17	10-Oct-17	14-Jun-17 A	11-Oct-17	5d														
58	DES1100	NTP Design Acknowledged		14-Jun-17		14-Jun-17 A	0d	AE-S1140	DES1130, DES1155												
59	DES1130	35% Design Start (milestone)	19-Jun-17		19-Jun-17 A		0d	DES1100	DES1140												
60	DES1140	35% Design & RFP	19-Jun-17	23-Jul-17	19-Jun-17 A	23-Jul-17 A	0d	DES1130	PROC1030, DES1145	(b) (5)											
61	DES1150	Geotechnical Survey	19-Jun-17	03-Aug-17	19-Jun-17 A	03-Aug-17 A	0d	AE-S1140													
62	DES1160	Topographic Survey	19-Jun-17	20-Jul-17	19-Jun-17 A	20-Jul-17 A	0d	AE-S1140	DES1220												
63	DES1155	Kickoff Meeting		26-Jun-17		26-Jun-17 A	0d	DES1100													
64	DES1110	Scoping Charrette	06-Jul-17	06-Jul-17	06-Jul-17 A	06-Jul-17 A	0d	AE-S1140	DES1120												
65	DES1120	Scoping Charrette Complete		06-Jul-17		06-Jul-17 A	0d	DES1110													
66	DES1145	35% Design Submittal (Draft Geotech Submittal)		23-Jul-17		23-Jul-17 A	0d	DES1140	DES1170, DES1180												
67	DES1170	35% Submittal Review	24-Jul-17	27-Jul-17	24-Jul-17 A	27-Jul-17 A	0d	DES1145	DES1190, DES1180												
68	DES1180	BCOES 35% Submittal Review	24-Jul-17	27-Jul-17	24-Jul-17 A	27-Jul-17 A	0d	DES1170, DES1145	DES1200, DES1190												
69	DES1190	35% Review Conference	28-Jul-17	28-Jul-17	28-Jul-17 A	28-Jul-17 A	0d	DES1170, DES1180	DES1200												
70	DES1200	35% Design Submittal Reviewed and Approved		28-Jul-17		28-Jul-17 A	0d	DES1190, DES1180	PROC1010, PROC1055, DES1230, DES1125	(b) (5)											
71	DES1220	65% Design & RFP	29-Jul-17	16-Aug-17	29-Jul-17 A	16-Aug-17 A	0d	DES1160, PROC1055, DES1220	DES1230, DES1240												
72	DES1125	65% Design Submittal		16-Aug-17		16-Aug-17 A	0d	DES1220	DES1230, DES1240												
73	DES1230	65% Submittal Review	17-Aug-17	21-Aug-17	17-Aug-17 A	21-Aug-17 A	0d	DES1220, DES1125	DES1250, DES1240												
74	DES1240	BCOES 65% Submittal Review	17-Aug-17	23-Aug-17	17-Aug-17 A	21-Aug-17 A	0d	DES1230, DES1125	DES1260												
75	DES1250	65% Review Conference	22-Aug-17	22-Aug-17	22-Aug-17 A	22-Aug-17 A	0d	DES1230	DES1260												
76	DES1260	65% Design Submittal Reviewed and Approved		23-Aug-17		22-Aug-17 A	0d	DES1250, DES1240	PROC1057, DES1280												
77	DES1280	95% Design/Final RFP Prep	24-Aug-17	10-Sep-17	23-Aug-17 A	10-Sep-17 A	0d	PROC1030, PROC1050, PR	DES1290, DES1275, DES1282												
78	DES1275	95% Design Submittal		10-Sep-17		10-Sep-17 A	0d	DES1280	DES1290, DES1300												
79	DES1282	Decision Point on Buy American Act				10-Sep-17 A	0d	DES1280													
80	DES1290	95% Submittal Review	11-Sep-17	14-Sep-17	11-Sep-17 A	14-Sep-17 A	0d	DES1280, DES1275	DES1310, DES1300	(b) (5)											
81	DES1300	BCOES 95% Submittal Review	11-Sep-17	14-Sep-17	11-Sep-17 A	14-Sep-17 A	0d	DES1290, DES1275	DES1320												
82	DES1310	95% Review Conference	15-Sep-17	15-Sep-17	15-Sep-17 A	15-Sep-17 A	0d	DES1290	DES1320												
83	DES1320	95% Design Submittal Reviewed and Approved		15-Sep-17		15-Sep-17 A	0d	DES1310, DES1300	DES1340												
84	DES1340	Corrected Final RFP Prep	16-Sep-17	04-Oct-17	16-Sep-17 A	05-Oct-17	2d	PROC1480, DES1320	DES1360, DES1350												
85																					
86																					
87																					

(b) (5)

CBP SWBBS RGV			Data Date 04-Oct-17																			
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors	17	2018				2019							
132																						
133																						
134																						
135																						
136																						
137																						
138																						
139																						
140																						
141																						
142																						
143																						
144																						
145																						
146																						
147																						
148																						
149																						
150																						
151																						

(b) (5)

CBP SWBBS RGV			Data Date 04-Oct-17																				
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors	17	2018				2019								
44	RE1241	Title Abstraction	10-Jul-17	13-Jul-18	10-Jul-17 A	13-Jul-18	194d		RE1242														
45	(b) (5)																						
46																							
47																							
48																							
49																							
50																							
51																							
52																							
53																							
54																							
55																							
56																							
57																							
58																							
59																							
60																							
61																							
62	466411.91000 Strategic Communications		19-Jul-17	02-Jul-19	19-Jul-17 A	02-Jul-19	437d																
63	SC1020	Initiate Congressional, State and Local Govt Engagement	19-Jul-17	05-Oct-17	19-Jul-17 A	27-Oct-17	17d																
64	RE3376	Develop outreach strategy	13-Sep-17	15-Sep-17	04-Oct-17	06-Oct-17	3d		RE3386														
65	SC1080	Survey Messaging	13-Sep-17	11-Oct-17	04-Oct-17	01-Nov-17	20d																
66	(b) (5)																						
67																							
68																							
69																							
70																							
71																							
72																							
73																							
74																							
75																							
76	466411.40000 Design Build/RFP & Procurement		14-Jun-17	10-Jul-18	14-Jun-17 A	10-Jul-18	191d																
77	466411.40000.01 AE Procurement - OBE		14-Jun-17	10-Jul-18	14-Jun-17 A	10-Jul-18	191d																
78	DES1530	AE Contract/Task Order Award		14-Jun-17		14-Jun-17 A	0d		DES1570, AE-C0991														
79	DES1570	A-E Task Order - W9126G17F0015	14-Jun-17	10-Jul-18	14-Jun-17 A	10-Jul-18	191d	DES1530	CONS1000														
80	466411.40000.02 AE Procurement		31-Jul-17	10-Jul-18	31-Jul-17 A	10-Jul-18	191d																
81	AE-S1090	A/E SOW Complete	31-Jul-17	17-Aug-17	31-Jul-17 A	17-Aug-17 A	0d		AE-S1100, PROC1000														
82	PROC1000	RG A/E SWF Support	31-Jul-17	29-Sep-17	31-Jul-17 A	26-Sep-17 A	0d	AE-S1090	AE-S1140														
83	AE-S1100	A/E RFP Complete	18-Aug-17	24-Aug-17	18-Aug-17 A	24-Aug-17 A	0d	AE-S1090	AE-S1110														
84	AE-S1110	A/E Proposal Preparation	25-Aug-17	22-Sep-17	25-Aug-17 A	19-Sep-17 A	0d	AE-S1100	AE-S1120														
85	AE-S1120	Pre-Award Activities	25-Sep-17	29-Sep-17	20-Sep-17 A	26-Sep-17 A	0d	AE-S1110	AE-S1140														
86	AE-S1140	Award		29-Sep-17		26-Sep-17 A	0d	AE-S1120, PROC1000	AE-S1150, AE-C0990														

CBP SWBBS RGV			Data Date 04-Oct-17																		
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors	7	8	9	10	11	12	13	14	15	16	17	18
87	AE-S1150	CBP SWBBS RGV MOA/E - W9126G17F0197	30-Sep-17	10-Jul-18	26-Sep-17 A	10-Jul-18	280d	AE-S1140	CONS1000												
88	466411.40000.03	Design	09-Aug-17	01-Mar-18	09-Aug-17 A	01-Mar-18	92d														
89																					
90																					
91																					
92																					
93																					
94																					
95																					
96																					
97																					
98																					
99																					
100																					
101																					
102																					
103																					
104																					
105																					
106																					
107																					
108																					
109																					
110																					
111																					
112																					
113																					
114																					
115																					
116																					
117																					
118																					
119																					
120																					
121																					
122																					
123																					
124																					
125																					
126																					
127																					
128																					
129																					

CBP SWBBS RGV: (b) (5)			Data Date 04-Oct-17																	
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors	17	2018				2019					
(b) (5)										(b) (5)										

CBP SWBBS RGV			Data Date 04-Oct-17																					
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors															
1	466412 CBP SWBBS RGV		10-Apr-17	01-Nov-19	10-Apr-17 A	01-Nov-19	522d																	
2	466412.01000 Project Management		13-Sep-17	01-Nov-19	04-Oct-17	01-Nov-19	522d																	
3	PM1000	Start PMP	13-Sep-17		04-Oct-17		0d		PM1020, PM1050, PM1055															
4	PM1020	Draft PMP	13-Sep-17	26-Sep-17	04-Oct-17	18-Oct-17	10d	PM1000	PM1030															
5	PM1050	Project Management (SWG)	13-Sep-17	01-Nov-19	04-Oct-17	01-Nov-19	522d	PM1000	PCO1000															
6	PM1055	Project Management (SWF)	13-Sep-17	01-Nov-19	04-Oct-17	01-Nov-19	522d	PM1000	PCO1000															
7																								
8																								
9																								
10																								
11	466412.01000.01 Planning Phase		13-Sep-17	10-Oct-17	04-Oct-17	31-Oct-17	19d																	
12	PLAN1020	Process PRD	13-Sep-17	10-Oct-17	04-Oct-17	31-Oct-17	19d		PLAN1030															
13																								
14	466412.95000 Environmental		10-Apr-17	09-Aug-18	10-Apr-17 A	09-Aug-18	213d																	
15	ENV1010	ESPs - Task Order Award	10-Apr-17	16-Jun-17	10-Apr-17 A	16-Jun-17 A	0d		ENV1015															
16	ENV1015	ESPs - Task Order Award Milestone		16-Jun-17		16-Jun-17 A	0d	ENV1010																
17	ENV1023	Obtain CATEX Required for Geotech	21-Jun-17	30-Jun-17	21-Jun-17 A	30-Jun-17 A	0d		ENV1025															
18	ENV1025	CATEX Required for Geotech		30-Jun-17		30-Jun-17 A	0d	ENV1023																
19	ENV1000	Waiver (DOJ, Secretary signature) - All RGV	01-Oct-17	15-Nov-17	04-Oct-17*	18-Nov-17	46d		ENV1005															
20																								
21																								
22																								
23																								
24																								
25																								
26																								
27	466412.90000 Real Estate		10-Jul-17	08-Apr-19	10-Jul-17 A	08-Apr-19	377d																	
28	466412.90000.1 Communications Outreach		10-Jul-17	22-Dec-17	10-Jul-17 A	22-Dec-17	55d																	
29	RE1060	Identify land owners via tax records	10-Jul-17	19-Sep-17	10-Jul-17 A	11-Oct-17	5d		RE1140															
30	RE1030	Develop outreach strategy	13-Sep-17	15-Sep-17	04-Oct-17	06-Oct-17	3d		RE1040, RE1050															
31																								
32																								
33																								
34																								
35																								
36																								
37																								
38																								
39																								
40																								
41																								
42																								
43	466412.90000.2 Real Estate Clearance		10-Jul-17	08-Apr-19	10-Jul-17 A	08-Apr-19	377d																	

2018

2019

</

CBP SWBBS RGVS			Data Date 04-Oct-17																	
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors	17	18	19	20	21	22	23	24	25	26	27
44	RE1241	Title Abstraction	10-Jul-17	13-Jul-18	10-Jul-17 A	13-Jul-18	194d		RE1242											
45	(b) (5)																			
46	(b) (5)																			
47	(b) (5)																			
48	(b) (5)																			
49	(b) (5)																			
50	(b) (5)																			
51	(b) (5)																			
52	(b) (5)																			
53	(b) (5)																			
54	(b) (5)																			
55	(b) (5)																			
56	(b) (5)																			
57	(b) (5)																			
58	(b) (5)																			
59	(b) (5)																			
60	(b) (5)																			
61	(b) (5)																			
62	466412.91000 Strategic Communications		19-Jul-17	06-Dec-18	19-Jul-17 A	06-Dec-18	294d													
63	SC1020	Initiate Congressional, State and Local Govt Engagement	19-Jul-17	05-Oct-17	19-Jul-17 A	27-Oct-17	17d													
64	RE3376	Develop outreach strategy	24-Jul-17	15-Sep-17	24-Jul-17 A	06-Oct-17	3d		RE3386											
65	(b) (5)																			
66	(b) (5)																			
67	(b) (5)																			
68	(b) (5)																			
69	(b) (5)																			
70	(b) (5)																			
71	(b) (5)																			
72	(b) (5)																			
73	(b) (5)																			
74	466412.40000 Design Build/RFP & Procurement		01-Jun-17	10-Jul-18	01-Jun-17 A	10-Jul-18	191d													
75	466412.40000.01 AE Procurement - Surveys		01-Jun-17	18-Mar-18	01-Jun-17 A	08-Apr-18	126d													
76	DES1580	Receipt of Funds	01-Jun-17		01-Jun-17 A		0d		DES1620, DES1590											
77	DES1590	A-E Selection	01-Jun-17	05-Jun-17	01-Jun-17 A	05-Jun-17 A	0d	DES1580	DES1620											
78	DES1620	Prepare AE SOW	06-Jun-17	12-Jun-17	06-Jun-17 A	12-Jun-17 A	0d	DES1580, DES1590	DES1540											
79	DES1540	AE SOW Development Complete		12-Jun-17		12-Jun-17 A	0d	DES1620	DES1550											
80	DES1550	Request for A-E Technical Qualification	13-Jun-17	14-Jun-17	13-Jun-17 A	14-Jun-17 A	0d	DES1540	DES1530											
81	DES1530	AE Contract/Task Order Award		14-Jun-17		14-Jun-17 A	0d	DES1550	DES1570											
82	DES1570	A-E Task Order - W9126G17F0015	15-Jun-17	18-Mar-18	15-Jun-17 A	08-Apr-18	187d	DES1530	AE-C0991											
83	466412.40000.02 AE Procurement - RFP		31-Jul-17	10-Jul-18	31-Jul-17 A	10-Jul-18	191d													
84	AE-S1090	A/E SOW Complete	31-Jul-17	15-Aug-17	31-Jul-17 A	15-Aug-17 A	0d		AE-S1100, PROC1000											
85	PROC1000	RGVS A/E SWF Support	31-Jul-17	25-Sep-17	31-Jul-17 A	22-Sep-17 A	0d	AE-S1090	AE-S1140											
86	AE-S1100	A/E RFP Complete	16-Aug-17	22-Aug-17	16-Aug-17 A	22-Aug-17 A	0d	AE-S1090	AE-S1110											

CBP SWBBS RG (b)(7)(E)			Data Date 04-Oct-17																		
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors												
87	AE-S1110	A/E Proposal Preparation	23-Aug-17	30-Aug-17	23-Aug-17 A	30-Aug-17 A	0d	AE-S1100	AE-S1120	(b) (5)											
88	AE-S1120	Pre-Award Activities	13-Sep-17	25-Sep-17	01-Sep-17 A	22-Sep-17 A	0d	AE-S1110	AE-S1140												
89	AE-S1140	Award		25-Sep-17		22-Sep-17 A	0d	AE-S1120, PROC1000	AE-S1150, AE-C0990												
90	AE-S1150	RGV D/B A/E RFP Prep W9126G17F0160	26-Sep-17	10-Jul-18	22-Sep-17 A	10-Jul-18	280d	AE-S1140	AP1070												
91	466412.40000.03	A/E Design & RFP Prep	09-Aug-17	01-Mar-18	09-Aug-17 A	01-Mar-18	91d														
92	AE-C1057	Pre-Qualification List Approved (Tied to P20 in Pre-Qual Schedule)		09-Aug-17		09-Aug-17 A	0d		AE-C1060	(b) (5)											
93																					
94																					
95																					
96																					
97																					
98																					
99																					
100																					
101																					
102																					
103																					
104																					
105																					
106																					
107																					
108																					
109																					
110																					
111																					
112																					
113																					
114																					
115																					
116																					
117																					
118																					
119																					
120																					
121																					
122																					
123																					
124																					
125																					
126																					
127																					
128																					
129																					

CBP SWBBS RGV			Data Date 04-Oct-17																
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors	17	2018				2019				
130																			
131																			
132																			
133																			
134																			
135																			
136																			
137																			
138																			
139																			
140																			
141																			
142																			
143																			
144																			
145																			
146																			
147																			
148																			
149																			
150																			
151																			
152																			
153																			
154																			
155																			
156																			
157																			
158																			
159																			
160																			
161																			
162																			
163																			
164																			
165																			
166																			
167																			
168																			
169																			
170																			
171																			
172																			

CBP SWBBS RGV			Data Date 04-Oct-17																		
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors	17	2018				2019						
173																					
174																					
(b) (5)																					

CBP SWBBS RGV			Data Date 04-Oct-17							
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors	
1	466413 CBP SWBBS RGV		10-Apr-17	01-Nov-19	10-Apr-17 A	01-Nov-19	522d			
2	466413.01000 Project Management		13-Sep-17	01-Nov-19	04-Oct-17	01-Nov-19	522d			
3	PM1000	Start PMP	13-Sep-17		04-Oct-17		0d		PM1020, PM1050, PM1055	
4	PM1020	Draft PMP	13-Sep-17	26-Sep-17	04-Oct-17	18-Oct-17	10d	PM1000	PM1030	
5	PM1050	Project Management (SWG)	13-Sep-17	01-Nov-19	04-Oct-17	01-Nov-19	522d	PM1000	PCO1000	
6	PM1055	Project Management (SWF)	13-Sep-17	01-Nov-19	04-Oct-17	01-Nov-19	522d	PM1000	PCO1000	
7	(b) (5)									
8										
9										
10										
11	466413.01000.01 Planning Phase		13-Sep-17	10-Oct-17	04-Oct-17	31-Oct-17	19d			
12	PLAN1020	Process PRD	13-Sep-17	10-Oct-17	04-Oct-17	31-Oct-17	19d		PLAN1030	
13	(b) (5)									
14	466413.95000 Environmental		10-Apr-17	09-Aug-18	10-Apr-17 A	09-Aug-18	213d			
15	ENV1010	ESPs - Task Order Award	10-Apr-17	16-Jun-17	10-Apr-17 A	16-Jun-17 A	0d		ENV1015	
16	ENV1015	ESPs - Task Order Award Milestone		16-Jun-17		16-Jun-17 A	0d	ENV1010		
17	ENV1023	Obtain CATEX Required for Geotech	21-Jun-17	30-Jun-17	21-Jun-17 A	30-Jun-17 A	0d		ENV1025	
18	ENV1025	CATEX Required for Geotech		30-Jun-17		30-Jun-17 A	0d	ENV1023		
19	ENV1000	Waiver (DOJ, Secretary signature) - All RGV	01-Oct-17	15-Nov-17	04-Oct-17*	18-Nov-17	46d		ENV1005	
20	(b) (5)									
21										
22										
23										
24										
25										
26										
27	466413.90000 Real Estate		10-Jul-17	08-Apr-19	10-Jul-17 A	08-Apr-19	377d			
28	466413.90000.1 Communications Outreach		10-Jul-17	22-Dec-17	10-Jul-17 A	22-Dec-17	55d			
29	RE1060	Identify land owners via tax records	10-Jul-17	19-Sep-17	10-Jul-17 A	11-Oct-17	5d		RE1140	
30	RE1030	Develop outreach strategy	24-Jul-17	15-Sep-17	24-Jul-17 A	06-Oct-17	3d		RE1040, RE1050	
31	RE1040	Develop outreach message/elevator speech	18-Sep-17	22-Sep-17	10-Oct-17	16-Oct-17	5d	RE1030	RE1150	
32	RE1050	Identify teams for visits	18-Sep-17	22-Sep-17	10-Oct-17	16-Oct-17	5d	RE1030		
33	(b) (5)									
34										
35										
36										
37										
38										
39										
40										
41										
42										
43	466413.90000.2 Real Estate Clearance		10-Jul-17	08-Apr-19	10-Jul-17 A	08-Apr-19	377d			

CBP SWBBS RGV			Data Date 04-Oct-17																	
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors	17	18	19	20	21	22	23	24	25	26	27
44	RE1241	Title Abstraction	10-Jul-17	13-Jul-18	10-Jul-17 A	13-Jul-18	194d		RE1242											
45	(b) (5)																			
46																				
47																				
48																				
49																				
50																				
51																				
52																				
53																				
54																				
55																				
56																				
57																				
58																				
59																				
60																				
61																				
62	466413.91000 Strategic Communications		19-Jul-17	06-Dec-18	19-Jul-17 A	06-Dec-18	294d													
63	SC1020	Initiate Congressional, State and Local Govt Engagement	19-Jul-17	05-Oct-17	19-Jul-17 A	27-Oct-17	17d													
64	RE3376	Develop outreach strategy	24-Jul-17	15-Sep-17	24-Jul-17 A	06-Oct-17	3d		RE3386											
65	(b) (5)																			
66																				
67																				
68																				
69																				
70																				
71																				
72																				
73																				
74	466413.40000 Design Build/RFP & Procurement		01-Jun-17	10-Jul-18	01-Jun-17 A	10-Jul-18	191d													
75	466413.40000.01 AE Procurement - Surveys		01-Jun-17	14-Oct-17	01-Jun-17 A	04-Nov-17	22d													
76	DES1580	Receipt of Funds	01-Jun-17		01-Jun-17 A		0d		DES1620, DES1590											
77	DES1590	A-E Selection	01-Jun-17	05-Jun-17	01-Jun-17 A	05-Jun-17 A	0d	DES1580	DES1620											
78	DES1620	Prepare AE SOW	06-Jun-17	12-Jun-17	06-Jun-17 A	12-Jun-17 A	0d	DES1580, DES1590	DES1540											
79	DES1540	AE SOW Development Complete		12-Jun-17		12-Jun-17 A	0d	DES1620	DES1550											
80	DES1550	Request for A-E Technical Qualification	13-Jun-17	14-Jun-17	13-Jun-17 A	14-Jun-17 A	0d	DES1540	DES1530											
81	DES1530	AE Contract/Task Order Award		14-Jun-17		14-Jun-17 A	0d	DES1550	DES1570, AE-C0991											
82	DES1570	A-E Task Order - W9126G17F0015	15-Jun-17	14-Oct-17	15-Jun-17 A	04-Nov-17	32d	DES1530												
83	466413.40000.02 AE Procurement - RFP		31-Jul-17	10-Jul-18	31-Jul-17 A	10-Jul-18	191d													
84	AE-S1090	A/E SOW Complete	31-Jul-17	15-Aug-17	31-Jul-17 A	15-Aug-17 A	0d		AE-S1100, PROC1000											
85	PROC1000	RGV A/E SWF Support	31-Jul-17	25-Sep-17	31-Jul-17 A	29-Sep-17 A	0d	AE-S1090	AE-S1140											
86	AE-S1100	A/E RFP Complete	16-Aug-17	22-Aug-17	16-Aug-17 A	22-Aug-17 A	0d	AE-S1090	AE-S1110											

CBP SWBBS RGV			Data Date 04-Oct-17																		
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors												
87	AE-S1110	A/E Proposal Preparation	23-Aug-17	30-Aug-17	23-Aug-17 A	30-Aug-17 A	0d	AE-S1100	AE-S1120	(b) (5)											
88	AE-S1120	Pre-Award Activities	13-Sep-17	25-Sep-17	22-Sep-17 A	29-Sep-17 A	0d	AE-S1110	AE-S1140												
89	AE-S1140	Award		25-Sep-17		29-Sep-17 A	0d	AE-S1120, PROC1000	AE-S1150, AE-C0990												
90	AE-S1150	RGV D/B A/E RFP Prep - W9126G-17-F-0200	26-Sep-17	10-Jul-18	29-Sep-17 A	10-Jul-18	280d	AE-S1140	AP1070												
91	466413.40000.03	A/E Design & RFP Prep	09-Aug-17	01-Mar-18	09-Aug-17 A	01-Mar-18	90d														
92	AE-C1057	Pre-Qualification List Approved (Tied to P20 in Pre-Qual Schedule)		09-Aug-17		09-Aug-17 A	0d		AE-C1060	(b) (5)											
93																					
94																					
95																					
96																					
97																					
98																					
99																					
100																					
101																					
102																					
103																					
104																					
105																					
106																					
107																					
108																					
109																					
110																					
111																					
112																					
113																					
114																					
115																					
116	466413.40000.04 Construction Procurement; Pre-Qual List		13-Sep-17	10-Jul-18	04-Oct-17	10-Jul-18	191d														
117	466413.40000.04.01 Pre-Solicitation Phase		13-Sep-17	23-Mar-18	04-Oct-17	23-Mar-18	116d														
118	PROC1010	ART Request		13-Sep-17		04-Oct-17	0d			PROC1070, PROC1020											
119	PROC1020	Prepare Draft Evaluation Criteria and Draft Source Selection Plan (SSP)	13-Sep-17	27-Sep-17	04-Oct-17	19-Oct-17	11d	PROC1030, PROC1010		PROC1040											
120	PROC1030	Prepare DIV 00 Specs 35%	13-Sep-17	19-Sep-17	04-Oct-17	11-Oct-17	5d			PROC1020											
121	PROC1057	Prepare DIV 00 Specs 95%	13-Sep-17	18-Sep-17	04-Oct-17	10-Oct-17	4d														
122	PROC1480	Prepare DIV 00 Specs 100%	13-Sep-17	18-Sep-17	04-Oct-17	10-Oct-17	4d														
123										(b) (5)											
124																					
125																					
126																					
127																					
128																					
129																					

CBP SWBBS RGV			Data Date 04-Oct-17																
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors	17	2018				2019				
130																			
131																			
132																			
133																			
134																			
135																			
136																			
137																			
138																			
139																			
140																			
141																			
142																			
143																			
144																			
145																			
146																			
147																			
148																			
149																			
150																			
151																			
152																			
153																			
154																			
155																			
156																			
157																			
158																			
159																			
160																			
161																			
162																			
163																			
164																			
165																			
166																			
167																			
168																			
169																			
170																			
171																			
172																			

(b) (5)

CBP SWBBS SDC Replace Secondary Pedestrian Fence			Data Date 04-Oct-17																
#	Activity ID	Activity Name	Start	Finish	Remaining Duration	Predecessors	Successors	7 J A S O N D J F M A M J J A S O N D J F M A M J J A S 2018 2019											
1	467742 CBP SWBBS SDC Replace Secondary Pedestrian Fence		11-Aug-17 A	03-Jan-18	61d			(b) (5)											
2	467742.01000 Project Management		11-Aug-17 A	03-Jan-18	61d														
3	PLAN1020	Process PRD	11-Aug-17 A	31-Oct-17	19d		PLAN1030												
4	PM1000	SPL PM Support	11-Aug-17 A	03-Jan-18	61d	PM1010	PCO1000												
5	PM1010	Start PMP	11-Aug-17 A		0d		PM1020, PM1000												
6	PM1020	Draft PMP	11-Aug-17 A	18-Oct-17	10d	PM1010	PM1030												
7	(b) (5)							(b) (5)											
8																			
9																			
10																			
11	467742.40000 Design & Procurement		11-Aug-17 A	03-Jan-18	61d			(b) (5)											
12	467742.40000.01 A/E Solicitation & Award		11-Aug-17 A	03-Jan-18	61d														
13	AE-S1000	SWF SDC Sec'd Fence A/E Prep Support	11-Aug-17 A	18-Sep-17 A	0d	AE-S1090	AE-S1140												
14	AE-S1010	SPL SDC Sec'd Fence A/E Prep Support	11-Aug-17 A	18-Sep-17 A	0d	AE-S1090	AE-S1140												
15	AE-S1090	A/E SOW Complete	11-Aug-17 A	22-Aug-17 A	0d		AE-S1100, AE-S1010, AE-S11												
16	AE-S1100	A/E RFP Complete	23-Aug-17 A	01-Sep-17 A	0d	AE-S1090	AE-S1110												
17	AE-S1110	A/E Proposal Preparation	02-Sep-17 A	06-Sep-17 A	0d	AE-S1100	AE-S1120												
18	AE-S1120	Pre-Award Activities	07-Sep-17 A	19-Sep-17 A	0d	AE-S1110	AE-S1140												
19	AE-S1140	Award		19-Sep-17 A	0d	AE-S1120, AE-S1010, AE-S	AE-C0990, AE-S1150												
20	AE-S1150	SDC Sec'd Fence A/E Task Order - Design & RFP - W9126G17F0144	19-Sep-17 A	03-Jan-18	61d	AE-S1140	AE-C1060												
21	(b) (5)							(b) (5)											
22																			
23																			
24																			
25																			
26																			
27																			
28																			
29																			
30																			
31																			
32																			
33																			
34																			
35																			
36																			
37																			
38																			
39																			
40																			
41																			
42																			

CBP SWBBS SDC Replace Secondary Pedestrian Fence			Data Date 04-Oct-17																															
#	Activity ID	Activity Name	Start	Finish	Remaining Duration	Predecessors	Successors	7	2018												2019													
43								J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S
44	(b) (5)								(b) (5)																									
45	(b) (5)								(b) (5)																									
46	(b) (5)								(b) (5)																									
47	(b) (5)								(b) (5)																									

CBP SWBBS RGV			Data Date 04-Oct-17									
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors			
1	468012	CBP SWBBS RGV	07-Aug-17	13-Apr-19	07-Aug-17 A	13-Apr-19	381d					
2	468012.01000	Project Management	13-Sep-17	13-Apr-19	04-Oct-17	13-Apr-19	381d					
3	PM1000	Start PMP	13-Sep-17		04-Oct-17		0d		PM1020, PM1050, PM1055			
4	PM1020	Draft PMP	13-Sep-17	26-Sep-17	04-Oct-17	18-Oct-17	10d	PM1000	PM1030, PLAN1040			
5	PM1050	Project Management (SWG)	13-Sep-17	12-Apr-19	04-Oct-17	12-Apr-19	381d	PM1000	PCO1000			
6	PM1055	Project Management (SWF)	13-Sep-17	12-Apr-19	04-Oct-17	12-Apr-19	381d	PM1000	PCO1000			
7	(b) (5)											
8												
9												
10												
11												
12												
13	468012.95000	Environmental	13-Sep-17	27-Jun-18	04-Oct-17	27-Jun-18	183d					
14	ENV1000	Waiver (DOJ, Secretary signature) - All RGV	01-Oct-17	15-Nov-17	04-Oct-17*	18-Nov-17	46d		ENV1005			
15	ENV1010	ESPs - Task Order Award	13-Sep-17	17-Nov-17	04-Oct-17	08-Dec-17	66d		ENV1015			
16	ENV1023	Obtain CATEX Required for Geotech	13-Sep-17	25-Oct-17	04-Oct-17	16-Nov-17	30d		ENV1025			
17	(b) (5)											
18												
19												
20												
21												
22												
23												
24												
25												
26	468012.90000	Real Estate	16-Aug-17	15-Nov-17	16-Aug-17 A	24-Nov-17	35d					
27	468012.90000.1	Communications Outreach	16-Aug-17	16-Oct-17	16-Aug-17 A	06-Nov-17	23d					
28	RE1025	Clearance from CBP to engage with USFWS		16-Aug-17		16-Aug-17 A	0d		RE1030, RE3466, RE1140, RE1040, RE1050			
29	RE1030	Develop outreach strategy	21-Aug-17	15-Sep-17	21-Aug-17 A	06-Oct-17	3d	RE1025				
30	RE1140	Decision Point on Acquisition of 150 ft concurrent w Gate Impacted		15-Sep-17		06-Oct-17	0d	RE1025, RE3466				
31	(b) (5)											
32												
33												
34												
35	468012.90000.2	Real Estate Clearance	21-Aug-17	15-Nov-17	21-Aug-17 A	24-Nov-17	35d					
36	RE3466	Validate USFWS Ownership	21-Aug-17	15-Sep-17	21-Aug-17 A	06-Oct-17	3d	RE1025	RE1140			
37	RE1241	Title Abstraction	13-Sep-17	01-Nov-17	04-Oct-17	24-Nov-17	35d	RE1025	RE1340			
38	(b) (5)											
39												
40												
41												
42	468012.91000	Strategic Communications	21-Aug-17	16-Jul-18	21-Aug-17 A	16-Jul-18	195d					
43	RE3376	Develop outreach strategy	21-Aug-17	15-Sep-17	21-Aug-17 A	06-Oct-17	3d		RE3386			
44	SC1020	Initiate Congressional, State and Local Govt Engagement	21-Aug-17	05-Oct-17	21-Aug-17 A	27-Oct-17	17d	RE1025	RE3396			
45	(b) (5)											
46												

CBP SWBBS RGV			Data Date 04-Oct-17																																					
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30							
43	(b) (5)																												(b) (5)											
44	(b) (5)																												(b) (5)											
45	(b) (5)																												(b) (5)											
46	(b) (5)																												(b) (5)											
47	468012.40000 Design Build/RFP & Procurement		07-Aug-17	13-Mar-18	07-Aug-17 A	13-Mar-18	108d																																	
48	468012.40000.01 AE Procurement - RFP		07-Aug-17	13-Mar-18	07-Aug-17 A	13-Mar-18	108d																																	
49	AE-S1090	A/E SOW Complete	07-Aug-17	18-Aug-17	07-Aug-17 A	18-Aug-17 A	0d		AE-S1100, PROC1000																															
50	PROC1000	RGV Mod CT Support	07-Aug-17	07-Sep-17	07-Aug-17 A	07-Sep-17 A	0d	AE-S1090	AE-S1140																															
51	AE-S1100	A/E RFP Complete	22-Aug-17	22-Aug-17	22-Aug-17 A	22-Aug-17 A	0d	AE-S1090	AE-S1110																															
52	AE-S1110	A/E Proposal Preparation	23-Aug-17	28-Aug-17	23-Aug-17 A	28-Aug-17 A	0d	AE-S1100	AE-S1120																															
53	AE-S1120	Pre-Award Activities	29-Aug-17	07-Sep-17	29-Aug-17 A	07-Sep-17 A	0d	AE-S1110	AE-S1140																															
54	AE-S1140	Award		07-Sep-17		07-Sep-17 A	0d	AE-S1120, PROC1000	AE-S1150, AE-C0990, AE-C1																															
55	AE-S1150	CBP SWBBS RGV A/E	07-Sep-17	13-Mar-18	07-Sep-17 A	13-Mar-18	161d	AE-S1140	AP1020																															
56	(b) (5)																												(b) (5)											
57	(b) (5)																												(b) (5)											
58	(b) (5)																												(b) (5)											
59	(b) (5)																												(b) (5)											
60	(b) (5)																												(b) (5)											
61	(b) (5)																												(b) (5)											
62	(b) (5)																												(b) (5)											
63	(b) (5)																												(b) (5)											
64	(b) (5)																												(b) (5)											
65	(b) (5)																												(b) (5)											
66	(b) (5)																												(b) (5)											
67	(b) (5)																												(b) (5)											
68	(b) (5)																												(b) (5)											
69	(b) (5)																												(b) (5)											
70	(b) (5)																												(b) (5)											
71	(b) (5)																												(b) (5)											
72	(b) (5)																												(b) (5)											
73	(b) (5)																												(b) (5)											
74	(b) (5)																												(b) (5)											
75	(b) (5)																												(b) (5)											
76	(b) (5)																												(b) (5)											
77	(b) (5)																												(b) (5)											
78	(b) (5)																												(b) (5)											
79	(b) (5)																												(b) (5)											
80	(b) (5)																												(b) (5)											
81	(b) (5)																												(b) (5)											
82	(b) (5)																												(b) (5)											
83	(b) (5)																												(b) (5)											
84	(b) (5)																												(b) (5)											
85	(b) (5)																												(b) (5)											

CBP SWBBS RGV			Data Date 04-Oct-17																			
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors	17	2018				2019							
86																						
87																						
88																						
89																						
90																						
91																						
92																						
93																						
94																						
95																						
96																						
97																						
98																						
99																						
100																						
101																						
102																						
103																						
104																						
105																						
106																						
107																						
108																						
109																						
110																						
111																						
112																						
113																						
114																						
115																						
116																						
117																						
118																						
119																						
120																						

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: T/E Meeting to discuss Design Team Spec data requirements

Date: Wed Oct 04 2017 11:18:16 EDT

Attachments:

Ha

Ha

Ha

(b)(6);(b)(7)(C)

Director, Business Operations Division
Border Patrol & Air and Marine Program Management Office
Facilities Management and Engineering
Office of Facilities and Asset Management
Mobile: (b)(6);(b)(7)(C)

-----Original Message-----

From: (b)(6);(b)(7)(C)

Sent: Wednesday, October 04, 2017 11:06 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: T/E Meeting to discuss Design Team Spec data requirements

I want everything hard role and hot peppers - (b)(6);(b)(7)(C) is referencing the "Italian Store" if you are short on cash they take CC (b)(6);(b)(7)(C) this cc means credit card)

From: (b)(6);(b)(7)(C)

Sent: Wednesday, October 04, 2017 10:47:40 AM

To: (b)(6);(b)(7)(C)

Subject: RE: T/E Meeting to discuss Design Team Spec data requirements

I'll take half a turkey please. No mayo.

(b)(6);(b)(7)(C)

Director, Business Operations Division
Border Patrol & Air and Marine Program Management Office Facilities Management and Engineering
Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

-----Original Message-----

From: (b)(6);(b)(7)(C)

Sent: Wednesday, October 04, 2017 10:46 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: T/E Meeting to discuss Design Team Spec data requirements

Ha! I wish!!

(b)(6);(b)(7)(C) PE

LMI Contractor

BPAM Chief Engineer

(b)(6);(b)(7)(C)

Sent from Samsung Galaxy

From: (b)(6);(b)(7)(C)

Sent: Wednesday, October 04, 2017 10:09:33 AM

To: (b)(6);(b)(7)(C)

Subject: RE: T/E Meeting to discuss Design Team Spec data requirements

Yes- get off the links.

Bring us Italian subs (from the spot in Arlington)

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO) Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (7)(E)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, October 03, 2017 2:05 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: T/E Meeting to discuss Design Team Spec data requirements

Sorry I was unable to participate. Any action items for me?

(b)(6);(b)(7)(C) P.E., PMP, Chief Engineer Border Patrol & Air and Marine (BPAM) PMO LMI Contractor

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

-----Original Appointment-----

From: (b)(6);(b)(7)(C)

Sent: Friday, September 29, 2017 4:09 PM

To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

Subject: T/E Meeting to discuss Design Team Spec data requirements

When: Monday, October 2, 2017 1:00 PM-2:00 PM (UTC-05:00) Eastern Time (US & Canada).

Where: via PhoneCon (or in person if possible)

All,

This meeting is being asked for by the T&E team to discuss with the PM's design specification team what data deliverables will be required after the Mockup and Prototype evaluation event in order to create design specs. This meeting, and the data required, will inform the test design strategy.

Phone: (b)(6);(b)(7)(C)

Participant code: (b)(6);(b)(7)(C)

Thanks,

(b)(6);(b)(7)(C)

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: FITT/GIS

Date: Tue Oct 03 2017 07:41:23 EDT

Attachments: FITT GIS plan forward ms.pptx

<<FITT_GIS plan forward ms.pptx>>

FITT and GIS Path Forward

October 3, 2017



Homeland
Security

~~PREDECISIONAL/FOR OFFICIAL USE ONLY~~

BW23 FOIA CBP 011321

(b) (5)



Security

~~PREDECISIONAL/FOR OFFICIAL USE ONLY~~

(b) (5)



Homeland
Security

(b) (5)



Homeland
Security

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: FITT/GIS

Date: Tue Oct 03 2017 07:41:23 EDT

Attachments: FITT_GIS plan forward ms.pptx

<<FITT_GIS plan forward ms.pptx>>

FITT and GIS Path Forward

October 3, 2017



Homeland
Security

~~PREDECISIONAL/FOR OFFICIAL USE ONLY~~

BW23 FOIA CBP 011326

(b) (5)



Security

~~PREDECISIONAL/FOR OFFICIAL USE ONLY~~

BW23 FOIA CBP 011327

Page 236 of 1286

2

(b) (5), (b) (7)(E)



Homeland
Security

(b) (5), (b) (7)(E)



Homeland
Security

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: FITT/GIS

Date: Tue Oct 03 2017 07:41:23 EDT

Attachments: FITT_GIS plan forward ms.pptx

<<FITT_GIS plan forward ms.pptx>>

FITT and GIS Path Forward

October 3, 2017



Homeland
Security

~~PREDECISIONAL/FOR OFFICIAL USE ONLY~~

BW23 FOIA CBP 011331

(b) (5)



Security

~~PREDECISIONAL/FOR OFFICIAL USE ONLY~~

BW23 FOIA CBP 011332

Page 242 of 1286

2

(b) (5)



Homeland
Security

(b) (5)



Homeland
Security

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject:

FITT/GIS

Date:

Tue Oct 03 2017 07:41:23 EDT

Attachments:

FITT_GIS plan forward ms.pptx

<<FITT_GIS plan forward ms.pptx>>

FITT and GIS Path Forward

October 3, 2017



Homeland
Security

~~PREDECISIONAL/FOR OFFICIAL USE ONLY~~

BW23 FOIA CBP 011336

(b) (5)



Security

~~PREDECISIONAL/FOR OFFICIAL USE ONLY~~

BW23 FOIA CBP 011337

Page 248 of 1286

2

(b) (5)



Homeland
Security

(b) (5)



Homeland
Security

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject:

FITT/GIS

Date:

Tue Oct 03 2017 07:41:23 EDT

Attachments:

FITT_GIS plan forward ms.pptx

<<FITT_GIS plan forward ms.pptx>>

FITT and GIS Path Forward

October 3, 2017



Homeland
Security

~~PREDECISIONAL/FOR OFFICIAL USE ONLY~~

BW23 FOIA CBP 011341

(b) (5)



Security

~~PREDECISIONAL/FOR OFFICIAL USE ONLY~~

BW23 FOIA CBP 011342

Page 254 of 1286

2

(b) (5)



Homeland
Security

FITT Path Forward (cont'd)

(b) (5)

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: FITT/GIS

Date: Tue Oct 03 2017 07:41:23 EDT

Attachments: FITT_GIS plan forward ms.pptx

<<FITT_GIS plan forward ms.pptx>>

FITT and GIS Path Forward

October 3, 2017



Homeland
Security

~~PREDECISIONAL/FOR OFFICIAL USE ONLY~~

BW23 FOIA CBP 011346

(b) (5)



Security

~~PREDECISIONAL/ FOR OFFICIAL USE ONLY~~

BW23 FOIA CBP 011347

(b) (5)



Homeland
Security

(b) (5)



Homeland
Security

From:

To:

Cc:

Bcc:

Subject: RE: FITT/GIS (130 pm EST call)

Date: Tue Oct 03 2017 06:34:27 EDT

Attachments: FITT_GIS plan forward ms.pptx

<<FITT_GIS plan forward ms.pptx>>

Deck for this call to give our convo a left and a right. (b)(6);(b)(7)(C) – Can you pls print for (b)(6);(b)(7)(C)?

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

-----Original Appointment-----

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 21, 2017 9:51 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: FITT/GIS

When: Tuesday, October 03, 2017 1:30 PM-2:00 PM (UTC-05:00) Eastern Time (US & Canada).

Where: (b)(7)(E) Phone: (b)(7)(E) Pin: (b)(7)(E)

FITT and GIS Path Forward

October 3, 2017



Homeland
Security

~~PREDECISIONAL/FOR OFFICIAL USE ONLY~~

BW23 FOIA CBP 011351

(b) (5)



Security

~~PREDECISIONAL/FOR OFFICIAL USE ONLY~~

BW23 FOIA CBP 011352

Page 267 of 1286

2

(b) (5)



Homeland
Security

(b) (5)



Homeland
Security

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: FW: DRAFT T&E Strategy Brief - Not Ready for Prime Time

Date: Mon Oct 02 2017 15:28:50 EDT

Attachments: TE Strategy Briefing Outline 20170830.docx

FYSA

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b) (6)

Sent: Monday, October 02, 2017 1:48 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

dhs.gov>; (b) (6)

Subject: RE: DRAFT T&E Strategy Brief - Not Ready for Prime Time

Here are the detailed instructions for T&E Strategy Briefing.

From: (b)(6);(b)(7)(C)

Sent: Monday, October 2, 2017 2:25 PM

To: (b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

Subject: DRAFT T&E Strategy Brief - Not Ready for Prime Time

Importance: High

All,

Attached is the slide deck we will be working through today.

v/r,

(b)(6);(b)(7)(C)

Acting Technical Director

Land Systems Operational Test Authority (LSOTA)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)


Homeland Security Systems Engineering Development Institute (HSSEDI)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)


T&E Strategy Briefing Outline

(b) (5)



T&E Strategy Briefing Outline

(b) (5)



From:

To:

Cc:

(b) (6)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b) (6)

Bcc:

Subject: W912EF-17-D-0011 - DHS CBP BPAM PMO - Weekly Status Report W/E 22Sep17

Date: Mon Oct 02 2017 14:59:39 EDT

Attachments: W912EF-17-D-0011 - Status Report 22Sep17.pdf

(b)(6); (b)(7)(C)

Attached please find the weekly status report for W/E 22Sep17.

If you have any questions about this status report, please feel free to contact myself, (b) (6)
(b) (6) (cc'd herein).

Thank you and best regards,

(b) (6)

(b) (6) P.E., C.C.P., P.M.P.
Senior Professional Engineer

PT&C

Office:


Mobile:

Fax:

(b) (6)

(b) (6)

(b) (5), (b) (6)



CONCERNS & ISSUES

- None

DELIVERABLES SUBMITTED THIS PERIOD

1. Weekly status report.
- 2.
- 3.
- 4.
- 5.

ACTION ITEMS	PERSON RESPONSIBLE	DEADLINE
1. None.		
2.		
3.		
4.		
5.		
6.		
7.		

PROJECT PERSONNEL

(b) (6), Lead Senior Cost Engineer

(b) (6) Alternate Lead Senior Cost Engineer

COMMENTS

- None

From:

(b)(6);(b)(7)(C)

To:

(b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

Bcc:
Subject: RE: Save the date: BPAM PMO/USACE Wall All-Hands
Date: Mon Oct 02 2017 12:09:02 EDT
Attachments:

Good afternoon,

All those driving or catching a ride, please send me your hotel info.

Thank you,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Wednesday, September 27, 2017 11:29 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

Subject: RE: Save the date: BPAM PMO/USACE Wall All-Hands

Good morning,

For coordination, please reply to me whether or not you will have a rental car on this trip and how many open spots you will have in your car. That way we can set up carpooling. Your arrival and departure time would also be helpful.

Thanks!

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

-----Original Appointment-----

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 14, 2017 4:04 PM

To: [REDACTED] (b)(6);(b)(7)(C)

[REDACTED] (b)(6);(b)(7)(C)

[REDACTED] (b)(6);(b)(7)(C)

[REDACTED] (b) (6)

(b) (6)

[REDACTED] (b) (6)

[REDACTED] (b)(6);(b)(7)(C)

[REDACTED] (b)(6);(b)(7)(C)

Cc: [REDACTED] (b) (6)

[REDACTED] (b) (6)

Subject: Save the date: BPAM PMO/USACE Wall All-Hands

When: Tuesday, October 10, 2017 12:00 PM-5:30 PM (UTC-08:00) Pacific Time (US & Canada).

Where: Confirmed location: San Diego Sector HQ

Purpose: Discuss roles and responsibilities, communication methods, project status, etc. Agenda to follow. We will use this meeting as a time out to make sure we are organized in the most efficient way to accomplish our mission at hand.

Since Monday 10/9 is a holiday, the meeting will start at noon pacific on 10/10 so everyone can travel in the morning. Please plan accordingly.

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: Good Morning (b)(6);(b)(7)(C) (UNCLASSIFIED)

Date: Mon Oct 02 2017 06:36:17 EDT

Attachments:

(b)(6);(b)(7)(C)

We can chat more when I get there this afternoon.

(b)(6);(b)(7)(C)

Eastern Corridors Director
Border Patrol and Air Marine Operations
Program Management Office
Facilities Management and Engineering

Mobile: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, October 02, 2017 6:33:18 AM

To: (b)(6);(b)(7)(C)

Subject: RE: Good Morning (b)(6);(b)(7)(C) (UNCLASSIFIED)

(b) (5), (b) (6)

From: (b)(6);(b)(7)(C)

Sent: Sunday, October 01, 2017 1:13:11 PM

To: (b)(6);(b)(7)(C)

Subject: RE: Good Morning (b)(6);(b)(7)(C) (UNCLASSIFIED)

Any thoughts/concerns?

(b)(6);(b)(7)(C)

BPAM Project Manager

LMI Contractor
(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Wednesday, September 27, 2017 11:33 AM
To: (b)(6);(b)(7)(C)
Subject: FW: Good Morning (b)(6);(b)(7)(C) (UNCLASSIFIED)

(b) (5) . Thoughts

From: (b) (6)
Sent: Wednesday, September 27, 2017 4:20:55 PM
To: (b)(6);(b)(7)(C)
Subject: Good Morning (b)(6);(b)(7)(C) (UNCLASSIFIED)
CLASSIFICATION: UNCLASSIFIED

(b)(6);(b)(7)(C)

Is there any possibility that I could be added to the daily distro for this reporting document originating with CBP " (b) (7)(E) DAILY REPORT". This would be helpful for (b)(7)(E) the newly established Regional Protection Working Group. Thanks

Very Respectfully

(b) (6)
Southwestern Division HQ
(b) (7)(E)
US Army Corps of Engineers
Email: (b) (6)
Email: (b) (6)
Comm.: (b) (6)
Secure: (b) (6)
Fax: (b) (6)

"This electronic transmission may contain ~~FOR OFFICIAL USE ONLY~~ (FOUO) information that must be protected under the Privacy Act of 1974. Do not release outside of DoD channels without the consent of the originator's office. If you received this message in error, please notify the sender by reply e-mail and delete all copies of message."

Use of this U.S. Government system, authorized or unauthorized, constitutes consent to monitoring of this system. Unauthorized use may subject you to criminal prosecution. Evidence of unauthorized use collected during monitoring may be used for administrative, criminal or other adverse actions.

CLASSIFICATION: UNCLASSIFIED

From:

(b)(6);(b)(7)(C)

To:

(b) (6)

Cc:

Bcc:

Subject: RE: FY18 Wall Schedules - 27 Sep 17

Date: Fri Sep 29 2017 13:35:39 EDT

Attachments:

Only (b)(6);(b)(7)(C) get the FY 18 schedules

(b)(6);(b)(7)(C)

-----Original Message-----

From: (b) (6)

Sent: Thursday, September 28, 2017 6:46 PM

To: (b)(6);(b)(7)(C)

Subject: FW: FY18 Wall Schedules - 27 Sep 17

Didn't you want us to limit this to just your (b)(6);(b)(7)(C)? You ok with (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

-----Original Message-----

From: (b) (6)

Sent: Thursday, September 28, 2017 5:42 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

Subject: FY18 Wall Schedules - 27 Sep 17

All,

Attached are the latest schedules for the FY18 Program.

Thank you,

(b) (6)

Program Specialist
CESWF-PM-PMO

W:

F: (b) (6)

From:

To:

Cc:

Bcc:

Subject: RE: Prototype Project Team Shout Out!

Date: Fri Sep 29 2017 10:29:06 EDT

Attachments:

Sweet! Great job guys

(b)(6);(b)(7)(C) P.E., PMP, Chief Engineer

Border Patrol & Air and Marine (BPAM) PMO

LMI Contractor

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, September 29, 2017 10:17 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Prototype Project Team Shout Out!

Hi (b)(6);(b)(7)(C) and (b)(6);(b)(7)(C)

I wanted to pass on the kudos that Acting (b)(6);(b)(7)(C) brought up on our daily tag-up today. Our tag-ups include USBP HQ, OPA, OCA, IPL, OCC, OFAM, & OA.

"I spent some time with (b)(6);(b)(7)(C) and (b)(6);(b)(7)(C) at the site yesterday and am tremendously impressed with the job they are doing. They have been doing a great job with organizational and logistical oversight. I enjoyed speaking with them and observing their work so much that I didn't want to go back into the office."

Happy Friday!

(b)(6); (b)(7)(C)

(b)(6);(b)(7)(C) BPAM PMO Communications

Kearns & West supporting

OFAM/FM&E/BPAM

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

From: Jose Nunez <jose.nunez@ibwc.gov>
To: Steve Smullen <steve.smullen@ibwc.gov>;

(b)(6);(b)(7)(C)
(b)(6)
Cc: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C) (b)(6)
<anna.morales@ibwc.gov>; Padinare Unnikrishna
<padinare.unnikrishna@ibwc.gov>; (b)(6)
(b)(6)

Bcc:
Subject: RE: [EXTERNAL] Re: Encroachments, Border Fence Projects
Date: Thu Sep 28 2017 14:55:16 EDT
Attachments:

Team:

We will send our Mexican counterparts (MxIBWC) a lettershortly officially notifying them of these additional encroachments and requesting that such encroachments be removed within a month or so. Please advise though if such encroachments can be removed as part of the Border Fence Project(s) if Mexico does not remove them in a timely manner. Thanks

José A. Nuñez, P.E.
Principal Engineer
IBWC, U.S. Section
Headquarters
(915) 832-4749
(915) 433-0680 Cell

>>> (b)(6) 9/27/2017 3:56 PM >>>

Everyone,

There are a number of encroachments noted east of (b)(7)(E) POE which are located in two areas - 1) Where the existing landing mat fence deviates from the International Border (b)(7)(E) mile east of the POE and 2) The residential area (b)(7)(E) mile from the east end of the existing landing mat fence. The list of the encroachments and approximate locations (Station and RFP Construction Plans sheet #) are below. The locations for area 1 are not shown on the current plans, so I have attached a map with the encroachments marked.

Area 1:
Existing building
(b)(7)(E)

Existing canopy
(b)(7)(E)

Existing retaining wall and fence
(b) (7)(E)

Area 2:
Existing walls and overhead utilities

(b) (7)(E)

Existing walls

(b) (7)(E)

If you need anything else, please let me know.

(b) (6)

(b) (6), P.G.
Project Manager
Interagency & International Services Branch
Arizona-Nevada Area Office, L.A. District
(b) (6) (O), (b) (6) (Cell)

-----Original Message-----

From: (b)(6);(b)(7)(C)
Sent: Tuesday, September 26, 2017 12:06 PM
To: Steve Smullen <Steve.Smullen@ibwc.gov>; Jose Nunez <Jose.Nunez@ibwc.gov>
Cc: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C) Anna Morales <Anna.Morales@ibwc.gov>; Padinare Unnikrishna
<Padinare.Unnikrishna@ibwc.gov>; (b) (6)
(b) (6)
Subject: Re: [EXTERNAL] Re: Encroachments, Border Fence Projects

Ok. Will confirm and supply

Sent using OWA for iPhone

From: Steve Smullen <Steve.Smullen@ibwc.gov>
Sent: Tuesday, September 26, 2017 2:28:23 PM
To: Jose Nunez; (b)(6);(b)(7)(C)
Cc: (b)(7)(E) Anna
Morales; Padinare Unnikrishna
Subject: [EXTERNAL] Re: Encroachments, Border Fence Projects

(b)(6);(b)(7)(C)

Please advise of encroachments on the east end of the fence that you know of. We have informed Mexico of the ones west of the (b)(7)(E) POE.

Thanks,
Steve

Steve Smullen
Area Operations Manager
IBWC, U.S. Section
San Diego Field Office
(619) 662 - 7601
(619) 662 - 7607 <tel:6196627607> Fax
"Excellence Through Teamwork"

>>> Jose Nunez <jose.nunez@ibwc.gov> 9/26/2017 12:21 PM >>>

CBP Team:

We sent the Mexican Section letters respectfully asking for their assistance with removing these encroachments. I am not sure how many, if any, have been removed to date. Thanks

Jose

Sent from my iPhone

> On Sep 26, 2017, at 11:03 AM, (b)(6);(b)(7)(C) wrote:
>
> I believe Steve Smullen has these already
>
> Sent using OWA for iPhone
>
> From: (b)(6);(b)(7)(C)
> Sent: Tuesday, September 26, 2017 1:59:42 PM
> To: Jose Nunez
> Cc: (b)(6);(b)(7)(C); Padinare Unnikrishna; (b)(6);(b)(7)(C)
> Subject: [EXTERNAL] RE: Encroachments, Border Fence Projects
>
> Yes-there are several locations on west and east end of the project where there appears to be Mexican structures connected to or relying on the existing fence for structural support. If you'd like I can set up a webex meeting and show you the locations we know of and are concerned about.
>
> (b)(6);(b)(7)(C) P.E., PMP, Chief Engineer
> Border Patrol & Air and Marine (BPAM) PMO
> LMI Contractor
> Mobile: (b)(6);(b)(7)(C)
> (b)(6);(b)(7)(C)
>
>
> -----Original Message-----
> From: Jose Nunez [mailto:Jose.Nunez@ibwc.gov]
> Sent: Tuesday, September 26, 2017 1:33 PM
> To: (b)(6);(b)(7)(C)
> Cc: (b)(6);(b)(7)(C); Padinare Unnikrishna
> <Padinare.Unnikrishna@ibwc.gov>
> Subject: Encroachments, Border Fence Projects
>
> (b)(6);(b)(7)(C)
>
> As you may be aware, we are working with our Mexican counterparts to remove the encroachments that CBP reported along the international boundary line in (b)(7)(E) California. Please

advise if any of these encroachments are in the way of erecting border fences in this area. Thanks

>

> Jose

>

> Sent from my iPad

>

From:
To:

(b)(6);(b)(7)(C)

Cc:
Bcc:
Subject: FW: Thanks
Date: Thu Sep 28 2017 14:01:08 EDT
Attachments:

FYSA

I don't know if (b)(6);(b)(7)(C) told you but for reasons still unknown (b)(6);(b)(7)(C) did not send us RFPs for next year's environmental compliance and NEPA support BPAs despite (b)(6);(b)(7)(C) requesting he do so. By the time we figured out we had been left off (b)(6);(b)(7)(C) bidders list, the proposal submission deadline had already past. As such, we weren't even able to submit proposals on the two BPAs we are currently the incumbent on. I'm super bummed as everything I've heard from (b)(6);(b)(7)(C) and (b)(6);(b)(7)(C) was we did a great job and I'm now having to lay-off a couple of high performers due to the loss of work. I sent the note below primarily for (b)(6);(b)(7)(C) benefit as he refused to talk to my contract specialist when she reached out him to find out why he didn't send us RFPs.

From: (b)(6);(b)(7)(C)
Sent: Thursday, September 28, 2017 1:57 PM
To: (b)(6);(b)(7)(C)
Cc: (b) (6)
Subject: [EXTERNAL] RE: Thanks

There always seems to be more work, and LMI has provided a good service/product so the chance of at least entering into the RFQ process in the future would seem positive.

Thank you,

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Thursday, September 28, 2017 1:52 PM
To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Cc: (b) (6)
Subject: Thanks

Hi (b)(6);(b)(7)(C)

Now that we are wrapping up this contract, I just wanted to send you a short note thanking you for the opportunity to support CBP BPAM this past year with your environmental compliance initiatives. We have thoroughly enjoyed working with you and your colleagues and have found the work to be both interesting and rewarding. I hope you have found our services and deliverables to be cost-effective and of high value, and sincerely hope we are afforded an opportunity to submit proposals on any future environmental compliance (and NEPA planning) BPAs/contracts you plan to award.

Best,

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, October 04, 2016 2:35 PM

To: (b) (6)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Request For Quote (b) (5)

Please see attached award for RFO (b) (5)

From: (b) (6)

Sent: Thursday, September 15, 2016 12:10 PM

To: (b)(6);(b)(7)(C)

Subject: RE: Request For Quote (b) (5)

Hi (b)(6);(b)(7)(C)

Please see attached for LMI's revised price proposal. (b) (4), (b) (5)

We assume all terms and conditions of the original 8/23/2016 proposal apply. Please do not hesitate to call or email (b)(6);(b)(7)(C) at (b)(6);(b)(7)(C) to discuss technical questions. For pricing and contractual-related questions, please contact me at (b)(6);(b)(7)(C).

Thank you,

(b) (6)

Contracts Administrator
LMI

7940 Jones Branch Drive,

Tysons, VA 22102

Office: (b) (6)

Complex Problems. Practical Solutions.
www.lmi.org

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 13, 2016 6:58 AM

To: (b) (6)

Subject: RE: Request For Quote (b) (5)

Good Morning,

(b) (5)

Thank you,

(b)(6);(b)(7)(C)

From: (b) (6)

Sent: Wednesday, September 07, 2016 8:36 AM

To: (b)(6);(b)(7)(C)

Subject: RE: Request For Quote (b) (5)

(b)(6);(b)(7)(C)

The attached .xls represents LMI's revised price proposal – (b) (5), (b) (4)

If you have any questions or require additional info, please let me know.

Thanks,

(b) (6)

(b) (6)

Contracts Manager
LMI
Office: (b) (6)

From: (b)(6);(b)(7)(C)
Sent: Tuesday, September 06, 2016 7:50 PM
To: (b) (6)
Subject: RE: Request For Quote (b) (5)

I need the pricing schedule that is on the GSA Schedule, in effect as of the closing day of the RFQ. Future/pending modifications are not applicable until they are exercised. Please resubmit current Pricing Schedule.

From: (b) (6)
Sent: Tuesday, September 06, 2016 3:34 PM
To: (b)(6);(b)(7)(C)
Subject: RE: Request For Quote (b) (5)

(b)(6);(b)(7)(C)

Attached is our GSA mod that added a few new labor categories. The same mod includes a rate

summary that covers the period of the subject quote.

Specifically, the last page of the attached mod is what you are seeking (Year 16 Rates). LMI's quoted rates for the subject effort incorporate (b) (4)

Thanks,

(b) (6)

Carlton Roxbrough

Contracts Manager

LMI

Office: (b) (6)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 06, 2016 3:01 PM

To: (b) (6)

Subject: RE: Request For Quote (b) (5)

Please forward me a copy of your GSA Schedule that has the rates you are quoting on this RFQ. A review of the LMI GSA Schedule could not confirm the hour rates you are providing.

Thanks,

(b)(6);(b)(7)(C)

From: (b) (6)

Sent: Tuesday, August 23, 2016 1:40 PM

To: (b)(6);(b)(7)(C)

Subject: RE: Request For Quote (b) (5)

(b)(6);(b)(7)(C)

Attached is LMI's proposal submitted under the subject RFQ. We appreciate the opportunity to submit this proposal. If you have any questions regarding its content, please call me at (b) (6)

Thank you,

(b) (6)

(b) (6)

Contracts Manager

LMI

Office: (b) (6)

From: (b)(6);(b)(7)(C)

Sent: Thursday, August 04, 2016 10:03 AM

To: (b) (6)

Subject: Request For Quote (b) (5)

I just for some reason didn't get one out to you folks. I will review to see if you received the others that I sent out on that same day.

Request For Quote,

PLEASE RESPOND USING THE "SUBJECT LINE" AS CURRENTLY WRITTEN AND HAVE YOUR PAST PERFORMANCE REFERENCES USE THIS SAME SUBJECT LINE WORDING, IF REFERENCE IS USING A PPQ TO APPLY TO MULTIPLE RFQ'S HAVE THEM INPUT THE RFQ NUMBERS IN THE SUBJECT LINE.

If your company will not be providing a quote, please let me know right away along with the reasons of non-submission.

Note: Contractor is now allowed to download and submit CPAR/PPIRS data for Past Performance requirement.

E-mail any questions you have to me.

Thank you,

(b)(6);(b)(7)(C)

Mission Support Procurement Branch

CBP

(b) (6)

Govt. Point of Contact:

(b) (6)

Phone: (b) (6)

E-Mail: (b) (6)

Contract Clauses/Exceptions:

[View the specifics for this contract](#)

Source

Title

00CORP

The Professional Services Schedule (PSS)

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: FW: ILSP submission for signature

Date: Thu Sep 28 2017 10:53:55 EDT

Attachments: image001.png

FYI

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 28, 2017 10:40 AM

To: (b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

Going into the system this morning...let me know anytime you want an update status.

Should move through pretty quickly.

(b)(6);(b)(7)(C) PMP

(Contractor, ManTech Team)

Senior Subject Matter Expert III

Supporting the Office of Acquisition

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Wednesday, September 27, 2017 8:43 AM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

(b)(6);(b)(7)(C) good morning!

Well....well, well we meet again via email.

Attached is the revised document incorporating the recommendation below. We've also attached the high level schedule.

Please let us know if any further action is required by the PMO.

We greatly appreciate your assistance and thank you for getting this into the system for signature.

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: **(b)(6);(b)(7)(C)**

Cell: **(b)(6);(b)(7)(C)**

(b)(6);(b)(7)(C)

[Click Here](#) to view the FMB team listed with areas of responsibility.

[Click Here](#) to view the PRR tracker.

[Click Here](#) to view the IAA Tracker

From: **(b)(6);(b)(7)(C)**

Sent: Tuesday, September 26, 2017 3:28 PM

To: **(b)(6);(b)(7)(C)**

Cc:

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

(b)(6);(b)(7)(C), I have thoroughly reviewed the attached ILSP. All comments and adjudication has been addressed in this version.

May I suggest one slight wording change (you don't have to accept it)? – Last paragraph in sub para 2 of Section B, add the words in red for clarity and for a more specific adjudication response:

(b) (5)

Please let me know if you have any questions and congratulations to you and your team for all of the hard work.

V/R

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) PMP

(Contractor, ManTech Team)

Senior Subject Matter Expert III

Supporting the Office of Acquisition

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, September 25, 2017 3:07 PM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

#youwin!

Attached corrections.

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From (b)(6);(b)(7)(C)(CTR)

Sent: Monday, September 25, 2017 12:27 PM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

Thanks, (b)(6);(b)(7)(C) I have screened this thoroughly (v10.0 09252017).

I just have two questions:

(b) (5), (b)(6); (b)(7)(C)

I probably just ended up with the wrong version from you (v10.0 09252017).

Before I can forward this on to (b)(6);(b)(7)(C) please address and let me know if you have any questions.

V/R

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) PMP

(Contractor, ManTech Team)

Senior Subject Matter Expert III

Supporting the Office of Acquisition

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, September 25, 2017 9:19 AM

To:

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

(b)(6);(b)(7)(C) good morning.

After our discussions on Friday, please view incorporated changes, signed by (b)(6);(b)(7)(C) and revised comment page.

Great teamwork everyone,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here](#) to view the FMB team listed with areas of responsibility.

[Click Here](#) to view the PRR tracker.

[Click Here](#) to view the IAA Tracker

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 19, 2017 6:26 AM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

Understood, (b)(6);(b)(7)(C). We need your documented adjudication to the DHS comments on the latest version of the comments sheet for the record please.

V/R

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) PMP

(Contractor, ManTech Team)

Senior Subject Matter Expert III

Supporting the Office of Acquisition

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, September 18, 2017 3:12 PM

To:

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

Hi (b)(6);(b)(7)(C)

This morning, we went through all the remaining comments to see if based on the intent and scope of the document we should include them. Based on a thorough review, and with (b)(6);(b)(7)(C) input, we will be pushing forward with the document as is. To close the loop and ensure our approach is sound, we are going to reach out to the POC for the comments we are not incorporating – we are targeting Thursday to have those meetings and will send a final version of the ILSP at that point.

Regards,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 12, 2017 1:05 PM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

Thank you (b)(6);(b)(7)(C) I didn't see any adjudication on the PARM comments so I imagine you are working on that as well.

Thanks,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) PMP

(Contractor, ManTech Team)

Senior Subject Matter Expert III

Supporting the Office of Acquisition

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 12, 2017 8:54 AM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

Good morning (b)(6);(b)(7)(C) and team,

Attached please find the revised signature page and accompanying documents, along with the most recent IMS (as of 9/8).

In respect to the comments on the LMS and LRFP – we are reviewing and will get back to you shortly.

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, September 08, 2017 1:45 PM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

(b)(6);(b)(7)(C) as (b)(6);(b)(7)(C) mentioned earlier today, we have received additional feedback on the draft ILSP.

DHS has reviewed and their comments have been added to the current adjudicated comments. These new comments need adjudication.

To summarize, the IMS didn't get attached as promised in the adjudication;
they present a case for an LRFP-extrapolated from known CTIMR contracts;
A request for an LMS,
and another take on the FODS/IT Technologies question.

Please take a look at the new comments (appended to the bottom) and adjudicate. When you're done, please edit the ILSP accordingly, add appendices and update the signature page – see comment nr. 6 with the recommendations if you agree.

Please let me know if you have any questions on this. I'll be right with you till we get this to signature.
And no, we don't expect any more comments in at this stage.

V/R

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) PMP

(Contractor, ManTech Team)

Senior Subject Matter Expert III

Supporting the Office of Acquisition

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Wednesday, September 6, 2017 10:06 AM

To:

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

Hey (b)(6);(b)(7)(C)

Hope all is well.

So (b)(6);(b)(7)(C) and I touched base and at this time we are not incorporating the TI piece.

Technology will be incorporated at a later date outside the (b)(7)(E) RGV miles (which is our current requirement for ADE2).

Please let us know if any further action is required from BPAM, otherwise tag you're it.

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 05, 2017 12:19 PM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: FW: ILSP submission for signature

(b)(6);(b)(7)(C)

See comments here and also attached revisions.

Please let us know if you need anything additional.

Overall: where the comments are in the form of a question and you are answering the question, suggest closing the loop on adjudication by adding the notation "No change to the document required" or some equivalent, to your response. This helps remove any potential ambiguity. Examples are comments 7, 11, 12, 18, 19 etc. updated

Going down the attached comment form in order:

(b) (5)

(b) (5)

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, September 01, 2017 3:52 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: FW: ILSP submission for signature

FYI

From: (b)(6);(b)(7)(C)

Sent: Friday, September 01, 2017 11:03:23 AM

To: (b)(6);(b)(7)(C)

Cc:

Subject: RE: ILSP submission for signature

Thanks (b)(6);(b)(7)(C) and I went over the adjudication and we would like to note just a few issues and offer some suggestions for resolution before we finalize.

Overall: where the comments are in the form of a question and you are answering the question, suggest closing the loop on adjudication by adding the notation "No change to the document required" or some equivalent, to your response. This helps remove any potential ambiguity. Examples are comments 7, 11, 12, 18, 19 etc.

Going down the attached comment form in order:

(b) (5)

(b) (5)

Please let me know if you have any questions or need any assistance at all.

V/R

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) PMP

(Contractor, ManTech Team)

Senior Subject Matter Expert III

Supporting the Office of Acquisition

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Wednesday, August 30, 2017 2:13 PM

To: (b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

(b)(6);(b)(7)(C)

Attached is the revised ILSP, accepted comments have been incorporated.

Document has been signed by our PMO.

Please assist with obtaining additional signatures.

Thank you,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 2:42 PM

To: (b)(6);(b)(7)(C)
Cc: (b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

(b)(6);(b)(7)(C)

Here are the comments on the ILSP

R

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Division Director

Acquisition Policy and Oversight (APO)

Office of Acquisition (OA)/AGO

(b)(6);(b)(7)(C) (office)

(b)(6);(b)(7)(C) (cell)

(b)(6);(b)(7)(C) (fax)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, August 03, 2017 2:35 PM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: ILSP submission for signature

(b)(6);(b)(7)(C)

Attached is the final draft of the Wall ILSP.

It has been reviewed/approved by BPAM PMO.

Please let us know if you have any questions or comments on the attached document.

We greatly appreciate your support in getting the ILSP signed.

Thank you,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: The Dream Team

Date: Thu Sep 28 2017 08:23:27 EDT

Attachments:

Thanks for sharing!

(b)(6);(b)(7)(C), P.E., PMP, Chief Engineer
Border Patrol & Air and Marine (BPAM) PMO
LMI Contractor
Mobile: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

-----Original Message-----

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 28, 2017 7:29 AM

To: (b)(6);(b)(7)(C)

Subject: FW: The Dream Team

For Imi news

From: (b)(6);(b)(7)(C)

Sent: Wednesday, September 27, 2017 7:33:57 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: The Dream Team

(b)(6);(b)(7)(C)

Eastern Corridors Director
Border Patrol and Air Marine Operations
Program Management Office
Facilities Management and Engineering

Mobile: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: incident summary

Date: Thu Sep 28 2017 08:20:54 EDT

Attachments:

I'll get on the road in about 30 minutes and will give you call.

(b)(6);(b)(7)(C)

Eastern Corridors Director
Border Patrol and Air Marine Operations
Program Management Office
Facilities Management and Engineering

Mobile: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 28, 2017 7:22:00 AM

To: (b)(6);(b)(7)(C)

Subject: RE: incident summary

Let me know when you are avail for a quick call

From: (b)(6);(b)(7)(C)

Sent: Wednesday, September 27, 2017 6:38:54 PM

To: (b)(6);(b)(7)(C)

Cc:

Subject: RE: incident summary

All in a days work.

And Caddell actually went ahead of schedule today. Not bad.

(b)(6);(b)(7)(C)

Eastern Corridors Director
Border Patrol and Air Marine Operations

Program Management Office
Facilities Management and Engineering

Mobile: (b)(6);(b)(7)(C)
Email: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Wednesday, September 27, 2017 5:54:03 PM
To: (b)(6);(b)(7)(C)
Cc: (b)(6);(b)(7)(C)
Subject: RE: incident summary

(b)(6);(b)(7)(C) thanks to you and your team on how you handled this stressful situation – Outstanding performance !

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Wednesday, September 27, 2017 4:28 PM
To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Cc: (b)(6);(b)(7)(C)
Subject: RE: incident summary

Thanks for getting this out (b)(6);(b)(7)(C)

And to compliment you and (b)(6);(b)(7)(C) working with this team making a bad situation work out well for that man. Great job!

(b)(6);(b)(7)(C)
Eastern Corridors Director
Border Patrol and Air Marine Operations
Program Management Office
Facilities Management and Engineering

Mobile: (b)(6);(b)(7)(C)
Email: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Wednesday, September 27, 2017 4:10:25 PM
To: (b)(6);(b)(7)(C)
Cc: (b)(6);(b)(7)(C)
Subject: incident summary

(b)(6);(b)(7)(C)

LMI
7940 Jones Branch Drive

Tysons, VA 22102
Cell: (b)(6);(b)(7)(C)

Complex Problems. Practical Solutions.
www.lmi.org<<http://www.lmi.org/>>

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: FW: The Dream Team

Date: Thu Sep 28 2017 07:29:13 EDT

Attachments: Image.jpg

For Imi news

From: (b)(6);(b)(7)(C)

Sent: Wednesday, September 27, 2017 7:33:57 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: The Dream Team

(b)(6);(b)(7)(C)

Eastern Corridors Director
Border Patrol and Air Marine Operations
Program Management Office
Facilities Management and Engineering

Mobile: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

(b)(6); (b)(7)(C)



From: (b) (6)
To: (b)(6);(b)(7)(C)
Steve Smullen <steve.smullen@ibwc.gov>; Jose Nunez <jose.nunez@ibwc.gov>
Cc: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C); Anna Morales <anna.morales@ibwc.gov>; Padinare Unnikrishna <padinare.unnikrishna@ibwc.gov>; (b) (6)
(b) (6)
Bcc:
Subject: RE: [EXTERNAL] Re: Encroachments, Border Fence Projects
Date: Wed Sep 27 2017 17:56:09 EDT
Attachments: Encroachment - with Aerial.pdf

Everyone,

There are a number of encroachments noted east of (b)(7)(E) POE which are located in two areas - 1) Where the existing landing mat fence deviates from the International Border ~ (b)(7)(E) mile east of the POE and 2) The residential area ~ (b)(7)(E) mile from the east end of the existing landing mat fence. The list of the encroachments and approximate locations (Station and RFP Construction Plans sheet #) are below. The locations for area 1 are not shown on the current plans, so I have attached a map with the encroachments marked.

Area 1:

Existing building

(b)(7)(E)

Existing canopy

(b)(7)(E)

Existing retaining wall and fence

(b)(7)(E)

Area 2:

Existing walls and overhead utilities

(b)(7)(E)

Existing walls

(b)(7)(E)

If you need anything else, please let me know.

(b) (6)

(b) (6)

Project Manager
Interagency & International Services Branch
Arizona-Nevada Area Office, L.A. District

(b) (6) (O), (b) (6) (Cell)

-----Original Message-----

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 26, 2017 12:06 PM

To: Steve Smullen <Steve.Smullen@ibwc.gov>; Jose Nunez <Jose.Nunez@ibwc.gov>

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C); Anna Morales <Anna.Morales@ibwc.gov>; Padinare Unnikrishna
<Padinare.Unnikrishna@ibwc.gov>; (b) (6)

Subject: Re: [EXTERNAL] Re: Encroachments, Border Fence Projects

Ok. Will confirm and supply

Sent using OWA for iPhone

From: Steve Smullen <Steve.Smullen@ibwc.gov>

Sent: Tuesday, September 26, 2017 2:28:23 PM

To: Jose Nunez; (b)(6);(b)(7)(C)

Cc: (b)(6); (b)(7)(C) Anna
Morales; Padinare Unnikrishna

Subject: [EXTERNAL] Re: Encroachments, Border Fence Projects

(b)(6);(b)(7)(C)

Please advise of encroachments on the east end of the fence that you know of. We have informed Mexico of the ones west of the (b)(6) POE.

Thanks,
Steve

Steve Smullen
Area Operations Manager
IBWC, U.S. Section
San Diego Field Office
(619) 662 - 7601
(619) 662 - 7607 <tel:6196627607> Fax
"Excellence Through Teamwork"

>>> Jose Nunez <jose.nunez@ibwc.gov> 9/26/2017 12:21 PM >>>

CBP Team:

We sent the Mexican Section letters respectfully asking for their assistance with removing these encroachments. I am not sure how many, if any, have been removed to date. Thanks

Jose

Sent from my iPhone

> On Sep 26, 2017, at 11:03 AM, (b)(6);(b)(7)(C) wrote:

>

> I believe Steve Smullen has these already

>

> Sent using OWA for iPhone

>

> From: (b)(6);(b)(7)(C)

> Sent: Tuesday, September 26, 2017 1:59:42 PM

> To: Jose Nunez

> Cc: (b)(6);(b)(7)(C); Padinare Unnikrishna; (b)(6);(b)(7)(C)

> Subject: [EXTERNAL] RE: Encroachments, Border Fence Projects

>

> Yes-there are several locations on west and east end of the project where there appears to be Mexican structures connected to or relying on the existing fence for structural support. If you'd like I can set up a webex meeting and show you the locations we know of and are concerned about.

>

> (b)(6);(b)(7)(C), P.E., PMP, Chief Engineer

> Border Patrol & Air and Marine (BPAM) PMO

> LMI Contractor

> Mobile: (b)(6);(b)(7)(C)

> (b)(6);(b)(7)(C)

>

>

> -----Original Message-----

> From: Jose Nunez [mailto:Jose.Nunez@ibwc.gov]

> Sent: Tuesday, September 26, 2017 1:33 PM

> To: (b)(6);(b)(7)(C)

> Cc: (b)(6);(b)(7)(C); Padinare Unnikrishna

<Padinare.Unnikrishna@ibwc.gov>

> Subject: Encroachments, Border Fence Projects

>

(b)(6);(b)(7)(C)

>

> As you may be aware, we are working with our Mexican counterparts to remove the encroachments that CBP reported along the international boundary line in (b)(7)(E) California. Please advise if any of these encroachments are in the way of erecting border fences in this area. Thanks

>

> Jose

>

> Sent from my iPad

>

(b) (7)(E)

From:
To:

(b)(6);(b)(7)(C)

Cc:

Bcc:
Subject: incident summary
Date: Wed Sep 27 2017 16:10:25 EDT
Attachments: Incident summary and actions following 9-27.pdf

(b)(6);(b)(7)(C)

LMI
7940 Jones Branch Drive
Tysons, VA 22102
Cell: (b)(6);(b)(7)(C)

Complex Problems. Practical Solutions.
www.lmi.org


(b)(6); (b)(7)(C); (b)(7)(E)



(b) (7)(E)



(b) (7)(E), (b)(6);(b)(7)(C)



From:

(b) (6)

To:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

Bcc:
Subject: RE: Save the date: BPAM PMO/USACE Wall All-Hands (UNCLASSIFIED)
Date: Wed Sep 27 2017 14:18:21 EDT
Attachments:

CLASSIFICATION: UNCLASSIFIED

(b) (6) and I will be coming down from LA in a GOV

-----Original Message-----

From: (b)(6);(b)(7)(C)

Sent: Wednesday, September 27, 2017 8:29 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b) (6)

(b) (6)

Subject: [EXTERNAL] RE: Save the date: BPAM PMO/USACE Wall All-Hands

Good morning,

For coordination, please reply to me whether or not you will have a rental car on this trip and how many open spots you will have in your car. That way we can set up carpooling. Your arrival and departure time would also be helpful.

Thanks!

(b)(6);(b)(7)(C)

-----Original Appointment-----

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 14, 2017 4:04 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b) (6)

(b) (6)

Subject: Save the date: BPAM PMO/USACE Wall All-Hands

When: Tuesday, October 10, 2017 12:00 PM-5:30 PM (UTC-08:00) Pacific Time (US & Canada).

Where: Confirmed location: San Diego Sector HQ

Purpose: Discuss roles and responsibilities, communication methods, project status, etc. Agenda to follow. We will use this meeting as a time out to make sure we are organized in the most efficient way to accomplish our mission at hand.

Since Monday 10/9 is a holiday, the meeting will start at noon pacific on 10/10 so everyone can travel in the morning. Please plan accordingly.

CLASSIFICATION: UNCLASSIFIED

From:

(b)(6);(b)(7)(C)

To:

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

Bcc:

Subject: RE: Save the date: BPAM PMO/USACE Wall All-Hands
Date: Wed Sep 27 2017 12:42:23 EDT
Attachments:

I will be using a GOV Van - departing from Laguna on the morning of the 10th - returning the evening of the 11th.

(b)(6);(b)(7)(C)
Chief, Financial Management Branch
Border Patrol & Air and Marine Program Management Office (BPAM PMO)
Facility Management & Engineering
Office: (b)(6);(b)(7)(C)
Mobile: (b)(6);(b)(7)(C)

[Click Here](#) to view the FMB team listed with areas of responsibility.
[Click Here](#) to view the PRR tracker.

From: (b)(6);(b)(7)(C)
Sent: Wednesday, September 27, 2017 8:29 AM
To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

Subject: RE: Save the date: BPAM PMO/USACE Wall All-Hands

Good morning,

For coordination, please reply to me whether or not you will have a rental car on this trip and how many open spots you will have in your car. That way we can set up carpooling. Your arrival and departure time would also be helpful.

Thanks!

(b)(6);(b)(7)(C)

-----Original Appointment-----

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 14, 2017 4:04 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b) (6)

(b) (6)

Subject: Save the date: BPAM PMO/USACE Wall All-Hands

When: Tuesday, October 10, 2017 12:00 PM-5:30 PM (UTC-08:00) Pacific Time (US & Canada).

Where: Confirmed location: San Diego Sector HQ

Purpose: Discuss roles and responsibilities, communication methods, project status, etc. Agenda to follow. We will use this meeting as a time out to make sure we are organized in the most efficient way to accomplish our mission at hand.

Since Monday 10/9 is a holiday, the meeting will start at noon pacific on 10/10 so everyone can travel in the morning. Please plan accordingly.

From:

(b) (6)

To:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

Bcc:
Subject: RE: Save the date: BPAM PMO/USACE Wall All-Hands
Date: Wed Sep 27 2017 11:33:52 EDT
Attachments:

The Fort Worth crew will have a large van. We are getting on a 1930 flight to Phoenix and will be traveling as a group to and from the meeting. Thanks (b) (6)

-----Original Message-----

From: (b)(6);(b)(7)(C)

Sent: Wednesday, September 27, 2017 10:29 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

Subject: [EXTERNAL] RE: Save the date: BPAM PMO/USACE Wall All-Hands

Good morning,

For coordination, please reply to me whether or not you will have a rental car on this trip and how many open spots you will have in your car. That way we can set up carpooling. Your arrival and departure time would also be helpful.

Thanks!

(b)(6);(b)(7)(C)

-----Original Appointment-----

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 14, 2017 4:04 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6)
(b) (6) (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Cc: (b)(6);(b)(7)(C) (b) (6)
(b) (6)

Subject: Save the date: BPAM PMO/USACE Wall All-Hands

When: Tuesday, October 10, 2017 12:00 PM-5:30 PM (UTC-08:00) Pacific Time (US & Canada).

Where: Confirmed location: San Diego Sector HQ

Purpose: Discuss roles and responsibilities, communication methods, project status, etc. Agenda to follow. We will use this meeting as a time out to make sure we are organized in the most efficient way to accomplish our mission at hand.

Since Monday 10/9 is a holiday, the meeting will start at noon pacific on 10/10 so everyone can travel in the morning. Please plan accordingly.

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: ILSP submission for signature

Date: Wed Sep 27 2017 08:42:31 EDT

Attachments: Border Wall System High Level Schedule_20170922.pdf
image001.png

Integrated_Logistics_Support_Plan_BPAM TI09272017BPAM.DOCX

Integrated Logistics Support Plan BPAM TI09272017BPAM.PDF

(b)(6);(b)(7)(C) good morning!

Well....well, well we meet again via email.

Attached is the revised document incorporating the recommendation below. We've also attached the high level schedule.

Please let us know if any further action is required by the PMO.

We greatly appreciate your assistance and thank you for getting this into the system for signature.

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 26, 2017 3:28 PM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

(b)(6);(b)(7)(C), I have thoroughly reviewed the attached ILSP. All comments and adjudication has been addressed in this version.

May I suggest one slight wording change (you don't have to accept it)? – Last paragraph in sub para 2 of Section B, add the words in red for clarity and for a more specific adjudication response:

(b) (5)

Please send schedule document to attach as per Section A sub para 2: "See Attachment 1: Border Wall System DRAFT High-Level Schedule."

If you wish to amend the ILSP as suggested above, please also ask the PM to sign and then send the resulting revised document with an attached schedule and I will get them both into the system for signature.

Please let me know if you have any questions and congratulations to you and your team for all of the hard work.

V/R

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) PMP

(Contractor, ManTech Team)

Senior Subject Matter Expert III

Supporting the Office of Acquisition

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, September 25, 2017 3:07 PM

To:

Cc:

(b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

#youwin!

Attached corrections.

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b)(6);(b)(7)(C)

Sent: Monday, September 25, 2017 12:27 PM

To:

(b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

Thanks, (b)(6);(b)(7)(C). I have screened this thoroughly (v10.0 09252017).

I just have two questions:

1. Section D sub para 5 – IT Resource Needs. In the Friday call (SEPT 22) your folks stated that the (b)(7)(E) and IT resource needs would be fully supported by PMOD. We understood (b)(7)(E) modify this paragraph to clearly reflect that support has been worked out with PMOD to assume the IT resource need (b)(7)(E). The copy of the ILSP you sent me shows no change and no mention of this clarification.

2. LRFP: In the Friday (SEPT 22) call, in response to the comment on meeting a minimal requirement to address LRFP, (b)(6);(b)(7)(C) gave clear guidance (b)(5)

(b) (5)

I probably just ended up with the wrong version from you (v10.0 09252017).

Before I can forward this on to (b)(6);(b)(7)(C), please address and let me know if you have any questions.

V/R

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) PMP

(Contractor, ManTech Team)

Senior Subject Matter Expert III

Supporting the Office of Acquisition

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, September 25, 2017 9:19 AM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

(b)(6);(b)(7)(C) good morning.

After our discussions on Friday, please view incorporated changes, signed by (b)(6);(b)(7)(C) and revised comment page.

Great teamwork everyone,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 19, 2017 6:26 AM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

Understood, (b)(6);(b)(7)(C) We need your documented adjudication to the DHS comments on the latest version of the comments sheet for the record please.

V/R

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) PMP

(Contractor, ManTech Team)

Senior Subject Matter Expert III

Supporting the Office of Acquisition

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, September 18, 2017 3:12 PM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

Hi (b)(6);(b)(7)(C)

This morning, we went through all the remaining comments to see if based on the intent and scope of the document we should include them. Based on a thorough review, and with (b)(6);(b)(7)(C) input, we will be pushing forward with the document as is. To close the loop and ensure our approach is sound, we are going to reach out to the POC for the comments we are not incorporating – we are targeting Thursday to have those meetings and will send a final version of the ILSP at that point.

Regards,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 12, 2017 1:05 PM

To:

Cc:

(b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

Thank you (b)(6);(b)(7)(C). I didn't see any adjudication on the PARM comments so I imagine you are working on that as well.

Thanks,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) PMP

(Contractor, ManTech Team)

Senior Subject Matter Expert III

Supporting the Office of Acquisition

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 12, 2017 8:54 AM

To:

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

Good morning (b)(6);(b)(7)(C) and team,

Attached please find the revised signature page and accompanying documents, along with the most recent IMS (as of 9/8).

In respect to the comments on the LMS and LRFP – we are reviewing and will get back to you shortly.

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, September 08, 2017 1:45 PM

To:

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

(b)(6);(b)(7)(C) as (b)(6);(b)(7)(C) mentioned earlier today, we have received additional feedback on the draft ILSP.

DHS has reviewed and their comments have been added to the current adjudicated comments. These new comments need adjudication.

To summarize, the IMS didn't get attached as promised in the adjudication;

they present a case for an LRFP-extrapolated from known CTIMR contracts;

A request for an LMS,

and another take on the (b)(7)(E) IT Technologies question.

Please take a look at the new comments (appended to the bottom) and adjudicate. When you're done, please edit the ILSP accordingly, add appendices and update the signature page – see comment nr. 6 with the recommendations if you agree.

Please let me know if you have any questions on this. I'll be right with you till we get this to signature.

And no, we don't expect any more comments in at this stage.

V/R

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) PMP

(Contractor, ManTech Team)

Senior Subject Matter Expert III

Supporting the Office of Acquisition

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Wednesday, September 6, 2017 10:06 AM

To:

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

Hey (b)(6);(b)(7)(C)

Hope all is well.

So (b)(6);(b)(7)(C) and I touched base and at this time we are not incorporating the TI piece.

Technology will be incorporated at a later date outside the (b)(7)(E) RGV miles (which is our current requirement for ADE2).

Please let us know if any further action is required from BPAM, otherwise tag you're it.

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 05, 2017 12:19 PM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: FW: ILSP submission for signature

(b)(6);(b)(7)(C)

See comments here and also attached revisions.

Please let us know if you need anything additional.

Overall: where the comments are in the form of a question and you are answering the question, suggest closing the loop on adjudication by adding the notation "No change to the document required" or some equivalent, to your response. This helps remove any potential ambiguity. Examples are comments 7, 11, 12, 18, 19 etc. updated

Going down the attached comment form in order:

(b) (5)

(b) (5), (b) (7)(E)

And...one for the calculator: Updated

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, September 01, 2017 3:52 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: FW: ILSP submission for signature

FYI

From: (b)(6);(b)(7)(C)

Sent: Friday, September 01, 2017 11:03:23 AM

To: (b)(6);(b)(7)(C)

Cc:


Subject: RE: ILSP submission for signature

Thanks (b)(6);(b)(7)(C) (b)(6);(b)(7)(C) and I went over the adjudication and we would like to note just a few issues and offer some suggestions for resolution before we finalize.

Overall: where the comments are in the form of a question and you are answering the question, suggest closing the loop on adjudication by adding the notation "No change to the document required" or some equivalent, to your response. This helps remove any potential ambiguity. Examples are comments 7, 11, 12, 18, 19 etc.

Going down the attached comment form in order:

(b) (5), (b) (7)(E)



And...one for the calculator:

- Subtotal error on the LCCE:

o In both tables 4 and 5, the total column (last column) - the 2.2 subtotal is incorrect. Strangely, this does not affect the grand totals. However, if someone independently adds the subtotals to check the grand total, they do not add up because the 2.2 subtotal is incorrect.

o Table 4 – 2.2 Subtotal is (b) (5) . If you sum all of 2.2 it should actually be (b) (5) which gets us to the correctly depicted grand total.

o Table 5 – 2.2 Subtotal is (b) (5) . If you sum all of 2.2 it should actually be (b) (5) , which gets us the correctly depicted grand total.

Please let me know if you have any questions or need any assistance at all.

V/R

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) PMP

(Contractor, ManTech Team)

Senior Subject Matter Expert III

Supporting the Office of Acquisition

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Wednesday, August 30, 2017 2:13 PM

To:

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

(b)(6);(b)(7)(C)

Attached is the revised ILSP, accepted comments have been incorporated.

Document has been signed by our PMO.

Please assist with obtaining additional signatures.

Thank you,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 2:42 PM

To:

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

(b)(6);(b)(7)(C)

Here are the comments on the ILSP

R

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Division Director

Acquisition Policy and Oversight (APO)

Office of Acquisition (OA)/AGO

(b)(6);(b)(7)(C) (office)

(b)(6);(b)(7)(C) (cell)

(b)(6);(b)(7)(C) (fax)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, August 03, 2017 2:35 PM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: ILSP submission for signature

(b)(6);(b)(7)(C)

Attached is the final draft of the Wall ILSP.

It has been reviewed/approved by BPAM PMO.

Please let us know if you have any questions or comments on the attached document.

We greatly appreciate your support in getting the ILSP signed.

Thank you,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

Border Wall System High-Level Schedule

Status as of 9/22/2017

Border Wall System High Level Schedule	FY17			FY18				FY19				FY20				FY21				FY22						
	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2					
	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F
-ADE 2A/B																										
-Documentation & ADE 2A/B (ARB) Briefing																										
-Funding																										
-Wall Prototype (San Diego)																										
-RFP/Contract Award																										
-Prototype Construction																										
-Testing/Report																										
-Update of Design Standards																										
-San Diego (SDC Secondary Wall)																										
-A/E Award / Design																										
-RFP/Contract Award																										
-Design Development (100% Design)																										
-San Diego Border Wall Construction (14 miles)																										
-Rio Grande Valley (RGV) Sector																										
-RGV (b)(7)(E) Mile Segment (Levee Wall)																										
-RGV (b)(7)(E) Project - (b)(7)(E) Miles																										
-A/E Award																										
-Design and RFP Preparation																										
-RFP Release/Proposal Preparation																										
-Evaluations/Award																										
-(b)(7)(E) Construction on Federally Owned Land (b)(7)(E) miles)																										
-Environmental Waiver																										
(b)(7)(E) Private Land Option (Real Estate)																										
Border Wall Construction on Private Land (b)(7)(E) miles)																										
-RGV (b)(7)(E) Project - (b)(7)(E) Miles (Border Wall Construction)																										
-RGV Project - (b)(7)(E) Miles (Border Wall Construction)																										
-RGV Project - (b)(7)(E) Miles (Border Wall Construction)																										
-RGV (b)(7)(E) Mile Segment (Flood Plain)																										
-RGV (b)(7)(E) Project - (b)(7)(E) Miles (Border Wall Construction)																										
-RGV Project - (b)(7)(E) Miles (Border Wall Construction)																										
-RGV Project - (b)(7)(E) Miles (Border Wall Construction)																										
-RGV Project - (b)(7)(E) Miles (Border Wall Construction)																										
-RGV Project - (b)(7)(E) Miles (Border Wall Construction)																										
-RGV Project - (b)(7)(E) Miles (Border Wall Construction)																										
-RGV Project - (b)(7)(E) Miles (Border Wall Construction)																										

Task
(on Critical Path)Task
(Not on Critical Path)Task
(Completed)Milestone
(on Critical Path)Milestone
(Not on Critical Path)Milestone
(Completed)Future RGV
Levee Wall ProjectBW23 FOIA b(7)(E) Future RGV
Flood Plain Project



Integrated Logistics Support Plan For Border Patrol Tactical Infrastructure Program

DHS Systems Engineering Life Cycle

**OFFICE OF FACILITIES AND ASSET
MANAGEMENT
BORDER PATROL AND AIR AND MARINE
PROGRAM MANAGEMENT OFFICE**

Integrated Logistics Support Plan

for

Border Patrol Tactical Infrastructure

Submitted by:

(b)(6);(b)(7)(C), Program Manager

Date

Endorsed by:

Lead Technical Authority, (IT)

Date

Endorsed by:

Lead Technical Authority, (Non-IT)

Date

Endorsed by:

Lead Business Authority, USBP
(Operating Component)

Date

Approved by:

Component Acquisition Executive
(Operating Component)

Date

Reviewed by:

Director, APMD

Date

Approved by:

Acquisition Decision Authority

Date

(b) (5)

Revision Summary (If Applicable)

Provide a bulleted high-level description of what changes have occurred and why in the current submission. Provide the date of the revisions. See format below.


DOCUMENT CHANGE HISTORY

Version Number	Date	Description


(b) (5)

(b) (5)

(b) (5), (b) (7)(E)




(b) (5), (b) (7)(E)




(b) (5)

(b) (5)


(b) (5), (b) (7)(E)



(b) (5), (b) (7)(E)



(b) (5), (b) (7)(E)



(b) (5)

(b) (5)

(b) (5)

(b) (5)

Sample Template and Guidance

Appendices

1. Acronyms

BPAM	Border Patrol and Air and Marine
CBP	U.S. Customs and Border Protection
COR	Contracting Officer's Representatives
CPFF	Cost Plus Fixed Fee
CTIMR	Comprehensive Tactical Infrastructure Maintenance and Repair
DHS	Department of Homeland Security
EO	Executive Order
FFP	Firm Fixed Price
(b)(7)(E)	
IBWC	International Boundary Water Commission
ILSP	Integrated Logistics Support Plan
LCCE	Life Cycle Cost Estimate
M&R	Maintenance and Repair
NEPA	National Environmental Policy Act
OJT	On-the-job Training
PM	Project Manager
PMO	Program Management Office
RGV	Rio Grande Valley
TI	Tactical Infrastructure
USBP	United States Border Patrol
WMS	Work Management System



Integrated Logistics Support Plan For Border Patrol Tactical Infrastructure Program

**DHS Systems Engineering
Life Cycle**

**OFFICE OF FACILITIES AND ASSET
MANAGEMENT
BORDER PATROL AND AIR AND MARINE
PROGRAM MANAGEMENT OFFICE**

Integrated Logistics Support Plan

for

Border Patrol Tactical Infrastructure

Submitted by:	(b)(6);(b)(7)(C), Program Manager	Date
Endorsed by:	Lead Technical Authority, (IT)	Date
Endorsed by:	Lead Technical Authority, (Non-IT)	Date
Endorsed by:	Lead Business Authority, USBP (Operating Component)	Date
Approved by:	Component Acquisition Executive (Operating Component)	Date
Reviewed by:	Director, APMD	Date
Approved by:	Acquisition Decision Authority	Date

(b) (5)

Revision Summary (If Applicable)

Provide a bulleted high-level description of what changes have occurred and why in the current submission. Provide the date of the revisions. See format below.


DOCUMENT CHANGE HISTORY

Version Number	Date	Description


(b) (5)

(b) (5)

(b) (5), (b) (7)(E)




(b) (5), (b) (7)(E)




(b) (5)

(b) (5)


(b) (5), (b) (7)(E)




(b) (5), (b) (7)(E)



(b) (5), (b) (7)(E)



(b) (5), (b) (7)(E)



(b) (5)

(b) (5)

(b) (5)

Appendices

1. Acronyms

BPAM	Border Patrol and Air and Marine
CBP	U.S. Customs and Border Protection
COR	Contracting Officer's Representatives
CPFF	Cost Plus Fixed Fee
CTIMR	Comprehensive Tactical Infrastructure Maintenance and Repair
DHS	Department of Homeland Security
EO	Executive Order
FFP	Firm Fixed Price
(b)(7)(E)	
IBWC	International Boundary Water Commission
ILSP	Integrated Logistics Support Plan
LCCE	Life Cycle Cost Estimate
M&R	Maintenance and Repair
NEPA	National Environmental Policy Act
OJT	On-the-job Training
PM	Project Manager
PMO	Program Management Office
RGV	Rio Grande Valley
TI	Tactical Infrastructure
USBP	United States Border Patrol
WMS	Work Management System

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: Are you on the rgv call

Date: Mon Sep 25 2017 13:38:28 EDT

Attachments:

I heard you thanks

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, September 25, 2017 1:37 PM

To: (b)(6);(b)(7)(C)

Subject: RE: Are you on the rgv call

Yes-I've been on

(b)(6);(b)(7)(C), P.E., PMP, Chief Engineer

Border Patrol & Air and Marine (BPAM) PMO

LMI Contractor

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, September 25, 2017 1:01 PM

To: (b)(6);(b)(7)(C)

Subject: Are you on the rgv call

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: Are you on the rgv call

Date: Mon Sep 25 2017 13:36:32 EDT

Attachments:

Yes-I've been on

(b)(6);(b)(7)(C), P.E., PMP, Chief Engineer

Border Patrol & Air and Marine (BPAM) PMO

LMI Contractor

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, September 25, 2017 1:01 PM

To: (b)(6);(b)(7)(C)

Subject: Are you on the rgv call

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: Border Wall IMS (as of 9/22/17)

Date: Mon Sep 25 2017 09:41:18 EDT

Attachments:

thanks

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, September 25, 2017 9:16 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: Re: Border Wall IMS (as of 9/22/17)

Done

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Monday, September 25, 2017 8:56:09 AM

To: (b)(6);(b)(7)(C)

Cc:

Subject: [EXTERNAL] FW: Border Wall IMS (as of 9/22/17)

Pls send updates to (b)(6);(b)(7)(C) on

line479, SWPPP install

Line 488 – Complete work on GSA site

Line 491 Mark ingress and egress

Line 530 – install fac

Line 549 and 554 conduct kick off

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, September 22, 2017 4:04 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Border Wall IMS (as of 9/22/17)

Hi All -

Attached is the Border Wall IMS (in .mpp and PDF) as of 9/22/17.

Unlike the last couple weeks, there are no significant changes to this version of the IMS compared to last Friday's version.

Thanks and have a great weekend!

(b)(6);(b)(7)(C)

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: FOR REVIEW - DRAFT EMAIL TO USFWS

Date: Fri Sep 22 2017 14:24:06 EDT

Attachments:

Me too

(b)(6);(b)(7)(C)

BPAM Project Manager

LMI Contractor

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, September 22, 2017 2:07 PM

To:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: FOR REVIEW - DRAFT EMAIL TO USFWS

I'm good with this.

From: (b)(6);(b)(7)(C)

Sent: Friday, September 22, 2017 2:04 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: FOR REVIEW - DRAFT EMAIL TO USFWS

No edits here – this looks good.

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, September 22, 2017 1:47 PM

To:

(b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: RE: FOR REVIEW - DRAFT EMAIL TO USFWS

Hi (b)(6);(b)(7)(C)

Sounds good. Copying (b)(6);(b)(7)(C) for visibility and/or comment.

(b)(6); (b)(7)(C) – Do you have any revisions to the below?

Thanks,

(b)(6); (b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, September 22, 2017 1:26 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: FOR REVIEW - DRAFT EMAIL TO USFWS

(b)(6);(b)(7)(C) – Thank you for drafting this. It looks great and hits the main issues that were brought up by (b)(6) during our meeting last week. I have few edits (in red). (b)(5)

If everyone is good with these changes I can send the email to (b)(6) and in advance of their meeting this weekend.

(b) (5)

From: (b)(6);(b)(7)(C)

Sent: Friday, September 22, 2017 9:00 AM

To:

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: FOR REVIEW - DRAFT EMAIL TO USFWS

Importance: High

Hi (b)(6);(b)(7)(C) and (b)(6);(b)(7)(C) –

Below is a draft email for USFWS/ (b) (6) to clarify the items that he indicated weren't clear to him. Please review for accuracy, specifically the language in red regarding environmental mitigation funding for FY18 requirements. (b) (5)

(b)(6);(b)(7)(C) – Please let us know if you're good with the content. Our understanding is that Chief Padilla and C2 are meeting with the USFWS Regional Director on Saturday at the Refuge. If we can get this email out to USFWS today, that would be ideal. We should also consider sending this to RGV Sector Wall Team to make sure Chief Padilla has visibility in case it comes up.

Thanks,

(b)(6); (b)(7)(C)

DRAFT EMAIL TO (b) (6) USFWS:

(b) (6)

Per our discussion, we want to clarify a few points regarding the border wall project at the Santa Ana Refuge. I hope this helps clarify the status of the border/levee wall system project, specifically on the Refuge. It is our understanding that CBP's Deputy Commissioner and USBP Chief Padilla are meeting with USFWS at the Refuge this weekend. Please let us know if you have any questions or need to discuss further.

Thank you,

(b)(6);(b)(7)(C)

(b) (5)

(b)(6);(b)(7)(C) BPAM PMO Communications

Kearns & West supporting

OFAM/FM&E/BPAM

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: ILSP submission for signature

Date: Fri Sep 22 2017 13:16:58 EDT

Attachments: image002.png
image003.png

(b)(6);(b)(7)(C) confirmed LRFP is not required (just need to make sure WBS/Cost Estimate is included), so once we plug in the cable verbiage

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here](#) to view the FMB team listed with areas of responsibility.

[Click Here](#) to view the PRR tracker.

[Click Here](#) to view the IAA Tracker

From: (b)(6);(b)(7)(C)
Sent: Friday, September 22, 2017 12:33 PM
To: (b)(6);(b)(7)(C)
Subject: RE: ILSP submission for signature

Hey there- so we talked to (b)(6);(b)(7)(C) and (b)(6);(b)(7)(C) on the comments yesterday am.

So (b)(6);(b)(7)(C) agreed we could clarify -

-Need to get language on "cable" and plug into the ILMS, reference comment 26

(b)(6);(b)(7)(C) said she would provide us a sample of LRFP, (b)(6);(b)(7)(C) agreed we would review/consider once we receive, reference comment 23.

Everything else agreed is good to go

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b)(6);(b)(7)(C)
Sent: Friday, September 22, 2017 11:29 AM
To: (b)(6);(b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: ILSP submission for signature

(b)(6);(b)(7)(C)

– How are we on this? Catching up from yesterday.

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Wednesday, September 20, 2017 8:56 AM

To: (b)(6); (b)(7)(C)

Subject: RE: ILSP submission for signature

Reminding you (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 19, 2017 8:28 AM

To: (b)(6);(b)(7)(C)

Cc:

Subject: RE: ILSP submission for signature

YESSSSSS

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 19, 2017 7:42 AM

To: (b)(6);(b)(7)(C)

Cc:

Subject: RE: ILSP submission for signature

Good morning- so we should provide the highlight madness?

Just kidding.

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 19, 2017 7:09 AM

To: (b)(6);(b)(7)(C)

Cc:

Subject: FW: ILSP submission for signature

(b)(6);(b)(7)(C) – FYA please.

(b)(6);(b)(7)(C) – Make sure I send this back over to (b)(6);(b)(7)(C) by the end of the week.

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 19, 2017 6:26 AM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

Understood, (b)(6);(b)(7)(C) We need your documented adjudication to the DHS comments on the latest version of the comments sheet for the record please.

V/R

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C), PMP

(Contractor, ManTech Team)

Senior Subject Matter Expert III

Supporting the Office of Acquisition

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, September 18, 2017 3:12 PM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

Hi (b)(6);(b)(7)(C)

This morning, we went through all the remaining comments to see if based on the intent and scope of the document we should include them. Based on a thorough review, and with (b)(6);(b)(7)(C) input, we will be pushing forward with the document as is. To close the loop and ensure our approach is sound, we are going to reach out to the POC for the comments we are not incorporating – we are targeting Thursday to have those meetings and will send a final version of the ILSP at that point.

Regards,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 12, 2017 1:05 PM

To:

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

Thank you (b)(6);(b)(7)(C). I didn't see any adjudication on the PARM comments so I imagine you are working on that as well.

Thanks,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) PMP

(Contractor, ManTech Team)

Senior Subject Matter Expert III

Supporting the Office of Acquisition

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 12, 2017 8:54 AM

To:

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

Good morning (b)(6);(b)(7)(C) and team,

Attached please find the revised signature page and accompanying documents, along with the most recent IMS (as of 9/8).

In respect to the comments on the LMS and LRFP – we are reviewing and will get back to you shortly.

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, September 08, 2017 1:45 PM

To:

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

(b)(6);(b)(7)(C), as (b)(6);(b)(7)(C) mentioned earlier today, we have received additional feedback on the draft ILSP. DHS has reviewed and their comments have been added to the current adjudicated comments. These new comments need adjudication.

To summarize, the IMS didn't get attached as promised in the adjudication;

they present a case for an LRFP-extrapolated from known CTIMR contracts;

A request for an LMS,

and another take on the (b)(7)(E) IT Technologies question.

Please take a look at the new comments (appended to the bottom) and adjudicate. When you're done, please edit the ILSP accordingly, add appendices and update the signature page – see comment nr. 6 with the recommendations if you agree.

Please let me know if you have any questions on this. I'll be right with you till we get this to signature.

And no, we don't expect any more comments in at this stage.

V/R

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) PMP

(Contractor, ManTech Team)

Senior Subject Matter Expert III

Supporting the Office of Acquisition

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Wednesday, September 6, 2017 10:06 AM

To:

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

Hey (b)(6);(b)(7)(C)

Hope all is well.

So (b)(6);(b)(7)(C) and I touched base and at this time we are not incorporating the TI piece.

Technology will be incorporated at a later date outside the (b)(7)(E) RGV miles (which is our current requirement for ADE2).

Please let us know if any further action is required from BPAM, otherwise tag you're it.

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 05, 2017 12:19 PM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: FW: ILSP submission for signature

(b)(6);(b)(7)(C)

See comments here and also attached revisions.

Please let us know if you need anything additional.

Overall: where the comments are in the form of a question and you are answering the question, suggest closing the loop on adjudication by adding the notation "No change to the document required" or some equivalent, to your response. This helps remove any potential ambiguity. Examples are comments 7, 11, 12, 18, 19 etc. updated

Going down the attached comment form in order:

(b) (5)

(b) (5), (b) (7)(E)

And...one for the calculator: Updated

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, September 01, 2017 3:52 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: FW: ILSP submission for signature

FYI

From: (b)(6);(b)(7)(C)

Sent: Friday, September 01, 2017 11:03:23 AM

To: (b)(6);(b)(7)(C)

Cc:

Subject: RE: ILSP submission for signature

Thanks (b)(6);(b)(7)(C) (b)(6);(b)(7)(C) and I went over the adjudication and we would like to note just a few issues and offer some suggestions for resolution before we finalize.

Overall: where the comments are in the form of a question and you are answering the question, suggest closing the loop on adjudication by adding the notation "No change to the document required" or some equivalent, to your response. This helps remove any potential ambiguity. Examples are comments 7, 11, 12, 18, 19 etc.

Going down the attached comment form in order:

(b) (5), (b) (7)(E)

And...one for the calculator:

- Subtotal error on the LCCE:

o In both tables 4 and 5, the total column (last column) - the 2.2 subtotal is incorrect. Strangely, this does not affect the grand totals. However, if someone independently adds the subtotals to check the grand total, they do not add up because the 2.2 subtotal is incorrect.

o Table 4 – 2.2 Subtotal is (b) (5). If you sum all of 2.2 it should actually be (b) (5), which gets us to the correctly depicted grand total.

o Table 5 – 2.2 Subtotal is (b) (5). If you sum all of 2.2 it should actually be (b) (5) which gets us the correctly depicted grand total.

Please let me know if you have any questions or need any assistance at all.

V/R

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) PMP

(Contractor, ManTech Team)

Senior Subject Matter Expert III

Supporting the Office of Acquisition

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Wednesday, August 30, 2017 2:13 PM

To: (b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

(b)(6);(b)(7)(C)

Attached is the revised ILSP, accepted comments have been incorporated.

Document has been signed by our PMO.

Please assist with obtaining additional signatures.

Thank you,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 2:42 PM

To: (b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

Subject: RE: ILSP submission for signature

(b)(6);(b)(7)(C)

Here are the comments on the ILSP

R

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Division Director

Acquisition Policy and Oversight (APO)

Office of Acquisition (OA)/AGO

(b)(6);(b)(7)(C) (office)

(b)(6);(b)(7)(C) (cell)

(b)(6);(b)(7)(C) fax)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, August 03, 2017 2:35 PM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: ILSP submission for signature

(b)(6);(b)(7)(C)

Attached is the final draft of the Wall ILSP.

It has been reviewed/approved by BPAM PMO.

Please let us know if you have any questions or comments on the attached document.

We greatly appreciate your support in getting the ILSP signed.

Thank you,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From:

(b) (6)

To:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

W: (b) (6)
F: (b) (6)

CBP SWBBS ELC Replacement Fence			Data Date 20-Sep-17																			
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors													
1	466484	CBP SWBBS ELC Replacement Fence	02-Jun-17	08-Aug-18	02-Jun-17 A	08-Aug-18	222d															
2	466484.01000	Project Management	12-Jun-17	08-Aug-18	12-Jun-17 A	08-Aug-18	222d															
3	PLAN1020	Process PRD	12-Jun-17	28-Jul-17	12-Jun-17 A	27-Jul-17 A	0d		PM1000, PM1010, PM1020,													
4	PM1000	Project Management - SPL	12-Jun-17	08-Aug-18	12-Jun-17 A	08-Aug-18	222d	PLAN1020	PCO1000													
5	PM1010	Project Management - SWF	12-Jun-17	08-Aug-18	12-Jun-17 A	08-Aug-18	222d	PLAN1020	PCO1000													
6	PM1020	USACE Structures Coordination with IBWC	12-Jun-17	07-Nov-17	12-Jun-17 A	07-Nov-17	34d	PLAN1020	AP1020													
7	PM1030	Start PMP	12-Jun-17		12-Jun-17 A		0d		PM1040													
8	PM1040	Draft PMP	12-Jun-17	01-Aug-17	12-Jun-17 A	26-Sep-17	5d	PM1030	PM1050													
9	PLAN1030	PRD Complete		28-Jul-17		27-Jul-17 A	0d	PLAN1020														
10	PM1050	Process PMP for Approval	02-Aug-17	14-Aug-17	27-Sep-17	10-Oct-17	9d	PM1040	PM1060													
11	PM1060	Approve PMP		14-Aug-17		10-Oct-17	0d	PM1050														
12	PCO1000	Fiscal Closeout		08-Aug-18		08-Aug-18	0d	CON1110, PM1000, PM10														
13	466484.95000	Environmental	12-Jun-17	27-Jan-18	12-Jun-17 A	27-Jan-18	87d															
14	ENV1010	ESPs - Task Order Award	12-Jun-17	11-Aug-17	12-Jun-17 A	22-Aug-17 A	0d		ENV1015													
15	ENV1023	Obtain CATEX Required for Geotech	21-Jun-17	03-Jul-17	21-Jun-17 A	03-Jul-17 A	0d		ENV1025													
16	ENV1025	CATEX Required for Geotech		03-Jul-17		03-Jul-17 A	0d	ENV1023	AE-C1420													
17	ENV1000	Waiver (DOJ, Secretary signature)	01-Aug-17	31-Aug-17	15-Aug-17 A	05-Sep-17 A	0d		ENV1005													
18	ENV1015	ESPs - Task Order Award Milestone		11-Aug-17		22-Aug-17 A	0d	ENV1010	ENV1017													
19	ENV1005	Waiver Complete		31-Aug-17		05-Sep-17 A	0d	ENV1000	ENV1017													
20	ENV1017	ESP Scope Development	01-Sep-17	29-Sep-17	06-Sep-17 A	29-Sep-17	8d	ENV1005, ENV1015	ENV1019													
21	ENV1019	ESP Contract Award Milestone		29-Sep-17		29-Sep-17	0d	ENV1017	ENV1020													
22	(b) (5)																					
23																						
24																						
25	466484.90000	Real Estate	19-Jul-17	17-Jan-18	19-Jul-17 A	20-Feb-18	103d															
26	RE1000	Real Estate Support - SPK	19-Jul-17	17-Jan-18	19-Jul-17 A	20-Feb-18	103d	RE1005	RE1170													
27	RE1002	Real Estate - Land Acq - SPK	19-Jul-17	02-Oct-17	19-Jul-17 A	02-Oct-17	9d															
28	RE1003	Real Estate Title Services - SPK	19-Jul-17	02-Oct-17	19-Jul-17 A	02-Oct-17	9d															
29	RE1005	Obtain BOR SUP - Far West Access	19-Jul-17	19-Sep-17	19-Jul-17 A	05-Sep-17 A	0d		RE1180, RE1000													
30	RE1095	Prepare Temporary Lease	19-Jul-17	07-Aug-17	19-Jul-17 A	07-Aug-17 A	0d	AE-C1510	RE1100													
31	RE1140	Valuation	19-Jul-17	18-Aug-17	19-Jul-17 A	07-Aug-17 A	0d		RE1170													
32	RE1100	Obtain Temporary Lease	08-Aug-17	12-Sep-17	08-Aug-17 A	16-Oct-17	18d	RE1095	RE1130, RE1120, RE1160, I													
33	RE1120	Title Work	08-Aug-17	21-Aug-17	08-Aug-17 A	21-Aug-17 A	0d	RE1100														
34	RE1130	Legal Description	08-Aug-17	12-Sep-17	08-Aug-17 A	16-Oct-17	18d	RE1100	RE1160													
35	RE1180	Real Estate Certified (Base - No Govt Staging & One Govt Access)		19-Sep-17		05-Sep-17 A	0d	RE1100, RE1005	CON1005													
36	RE1160	Possession through Condemnation (One access)	13-Sep-17	17-Jan-18	17-Oct-17	20-Feb-18	85d	RE1130, RE1100	RE1170													
37	RE1170	Real Estate Certified (Option - Govt Staging & Add'l Access)		17-Jan-18		20-Feb-18	0d	RE1160, RE1140, RE1000														
38	466484.40000	Design & Procurement	02-Jun-17	07-Nov-17	02-Jun-17 A	07-Nov-17	34d															
39	PROC1000	Design & Procurement Support - SPL	26-Jul-17	07-Nov-17	15-Jun-17 A	07-Nov-17	34d	AE-C1330	AP1020													
40	PROC1010	Design & Procurement Support - ERDC	26-Jul-17	07-Nov-17	15-Jun-17 A	07-Nov-17	34d	AE-C1330	AP1020													
41	PROC1020	Design & Procurement Support - SWF	26-Jul-17	07-Nov-17	15-Jun-17 A	07-Nov-17	34d	AE-C1330	AP1020													
42	466484.40000.01	A/E Solicitation & Award	02-Jun-17	07-Nov-17	02-Jun-17 A	07-Nov-17	34d															
43	AE-S1020	ROE-S Required		02-Jun-17		02-Jun-17 A	0d															

CBP SWBBS ELC Replacement Fence			Data Date 20-Sep-17																			
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors													
44	AE-S1035	Funds Receipt		12-Jun-17		12-Jun-17 A	0d		AE-S1060	(b) (5)												
45	AE-S1050	Award A/E Base		14-Jun-17		14-Jun-17 A	0d		AE-S1060, AE-S1065													
46	AE-S1060	Award A/E Option		14-Jun-17		14-Jun-17 A	0d	AE-S1035, AE-S1050														
47	AE-S1065	AE Task Order - W9126G17F0015	14-Jun-17	07-Nov-17	14-Jun-17 A	07-Nov-17	49d	AE-S1050	AP1020													
48	466484.40000.02	Design	15-Jun-17	25-Aug-17	15-Jun-17 A	25-Aug-17 A	0d															
49	AE-C1140	RFP Review - SPL	15-Jun-17	05-Jul-17	15-Jun-17 A	05-Jul-17 A	0d			(b) (5)												
50	AE-C1330	Draft RFP Prep	15-Jun-17	25-Jul-17	15-Jun-17 A	25-Jul-17 A	0d		AE-C1830, PROC1000, PRI													
51	AE-C1450	30% Design (DBB Features)	15-Jun-17	25-Jul-17	15-Jun-17 A	25-Jul-17 A	0d		AE-C1830													
52	AE-C1430	Topographic Survey	19-Jun-17	28-Jun-17	19-Jun-17 A	28-Jun-17 A	0d		AE-C1350, AE-C1470													
53	AE-C1410	Kickoff Meeting	26-Jun-17	26-Jun-17	26-Jun-17 A	26-Jun-17 A	0d		AE-C1510													
54	AE-C1420	Geotechnical Survey	06-Jul-17	07-Jul-17	06-Jul-17 A	07-Jul-17 A	0d	ENV1025	AE-C1350, AE-C1470	(b) (5)												
55	AE-C1510	Scoping Charrette	11-Jul-17	11-Jul-17	11-Jul-17 A	11-Jul-17 A	0d	AE-C1410	RE1095													
56	AE-C1830	Draft RFP/30% Design Submittal		25-Jul-17		25-Jul-17 A	0d	AE-C1330, AE-C1450	AE-C1340, AE-C1460													
57	AE-C1340	Draft Submittal Review	26-Jul-17	28-Jul-17	26-Jul-17 A	28-Jul-17 A	0d	AE-C1830	AE-C1350, AE-C1470													
58	AE-C1460	30% Design (DBB Features) Review	26-Jul-17	28-Jul-17	26-Jul-17 A	28-Jul-17 A	0d	AE-C1830	AE-C1675, AE-C1350, AE-C													
59	AE-C1675	Draft RFP/30% Design Review Conference	31-Jul-17	31-Jul-17	31-Jul-17 A	31-Jul-17 A	0d	AE-C1460	AE-C1350, AE-C1470, AE-C	(b) (5)												
60	AE-C1350	Final RFP Prep	01-Aug-17	12-Aug-17	01-Aug-17 A	12-Aug-17 A	0d	AE-C1420, AE-C1430, AE	AE-C1400, AE-C1475													
61	AE-C1470	90% Design (DBB Features)	01-Aug-17	12-Aug-17	01-Aug-17 A	12-Aug-17 A	0d	AE-C1420, AE-C1430, AE	AE-C1475													
62	AE-C1678	Onsite Field Review	08-Aug-17	08-Aug-17	08-Aug-17 A	08-Aug-17 A	0d	AE-C1675														
63	AE-C1400	Decision Point on Buy American Act		12-Aug-17		12-Aug-17 A	0d	AE-C1350	AE-C1390	(b) (5)												
64	AE-C1475	Final RFP/90% Design Submittal		12-Aug-17		12-Aug-17 A	0d	AE-C1350, AE-C1470	AE-C1485, AE-C1480													
65	AE-C1480	90% Design (DBB Features) Review	14-Aug-17	16-Aug-17	14-Aug-17 A	16-Aug-17 A	0d	AE-C1475	AE-C1490, AE-C1692													
66	AE-C1485	Final Submittal Review	14-Aug-17	16-Aug-17	14-Aug-17 A	16-Aug-17 A	0d	AE-C1475	AE-C1370													
67	AE-C1370	Corrected Final RFP Prep	17-Aug-17	21-Aug-17	17-Aug-17 A	21-Aug-17 A	0d	AE-C1485	AE-C1850	(b) (5)												
68	AE-C1490	100% Design (DBB Features)	17-Aug-17	21-Aug-17	17-Aug-17 A	21-Aug-17 A	0d	AE-C1480	AE-C1850													
69	AE-C1692	Final RFP/90% Design Review Conference	17-Aug-17	17-Aug-17	17-Aug-17 A	17-Aug-17 A	0d	AE-C1480														
70	AE-C1850	Corrected Final RFP/100% Design Submittal		21-Aug-17		21-Aug-17 A	0d	AE-C1370, AE-C1490	AE-C1380, AE-C1500													
71	AE-C1380	Corrected Final RFP Review	22-Aug-17	22-Aug-17	22-Aug-17 A	22-Aug-17 A	0d	AE-C1850	AE-C1740	(b) (5)												
72	AE-C1500	100% Design (DBB Features) Review	22-Aug-17	22-Aug-17	22-Aug-17 A	22-Aug-17 A	0d	AE-C1850	AE-C1740													
73	AE-C1740	OC Review	23-Aug-17	25-Aug-17	23-Aug-17 A	25-Aug-17 A	0d	AE-C1380, AE-C1500	AE-C1390, AE-C1059													
74	AE-C1059	IBWC Letter of Concurrence for Drainage Designs (DBB Features)		24-Aug-17		24-Aug-17 A	0d	AE-C1740														
75	AE-C1390	RTA		25-Aug-17		25-Aug-17 A	0d	AE-C1400, AE-C1740	DB-S1000	(b) (5)												
76	466484.40000.03	Construction Procurement: SB MATOC	28-Aug-17	07-Nov-17	28-Aug-17 A	07-Nov-17	34d															
77	466484.40000.03.01	DB Solicitation & SSEB	28-Aug-17	17-Oct-17	28-Aug-17 A	17-Oct-17	19d															
78	DB-S1000	Solicitation Reviews	28-Aug-17	30-Aug-17	28-Aug-17 A	30-Aug-17 A	0d	AE-C1390	DB-S1015													
79	DB-S1015	Advertise	31-Aug-17		31-Aug-17 A		0d	DB-S1000	DB-S1020	(b) (5)												
80	DB-S1020	Advertisement Period	31-Aug-17	29-Sep-17	31-Aug-17 A	02-Oct-17	13d	DB-S1015	DB-S1025, DB-S1060													
81	DB-S1060	Pre-Bid Site Visit	08-Sep-17	08-Sep-17	08-Sep-17 A	08-Sep-17 A	0d	DB-S1020														
82	DB-S1025	Receipt of Proposals		29-Sep-17		02-Oct-17	0d	DB-S1020	DB-S1030													
83											(b) (5)											
84																						
85																						
86																						
87																						

CBP SWBBS ELC Replacement Fence			Data Date 20-Sep-17																		
#	Activity ID	Activity Name	Baseline Start	Baseline Finish	Start	Finish	Remaining Duration	Predecessors	Successors												
88										J	A	S									
89																					
90																					
91																					
92																					
93																					
94																					
95																					
96																					
97																					
98																					
99																					
100																					
101																					
102																					
103																					
104																					
105																					
106																					
107																					
108																					

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: Phoenix meeting

Date: Thu Sep 21 2017 14:10:29 EDT

Attachments:

Copy

(b)(6);(b)(7)(C) P.E., PMP, Chief Engineer

Border Patrol & Air and Marine (BPAM) PMO

LMI Contractor

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 21, 2017 1:36 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Phoenix meeting

Sorry, (b)(6);(b)(7)(C) had us watching this video. <https://www.usatoday.com/border-wall/>

(b)(6);(b)(7)(C) said you don't need to go to Phoenix.

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 21, 2017 1:24 PM

To: (b)(6);(b)(7)(C)

Cc:

Subject: Phoenix meeting

(b)(6);(b)(7)(C). I'm going to book my travel for the San Diego all hands on the 10th and wanted to know if you wanted me to participate in the Phoenix meeting(s) as well. Please advise.

(b)(6);(b)(7)(C) -no need to call me. This is what I was going to ask you.

Best,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) P.E., PMP, Chief Engineer

Border Patrol & Air and Marine (BPAM) PMO

LMI Contractor

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: RGV Wall Weekly Meeting Minutes

Date: Thu Sep 21 2017 13:56:11 EDT

Attachments:

Agreed. (b)(6);(b)(7)(C) told me he feels his 65% number should hold true... I'll believe it when I see it.

(b)(6);(b)(7)(C) P.E. LEED AP BD+C

Program Manager

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 21, 2017 1:55 PM

To: (b)(6);(b)(7)(C)

Subject: RE: RGV Wall Weekly Meeting Minutes

Lets hope the 95% doesn't move + 25%

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 21, 2017 1:50 PM

To: (b)(6);(b)(7)(C)

Subject: RE: RGV Wall Weekly Meeting Minutes

The 15% estimate was (b) (5)

65% was (b) (7)(E)

Delta: (b) (7)(E) that is mostly because the scope wasn't really defines well at 15%

(b)(6);(b)(7)(C) P.E. LEED AP BD+C

Program Manager

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Thursday, September 21, 2017 1:47 PM
To: (b)(6);(b)(7)(C)
Subject: RE: RGV Wall Weekly Meeting Minutes

What was the change the 35% vs 65% est - thx

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Thursday, September 21, 2017 1:16 PM
To: (b)(6);(b)(7)(C)
Subject: RE: RGV Wall Weekly Meeting Minutes

I'm sorry thought you requested the 95%, which we do not have. We do have the 65% estimate (b) (5)
(b) (5) please see attached.

(b)(6);(b)(7)(C) P.E. LEED AP BD+C
Program Manager
Border Patrol & Air and Marine Program Management Office (BPAM PMO)
Facilities Management & Engineering
Mobile: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

<< File: RGV (b) (7)(E) - Cost Estimate 65 Percent.pdf >>

From: (b)(6);(b)(7)(C)
Sent: Thursday, September 21, 2017 12:50 PM
To: (b)(6);(b)(7)(C)
Subject: RE: RGV Wall Weekly Meeting Minutes

Thanks - do we have a 65% cost est yet?

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Thursday, September 21, 2017 9:00 AM
To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RGV Wall Weekly Meeting Minutes

Please find the attached meeting minutes for your use. Please send any modifications by COB Friday 22 Sept 2017.

v/r,

(b)(6);(b)(7)(C) P.E. LEED AP BD+C

Program Manager

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

<< File: RGV Wall Meeting Minutes 25AUG2017.docx >>

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: RGV Wall Weekly Meeting Minutes

Date: Thu Sep 21 2017 13:15:54 EDT

Attachments: RGV (b)(7)(E) - Cost Estimate 65 Percent.pdf

I'm sorry thought you requested the 95%, which we do not have. We do have the 65% estimate (b)(5) (b)(5) please see attached.

(b)(6);(b)(7)(C), P.E. LEED AP BD+C

Program Manager

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

<<RGV (b)(7)(E) - Cost Estimate 65 Percent.pdf>>

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 21, 2017 12:50 PM

To: (b)(6);(b)(7)(C)

Subject: RE: RGV Wall Weekly Meeting Minutes

Thanks – do we have a 65% cost est yet?

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 21, 2017 9:00 AM

To:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6)

(b)(6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RGV Wall Weekly Meeting Minutes

Please find the attached meeting minutes for your use. Please send any modifications by COB Friday 22 Sept 2017.

v/r,

(b)(6);(b)(7)(C) P.E. LEED AP BD+C

Program Manager

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

<< File: RGV Wall Meeting Minutes 25AUG2017.docx >>

Print Date Wed 23 August 2017
Eff. Date 7/27/2017

Project RGV (b) (6) RGV (b) (6) - FLOODWALL CONSTRUCTION PROJECT - 65% Design

Time 00:54:16
Title Page

Estimated by Michael Baker Intl.
Designed by Michael Baker Intl.
Prepared by (b) (6) Revisions by (b) (6)
Preparation Date 7/27/2017
Effective Date of Pricing 7/27/2017
Estimated Construction Time 180 Days

This report is not copyrighted, but the information contained herein is For ~~Official Use Only~~.

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject:

RE: Safety Plan

Date:

Thu Sep 21 2017 12:42:34 EDT

Attachments:

(b) (5)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 21, 2017 11:05 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: FW: Safety Plan

Before I push back really hard, I wanted to make sure you agree with me on this.

(b) (5)

Thoughts?

(b)(6);(b)(7)(C)

BPAM Project Manager

LMI Contractor

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 21, 2017 11:00 AM

To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C); (b)(6)

Cc: (b)(6);(b)(7)(C)

Subject: RE: Safety Plan

Recommend talking to the HQ Safety... (b)(7)(E)

. I will reach out to see who may be available within the SD Sector. Recommend talking to and/or emailing (b)(6);(b)(7)(C) who is our PMO POC to the T&E IPT. He knows what is currently being planned for safety and security... Probably should request he update us at next meeting.

(b)(6);(b)(7)(C)

(b)(6); (b)(7)(C) is with the Test and Evaluation Branch (TEB) who has the lead for developing the test plan for the mockups and prototypes. A standard part of the test plan is a safety plan which she is developing, any help or information you could provide her would be greatly appreciated. Also could you address current safety and security plans in SD in support of the test at the next IPT meeting?

r/

(b)(6);(b)(7)(C)

MITRE/LSOTA

(b)(6);(b)(7)(C)(O)

(b)(6);(b)(7)(C)(M)

From: (b)(6);(b)(7)(C)

Sent: Wednesday, September 20, 2017 12:40 PM

To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C); (b)(6)

(b)(6)
Subject: Safety Plan

Good Afternoon,

I'm working on putting information together to generate a safety plan. Is there a possibility that we can get in contact with anyone in the USBP Station that is supporting the test event and it's on change with safety (Safety Officer)?

I have been asking around here and it seems like there is not a safety officer in the building. There are a lot of OSHA and legal matters in this case that we would have to cover in the plan.

Thanks,

Regards,

(b)(6);(b)(7)(C)

Test and Evaluation Engineer

System Engineering Division

CBP

Contractor

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: Safety Plan

Date: Thu Sep 21 2017 11:19:12 EDT

Attachments:

Ok, my only thought after I sent this is that (b) (5)
I reached out to (b)(6);(b)(7)(C) for a POC but don't believe Sector should have to be involved in developing this.

(b)(6);(b)(7)(C)

BPAM Project Manager

LMI Contractor

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 21, 2017 11:17 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Safety Plan

I see it that the TE group needs to develop their own safety plan based off of their planned activities.

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 21, 2017 11:05:01 AM

To: (b)(6);(b)(7)(C)

Subject: FW: Safety Plan

Before I push back really hard, I wanted to make sure you agree with me on this.

(b) (5)

Thoughts?

(b)(6);(b)(7)(C)

BPAM Project Manager

LMI Contractor

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 21, 2017 11:00 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C); (b) (6)

(b) (6)

Cc: (b)(6);(b)(7)(C)

Subject: RE: Safety Plan

Recommend talking to the HQ Safety.. (b)(7)(E)

. I will reach out to see who may be available within the SD Sector. Recommend talking to and/or emailing (b)(6);(b)(7)(C) who is our PMO POC to the T&E IPT. He knows what is currently being planned for safety and security... Probably should request he update us at next meeting.

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) is with the Test and Evaluation Branch (TEB) who has the lead for developing the test plan for the mockups and prototypes. A standard part of the test plan is a safety plan which she is developing, any help or information you could provide her would be greatly appreciated. Also could you address current safety and security plans in SD in support of the test at the next IPT meeting?

r/

(b)(6);(b)(7)(C)

MITRE/LSOTA

(b)(6);(b)(7)(C) (O)

(b)(6);(b)(7)(C) (M)

From: (b)(6);(b)(7)(C)

Sent: Wednesday, September 20, 2017 12:40 PM

To: (b)(6);(b)(7)(C)

gov>; (b) (6)

(b) (6)

Subject: Safety Plan

Good Afternoon,

I'm working on putting information together to generate a safety plan. Is there a possibility that we can get in contact with anyone in the USBP Station that is supporting the test event and it's on change with safety (Safety Officer)?

I have been asking around here and it seems like there is not a safety officer in the building. There are a lot of OSHA and legal matters in this case that we would have to cover in the plan.

Thanks,

Regards,

(b)(6);(b)(7)(C)

Test and Evaluation Engineer

System Engineering Division

CBP

Contractor

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: (b)(7)(E) at Prototype Site - Request

Date: Thu Sep 21 2017 10:50:14 EDT

Attachments:

copy

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 21, 2017 10:32 AM

To: (b)(6);(b)(7)(C)

Subject: RE: (b)(7)(E) at Prototype Site - Request

Just did. Actually thought it was about a different question when i scanned it yesterday

From: (b)(6);(b)(7)(C)

Sent: Thursday, September 21, 2017 3:02:09 PM

To: (b)(6);(b)(7)(C)

Subject: FW: (b)(7)(E) at Prototype Site - Request

Did see your answer – which I am sure is no

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Wednesday, September 20, 2017 3:09 PM

To: (b)(6);(b)(7)(C)
Cc: (b)(6);(b)(7)(C)
Subject: RE: (b)(7)(E) at Prototype Site - Request

(b)(6);(b)(7)(C)

(b) (5), (b) (7)(E)
It would be more cost-effective and efficient if this were the case.

R,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Portfolio Manager

Mobile and Agent Centric Systems

Headquarters, United States Border Patrol

Office: (b)(6);(b)(7)(C) Mobile: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Tuesday, September 19, 2017 2:13 PM
To: (b)(6);(b)(7)(C) (b)(6);(b)(7)(C)
Subject: RE: (b)(7)(E) at Prototype Site - Request

(b)(6);(b)(7)(C) relayed to (b)(6);(b)(7)(C) that after the testing is complete, (b) (5), (b) (7)(E)
Believe that given the current timing, that should be done around
end of December this year

(b)(6);(b)(7)(C)

BPAM Project Manager

LMI Contractor

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Tuesday, September 19, 2017 2:09 PM
To: (b)(6);(b)(7)(C)
Subject: FW: (b)(7)(E) at Prototype Site - Request

Good afternoon (b)(6);(b)(7)(C)

I just wanted to follow up on (b)(6);(b)(7)(C) email below related to installing (b)(7)(E) at the Wall Prototype site.
Please advise....

Thanks,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Portfolio Manager

Mobile and Agent Centric Systems

Headquarters, United States Border Patrol

Office: (b)(6);(b)(7)(C) | Mobile: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Friday, September 15, 2017 8:05 AM
To: (b)(6);(b)(7)(C)
Subject: FW: (b)(7)(E) at Prototype Site - Request

FYSA

(b)(6);(b)(7)(C), PMP

Program Manager, Cross Border Tunnel Threat &

Linear Ground Detection System

Headquarters, United States Border Patrol

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, September 15, 2017 8:05 AM

To: (b)(6);(b)(7)(C)

Subject: (b)(7)(E) at Prototype Site - Request

(b)(6);(b)(7)(C)

(b) (5), (b) (7)(E)

I am headed out on AL and back on Oct. 1 but let me know and I'll be checking email today.

Thanks for the consideration,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) PMP

Program Manager, Cross Border Tunnel Threat &

Linear Ground Detection System

Headquarters, United States Border Patrol

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: (b)(7)(E) at Prototype Site - Request

Date: Thu Sep 21 2017 10:31:44 EDT

Attachments:

(b)(6);(b)(7)(C) no. We have 6 companies each building a 30' long prototype (2 are doing 2). No way to add this within their scopes nor coordinate across them for the work.

Thanks

From: (b)(6);(b)(7)(C)

Sent: Wednesday, September 20, 2017 8:08:59 PM

To: (b)(6);(b)(7)(C)

Cc:

Subject: RE: (b)(7)(E) at Prototype Site - Request

(b)(6);(b)(7)(C)

(b)(5), (b)(7)(E)

It would be more cost-effective and efficient if this were the case.

R,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Portfolio Manager

Mobile and Agent Centric Systems

Headquarters, United States Border Patrol

Office: (b)(6);(b)(7)(C) | Mobile: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Tuesday, September 19, 2017 2:13 PM
To: (b)(6);(b)(7)(C)
Subject: RE: (b)(7)(E) at Prototype Site - Request

(b)(6);(b)(7)(C) relayed to (b)(6);(b)(7)(C) that after the testing is complete, (b)(5), (b)(7)(E) believes that given the current timing, that should be done around end of December this year

(b)(6);(b)(7)(C)

BPAM Project Manager

LMI Contractor

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Tuesday, September 19, 2017 2:09 PM
To: (b)(6);(b)(7)(C)
Subject: FW: (b)(7)(E) at Prototype Site - Request

Good afternoon (b)(6);(b)(7)(C)

I just wanted to follow up on (b)(6);(b)(7)(C) email below related to installing (b)(7)(E) at the Wall Prototype site.
Please advise....

Thanks,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Portfolio Manager

Mobile and Agent Centric Systems

Headquarters, United States Border Patrol

Office: (b)(6);(b)(7)(C) | Mobile: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Friday, September 15, 2017 8:05 AM
To: (b)(6);(b)(7)(C)
Subject: FW: (b)(7)(E) at Prototype Site - Request

FYSA

(b)(6);(b)(7)(C) PMP

Program Manager, Cross Border Tunnel Threat &

Linear Ground Detection System

Headquarters, United States Border Patrol

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Friday, September 15, 2017 8:05 AM
To: (b)(6);(b)(7)(C)
Subject: (b)(7)(E) at Prototype Site - Request

(b)(6);(b)(7)(C)

(b) (5)

(b) (5), (b) (7)(E)

I am headed out on AL and back on Oct. 1 but let me know and I'll be checking email today.

Thanks for the consideration,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) PMP

Program Manager, Cross Border Tunnel Threat &

Linear Ground Detection System

Headquarters, United States Border Patrol

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From:

(b)(6);(b)(7)(C)

To:

<padinare.unnikrishna@ibwc.gov>

Cc:

Jose Nunez <jose.nunez@ibwc.gov>;

(b)(6);(b)(7)(C)

Bcc:

Subject: RE: DHS Projects in Lower Rio Grande Valley

Date: Wed Sep 20 2017 21:41:09 EDT

Attachments: MR (b)(7)(E) RGV FY18 v3.pdf

Unni-here you go.

Thanks,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C), P.E., PMP, Chief Engineer

Border Patrol & Air and Marine (BPAM) PMO

LMI Contractor

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: Padinare Unnikrishna [mailto:Padinare.Unnikrishna@ibwc.gov]

Sent: Wednesday, September 20, 2017 5:13 PM

To: (b)(6);(b)(7)(C)

Cc: Jose Nunez <Jose.Nunez@ibwc.gov>

Subject: DHS Projects in Lower Rio Grande Valley

(b)(6);(b)(7)(C)

This is a follow up to our phone conversation this Monday Sep 18th. Please send us the draft alignments for the fence segments in the (b)(7)(E) mile (b)(7)(E)

Thanks

Unni

RGV Proposed Barrier

Page 1 of 14

(b) (5), (b) (7)(E)

LEGEND

Approximate Flood Plain Limit



FY 18 Proposed Barrier

**If sheet measures less than 11x17" it is a reduced print
Reduce scale accordingly*

1 in = 0.5 mi

1:31,680

(b)(7)(E)

Michael Baker
INTERNATIONAL

WARNING: This document is designated **FOR OFFICIAL USE ONLY (FOUO)** and contains information that is **LAW ENFORCEMENT SENSITIVE**. It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). This document is to be controlled, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information, and is not to be released to the public or personnel who do not have a valid "need-to-know" without prior approval from Department of Homeland Security (DHS) / Customs and Border Protection (CBP).

RGV Proposed Barrier

Page 2 of 14

(b) (5), (b) (7)(E)

LEGEND

Approximate Flood Plain Limit



FY 18 Proposed Barrier

**If sheet measures less than 11x17" it is a reduced print
Reduce scale accordingly*

1 in = 0.5 mi

1:31,680

(b)(7)(E)

Michael Baker
INTERNATIONAL

WARNING: This document is designated **FOR OFFICIAL USE ONLY (FOUO)** and contains information that is **LAW ENFORCEMENT SENSITIVE**. It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). This document is to be controlled, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information, and is not to be released to the public or personnel who do not have a valid "need-to-know" without prior approval from: Department of Homeland Security (DHS) / Customs and Border Protection (CBP).

RGV Proposed Barrier

Page 3 of 14

(b) (5), (b) (7)(E)

LEGEND

Approximate Flood Plain Limit



FY 18 Proposed Barrier

**If sheet measures less than 11x17" it is a reduced print
Reduce scale accordingly.*

1 in = 0.5 mi

1:31,680

(b)(7)(E)

Michael Baker
INTERNATIONAL

WARNING: This document is designated **FOR OFFICIAL USE ONLY (FOUO)** and contains information that is **LAW ENFORCEMENT SENSITIVE**. It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). This document is to be controlled, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information, and is not to be released to the public or personnel who do not have a valid "need-to-know" without prior approval from Department of Homeland Security (DHS) / Customs and Border Protection (CBP).

RGV Proposed Barrier

Page 4 of 14

LEGEND

Approximate Flood Plain Limit



FY 18 Proposed Barrier

(b) (5), (b) (7)(E)

**If sheet measures less than 11x17" it is a reduced print
Reduce scale accordingly*

1 in = 0.5 mi

1:31,680

(b)(7)(E)

Michael Baker
INTERNATIONAL

WARNING: This document is designated **FOR OFFICIAL USE ONLY (FOUO)** and contains information that is **LAW ENFORCEMENT SENSITIVE**. It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). This document is to be controlled, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information, and is not to be released to the public or personnel who do not have a valid "need-to-know" without prior approval from Department of Homeland Security (DHS) / Customs and Border Protection (CBP).

RGV Proposed Barrier

Page 5 of 14

(b) (5), (b) (7)(E)

LEGEND

Approximate Flood Plain Limit



FY 18 Proposed Barrier

**If sheet measures less than 11x17" it is a reduced print
Reduce scale accordingly*

1 in = 0.5 mi

1:31,680

(b)(7)(E)

Michael Baker
INTERNATIONAL

WARNING: This document is designated **FOR OFFICIAL USE ONLY (FOUO)** and contains information that is **LAW ENFORCEMENT SENSITIVE**. It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). This document is to be controlled, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information, and is not to be released to the public or personnel who do not have a valid "need-to-know" without prior approval from Department of Homeland Security (DHS) / Customs and Border Protection (CBP).


RGV Proposed Barrier

Page 6 of 14

(b) (5), (b) (7)(E)

LEGEND

Approximate Flood Plain Limit

 FY 18 Proposed Barrier

**If sheet measures less than 11x17" it is a reduced print
Reduce scale accordingly.*

1 in = 0.5 mi

1:31,680

(b)(7)(E)

Michael Baker
INTERNATIONAL

WARNING: This document is designated **FOR OFFICIAL USE ONLY (FOUO)** and contains information that is **LAW ENFORCEMENT SENSITIVE**. It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). This document is to be controlled, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information, and is not to be released to the public or personnel who do not have a valid "need-to-know" without prior approval from: Department of Homeland Security (DHS) / Customs and Border Protection (CBP).


RGV Proposed Barrier

Page 7 of 14

(b) (5), (b) (7)(E)

LEGEND

Approximate Flood Plain Limit

 FY 18 Proposed Barrier

**If sheet measures less than 11x17" it is a reduced print
Reduce scale accordingly*

1 in = 0.5 mi

1:31,680

(b)(7)(E)

Michael Baker
INTERNATIONAL

WARNING: This document is designated **FOR OFFICIAL USE ONLY (FOUO)** and contains information that is **LAW ENFORCEMENT SENSITIVE**. It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). This document is to be controlled, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information, and is not to be released to the public or personnel who do not have a valid "need-to-know" without prior approval from Department of Homeland Security (DHS) / Customs and Border Protection (CBP).


RGV Proposed Barrier

Page 8 of 14

(b) (5), (b) (7)(E)

LEGEND

Approximate Flood Plain Limit

 FY 18 Proposed Barrier

**If sheet measures less than 11x17" it is a reduced print
Reduce scale accordingly*

1 in = 0.5 mi

1:31,680

(b)(7)(E)

Michael Baker
INTERNATIONAL

WARNING: This document is designated **FOR OFFICIAL USE ONLY (FOUO)** and contains information that is **LAW ENFORCEMENT SENSITIVE**. It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). This document is to be controlled, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information, and is not to be released to the public or personnel who do not have a valid "need-to-know" without prior approval from Department of Homeland Security (DHS) / Customs and Border Protection (CBP).

RGV Proposed Barrier

Page 9 of 14

(b) (5), (b) (7)(E)

LEGEND

- IBWC Levee
- Approximate Flood Plain Limit
- FY 18 Proposed Barrier
- Existing Pedestrian Fence
- Existing Pedestrian Fence

**If sheet measures less than 11x17" it is a reduced print
Reduce scale accordingly*

1 in = 0.5 mi

1:31,680

(b)(7)(E)

Michael Baker
INTERNATIONAL

WARNING: This document is designated **FOR OFFICIAL USE ONLY (FOUO)** and contains information that is **LAW ENFORCEMENT SENSITIVE**. It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). This document is to be controlled, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information, and is not to be released to the public or personnel who do not have a valid "need-to-know" without prior approval from Department of Homeland Security (DHS) / Customs and Border Protection (CBP).

RGV Proposed Barrier

Page 10 of 14

(b) (5), (b) (7)(E)

LEGEND

- IBWC Levee
- Approximate Flood Plain Limit
- FY 18 Proposed Barrier
- Existing Pedestrian Fence
- Existing Pedestrian Fence

**If sheet measures less than 11x17" it is a reduced print
Reduce scale accordingly.*

1 in = 0.5 mi

1:31,680

(b)(7)(E)

Michael Baker
INTERNATIONAL

WARNING: This document is designated **FOR OFFICIAL USE ONLY (FOUO)** and contains information that is **LAW ENFORCEMENT SENSITIVE**. It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). This document is to be controlled, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information, and is not to be released to the public or personnel who do not have a valid "need-to-know" without prior approval from Department of Homeland Security (DHS) / Customs and Border Protection (CBP).

RGV Proposed Barrier

Page 11 of 14

(b) (5), (b) (7)(E)

LEGEND

- IBWC Levee
- Approximate Flood Plain Limit
- FY 18 Proposed Barrier
- Existing Pedestrian Fence
- Existing Pedestrian Fence

**If sheet measures less than 11x17" it is a reduced print
Reduce scale accordingly*

1 in = 0.5 mi

1:31,680

(b)(7)(E)

Michael Baker
INTERNATIONAL

WARNING: This document is designated **FOR OFFICIAL USE ONLY (FOUO)** and contains information that is **LAW ENFORCEMENT SENSITIVE**. It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). This document is to be controlled, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information, and is not to be released to the public or personnel who do not have a valid "need-to-know" without prior approval from Department of Homeland Security (DHS) / Customs and Border Protection (CBP).

RGV Proposed Barrier

Page 12 of 14

(b) (5), (b) (7)(E)

LEGEND

- IBWC Levee
- Approximate Flood Plain Limit
- FY 18 Proposed Barrier
- Existing Pedestrian Fence
- Existing Pedestrian Fence

**If sheet measures less than 11x17" it is a reduced print.
Reduce scale accordingly.*

1 in = 0.5 mi

1:31,680

(b)(7)(E)

Michael Baker
INTERNATIONAL

WARNING: This document is designated **FOR OFFICIAL USE ONLY (FOUO)** and contains information that is **LAW ENFORCEMENT SENSITIVE**. It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). This document is to be controlled, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information, and is not to be released to the public or personnel who do not have a valid "need-to-know" without prior approval from Department of Homeland Security (DHS) / Customs and Border Protection (CBP).

RGV Proposed Barrier

Page 13 of 14

(b) (5), (b) (7)(E)

LEGEND

- IBWC Levee
- Approximate Flood Plain Limit
- FY 18 Proposed Barrier
- Existing Pedestrian Fence
- Existing Pedestrian Fence

**If sheet measures less than 11x17" it is a reduced print
Reduce scale accordingly.*

1 in = 0.5 mi

1:31,680

(b)(7)(E)

Michael Baker
INTERNATIONAL

WARNING: This document is designated **FOR OFFICIAL USE ONLY (FOUO)** and contains information that is **LAW ENFORCEMENT SENSITIVE**. It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). This document is to be controlled, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information, and is not to be released to the public or personnel who do not have a valid "need-to-know" without prior approval from Department of Homeland Security (DHS) / Customs and Border Protection (CBP).

RGV Proposed Barrier

Page 14 of 14

(b) (5), (b) (7)(E)

LEGEND

- IBWC Levee
- Approximate Flood Plain Limit
- FY 18 Proposed Barrier
- Existing Pedestrian Fence
- Existing Pedestrian Fence

**If sheet measures less than 11x17" it is a reduced print
Reduce scale accordingly*

1 in = 0.5 mi

1:31,680

(b)(7)(E)

Michael Baker
INTERNATIONAL

WARNING: This document is designated **FOR OFFICIAL USE ONLY (FOUO)** and contains information that is **LAW ENFORCEMENT SENSITIVE**. It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). This document is to be controlled, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information, and is not to be released to the public or personnel who do not have a valid "need-to-know" without prior approval from Department of Homeland Security (DHS) / Customs and Border Protection (CBP).

From:

(b) (6)

To:

(b)(6);(b)(7)(C)

Cc:

Bcc:

Subject:

RE: Updated Risk Register / Draft ORD for Border Wall Program

Date:

Wed Sep 20 2017 13:13:17 EDT

Attachments:

Excellent, thanks!

From: (b)(6);(b)(7)(C)

Sent: Wednesday, September 20, 2017 1:08 PM

To: (b) (6)

Cc: (b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Updated Risk Register / Draft ORD for Border Wall Program

Hey there (b)(6)

We've attached the ORD/SELC both under internal review, to include the risk register for RGV (b)(7)(E) only.

<< File: Impedance_denial_ORD_v7.5.docx >> << File: RGV- (b)(7)(E) PRD_Risk Register 07-13-17.xls >>
<< File: DHS SELC_Project_Tailoring_Plan_Border Wall System (002).doc >>

Also included the

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)
Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b)(6)

Sent: Wednesday, September 20, 2017 11:31 AM

To: (b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C); (b)(6)

(b)(6)

(b)(6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Updated Risk Register / Draft ORD for Border Wall Program

(b)(6);(b)(7)(C)

Following up on the original batch of documents provided in support of the Technical Assessment.

With the understanding that the ORD and SELC Tailoring Plan may not yet be finalized, do you have a draft copies you could provide in support of the TA?

I am also looking for an updated risk register. A register dated May 31, 2017 was included with the Risk Management Plan. We'd like to see any updates and the associated mitigation plans for risks

currently being managed.

Thanks for your help.

(b) (6)

(b) (6)

Systems Engineer/Support Contractor
DHS S&T Capability Development Support Group
Office of Systems Engineering

(b) (6)

Office: (b) (6)

Mobile: (b) (6)

From: (b)(6);(b)(7)(C)

Sent: Thursday, August 24, 2017 10:42 AM

To: (b)(6);(b)(7)(C)

(b) (6)

(b) (6)

Cc: (b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b)(6);(b)(7)(C)

Subject: RE: Systems Engineering

All- << File: Impedence_and_Denial_MNS_20170317_Approved.pdf >> << File:
CBP_Wall_CDP_USMSigned.pdf >> << File: Integrated_Logistics_Support_Plan_BPAM.PDF >> <<
File: Border Barrier System Risk Management Plan Signed.pdf >> << File: Boder Barrier PgMP 071117
Signed.pdf >>

Highlighted below is what we have attached;

- Acquisition Program Artifacts
- Mission Needs Statement (MNS)- attached
- Capability Development Plan (CDP)- attached
- Concept of Operations (CONOPS)- currently in signature cycle
- Operational Requirements Document (ORD)- currently in development
- Analysis of Alternatives (AoA)/Alternatives Analysis (AA) - currently in development
- Other trade studies or analysis performed
- Systems Engineering Life Cycle (SELC) Tailoring Plan for ADE 2B - currently in development
- Life Cycle Cost Estimate (LCCE)- pending ICE finalization
- Integrated Logistics Support Plan (ILSP)- attached and in signature cycle

- Program Management Artifacts
- Risk Register- attached

- High Level Architecture- do not have this document
- Interface descriptions- do not have this document
- Technology Capability Development Roadmap- do not have this document
- Draft Security Plan-do not have this document
- Draft Program Management Plan- attached

Thanks,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)
Facilities Management & Engineering

Office: **(b)(6);(b)(7)(C)**

Cell: **(b)(6);(b)(7)(C)**

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From **(b)(6);(b)(7)(C)**

Sent: Thursday, August 24, 2017 9:49 AM

To: **(b)(6)**

(b)(6)

Cc: **(b)(6);(b)(7)(C)**

(b)(6)

(b)(6)

(b)(6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6)

(b)(6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Systems Engineering

Please forward the list of required documents discussed during today's call and we will provide the most recent version for your use. Your POC for this action will be **(b)(6);(b)(7)(C)**

Respectfully,

(b)(6);(b)(7)(C) P.E. LEED AP BD+C

Program Manager

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Mobile: **(b)(6);(b)(7)(C)**

(b)(6);(b)(7)(C)

-----Original Appointment-----

From: (b)(6);(b)(7)(C)

Sent: Tuesday, August 22, 2017 3:12 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) (b)(6)

(b)(6) (b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Systems Engineering

When: Thursday, August 24, 2017 9:00 AM-9:30 AM (UTC-05:00) Eastern Time (US & Canada).

Where: (b)(7)(E) Phone: (b)(6);(b)(7)(C) Pin: (b)(7)(E)

This is a priority meeting that (b)(6);(b)(7)(C) would like to occur before he is out of the office on Friday. Please let me know if you cannot attend.

<< File: CBP-The Wall Technical Assessment Overview Brief - DRAFT.PPTX >>

1331 Pennsylvania Ave NW
Suite 755N
Washington DC 20004

Entrance is on F street, between 13th and 14th street next to Dress Barn. Proceed in the building to the back elevators, take them to the 7th Floor, and please call (b)(6);(b)(7)(C) at (b)(6);(b)(7)(C) to gain access to the suite.

From:

(b)(6);(b)(7)(C)

To:

(b) (6)

Cc:

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Bcc:

Subject: RE: Updated Risk Register / Draft ORD for Border Wall Program

Date: Wed Sep 20 2017 13:07:41 EDT

Attachments: DHS SELC_Project_Tailoring_Plan_Border Wall System (002).doc

Impedance_denial_ORD_v7.5.docx

RGV-^{(b) (7)(E)} PRD Risk Register 07-13-17.xls

Hey there (b) (6)

We've attached the ORD/SELC both under internal review, to include the risk register for RGV-^{(b) (7)(E)} only.

Also included the

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)
Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b) (6)

Sent: Wednesday, September 20, 2017 11:31 AM

To: (b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Updated Risk Register / Draft ORD for Border Wall Program

(b)(6);(b)(7)(C)

Following up on the original batch of documents provided in support of the Technical Assessment.

With the understanding that the ORD and SELC Tailoring Plan may not yet be finalized, do you have a draft copies you could provide in support of the TA?

I am also looking for an updated risk register. A register dated May 31, 2017 was included with the Risk Management Plan. We'd like to see any updates and the associated mitigation plans for risks currently being managed.

Thanks for your help.

(b) (6)

(b) (6)

Systems Engineer/Support Contractor
DHS S&T Capability Development Support Group
Office of Systems Engineering

(b) (6)

Office: (b) (6)

Mobile: (b) (6)

From: (b)(6);(b)(7)(C)

Sent: Thursday, August 24, 2017 10:42 AM

To: (b)(6);(b)(7)(C)

(b)(6)

Cc: (b)(6);(b)(7)(C)

(b)(6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

: Midden, Henry (CTR) <henry.midden@associates.hq.dhs.gov>;

(b)(6);(b)(7)(C)

Subject: RE: Systems Engineering

All- << File: Impedence_and_Denial_MNS_20170317_Approved.pdf >> << File: CBP_Wall_CDP_USMSigned.pdf >> << File: Integrated_Logistics_Support_Plan_BPAM.PDF >> << File: Border Barrier System Risk Management Plan Signed.pdf >> << File: Boder Barrier PgMP 071117 Signed.pdf >>

Highlighted below is what we have attached;

- Acquisition Program Artifacts
- Mission Needs Statement (MNS)- attached
- Capability Development Plan (CDP)- attached
- Concept of Operations (CONOPS)- currently in signature cycle
- Operational Requirements Document (ORD)- currently in development
- Analysis of Alternatives (AoA)/Alternatives Analysis (AA) - currently in development
- Other trade studies or analysis performed
- Systems Engineering Life Cycle (SELC) Tailoring Plan for ADE 2B - currently in development
- Life Cycle Cost Estimate (LCCE)- pending ICE finalization
- Integrated Logistics Support Plan (ILSP)- attached and in signature cycle
- Program Management Artifacts
- Risk Register- attached
- High Level Architecture- do not have this document
- Interface descriptions- do not have this document
- Technology Capability Development Roadmap- do not have this document
- Draft Security Plan-do not have this document
- Draft Program Management Plan- attached

Thanks,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)
Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Click Here to view the FMB team listed with areas of responsibility.
Click Here to view the PRR tracker.
Click Here to view the IAA Tracker

From: (b)(6);(b)(7)(C)

Sent: Thursday, August 24, 2017 9:49 AM

To: (b)(6)

(b)(6)

Cc: (b)(6);(b)(7)(C)

(b)(6)

(b)(6)

(b)(6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6)

(b)(6)
(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Systems Engineering

Please forward the list of required documents discussed during today's call and we will provide the most recent version for your use. Your POC for this action will be (b)(6);(b)(7)(C)

Respectfully,

(b)(6);(b)(7)(C) P.E. LEED AP BD+C

Program Manager

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

-----Original Appointment-----

From: (b)(6);(b)(7)(C)

Sent: Tuesday, August 22, 2017 3:12 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6)

(b)(6)

Subject: Systems Engineering

When: Thursday, August 24, 2017 9:00 AM-9:30 AM (UTC-05:00) Eastern Time (US & Canada).

Where: (b)(7)(E) Phone: (b)(6);(b)(7)(C) Pin: (b)(7)(E)

This is a priority meeting that (b)(6);(b)(7)(C) would like to occur before he is out of the office on Friday. Please let me know if you cannot attend.

<< File: CBP-The Wall Technical Assessment Overview Brief - DRAFT.PPTX >>

1331 Pennsylvania Ave NW
Suite 755N
Washington DC 20004

Entrance is on F street, between 13th and 14th street next to Dress Barn. Proceed in the building to the back elevators, take them to the 7th Floor, and please call (b)(6);(b)(7)(C) to gain access to the suite.



DEPARTMENT OF HOMELAND SECURITY

**SYSTEMS ENGINEERING LIFE CYCLE
(SELC)**

**Border Wall System Program
(BWS P)**

~~For Official Use Only (FOFU)~~

Doc No:

20 September 2017

Developed By:

Border Patrol Air & Marine Program Management Office (BPAM),
Facilities Management & Engineering (FM&E)
1331 Pennsylvania Ave NW
Washington DC 20002

UNCLASSIFIED//~~FOUO~~

BW23 FOIA CBP 011578

(b) (5)

(b) (5)

SELC Tailoring Plan Template

Signature Page

Border Wall System Program

Submitted By:

(b)(6);(b)(7)(C)
Program Manager, Acquisition Program
Manager

Date

Endorsed By:

Chief Scott Luck
Lead Business Authority

Date

Approved By:

(b)(6); (b)(7)(C)
Lead Technical Authority (Non- IT)

Date


Approved By:

Mark S. Borkowski
Component Acquisition Executive

Date

(b) (5)

(b) (5), (b) (7)(E)



(b) (5), (b)(6); (b)(7)(C)



SELC Tailoring Plan

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)



Department of Homeland Security

Preliminary Operational Requirements Document for Impedance and Denial (I&D)

September 15, 2017

United States Border Patrol Strategic Planning and Analysis Directorate (SPAD), Operational Requirements Management Division (ORMD)

This document was prepared for authorized distribution only.

WARNING: This document is FOR OFFICIAL USE ONLY (FOUO). It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). It is to be controlled, stored, handled, transmitted, distributed, and disposed of in accordance with Department of Homeland Security (DHS) policy relating to FOUO information and is not to be released to the public or other personnel who do not have a valid "need to know" without prior approval of an authorized DHS official.

Page 985 of 1286

(b) (5)

(b) (5)

Revision Summary

Table 1: Revision Summary

Version #	Date	Section	Paragraph	Description

DRAFT

(b) (5)


(b) (5)

(b) (5)


(b) (5)

(b) (5)


(b) (5), (b) (7)(E)




(b) (5), (b) (7)(E)




(b) (5), (b) (7)(E)



(b) (5), (b) (7)(E)




(b) (5), (b) (7)(E)




(b) (5)

(b) (5), (b) (7)(E)




(b) (5), (b) (7)(E)



(b) (5)


(b) (5), (b) (7)(E)



(b) (5)

(b) (5)

(b) (5), (b) (7)(E)



(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

Program	Tactical Infrastructure
FM&E # & Project Title	RGV
Date	Thursday, Jul 13, 2017
Project Manager	(b) (5), (b) (6): (b) (7)(C)
Project Base Cost Est.	
PBC + Est. Impact	

Border Patrol Facilities and Tactical Infrastructure

Facilities Management & Engineering

Risk Register

FM&E

Building for a Secure America

RISK MANAGEMENT SUMMARY RESULTS (planned)

3 Point Impact Estimate		
Low	Medium	High
\$	(b) (5)	

Total Expected Impact - Dollars \$ (b) (5), (b) (7)(E)

Total Expected Impact - Days

Impact to Critical Path - Total Days

ID #	Month/Year	Risk May Affect Critical Path	Milestone Affected	Risk Category	Detailed Description of Risk (Specific, Measurable, Attainable, Relevant, Timebound)	Mitigation of Risk	Estimated Impact - Days	Probability (%)	\$ Impact	Estimated Impact (\$)	Risk Level
1	(b) (5), (b) (7)(E)										
2											
3											
4											
5											
6											
7											

(b) (7)(E)



RGV PRD Risk Register 07-13-17.xls for Printed Item: 2642 (Attachment 3 of 3)

Program	Tactical Infrastructure
FM&E # & Project Title	RG
Date	Thursday, July 13, 2017
Project Manager	(b) (5), (b) (6), (b) (7) (C)
Project Base Cost Est.	
PBC + Est. Impact	

Border Patrol Facilities and Tactical Infrastructure

Facilities Management & Engineering

Risk Register



RISK MANAGEMENT SUMMARY RESULTS (planned)

3 Point Impact Estimate		
Low	Medium	High
\$	(b) (5)	

Total Expected Impact - Dollars \$ (b) (5), (b) (7) (E)

Total Expected Impact - Days

Impact to Critical Path - Total Days

ID #	Month/Year	Risk May Affect Critical Path	Milestone Affected	Risk Category	Detailed Description of Risk (Specific, Measurable, Attainable, Relevant, Timebound)	Mitigation of Risk	Estimated Impact - Days	Probability (%)	\$ Impact	Estimated Impact (\$)	Risk Level
8					(b) (5), (b) (7) (E)						
9											
10											
11											

(b) (5)

(b) (7)(E)



(b) (7)(E)

(b) (7)(E)

(b) (5)

(b) (5)

(b) (5)

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: (b)(7)(E) at Prototype Site - Request

Date: Tue Sep 19 2017 16:18:31 EDT

Attachments:

Sounds correct dec

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 19, 2017 2:13:04 PM

To: (b)(6);(b)(7)(C)

Subject: RE: (b)(7)(E) at Prototype Site - Request

(b)(6);(b)(7)(C) relayed to (b)(6);(b)(7)(C) that after the testing is complete, (b)(5), (b)(7)(E) Believe that given the current timing, that should be done around end of December this year

(b)(6);(b)(7)(C)

BPAM Project Manager

LMI Contractor

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 19, 2017 2:09 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: FW: (b)(7)(E) at Prototype Site - Request

Good afternoon (b)(6);(b)(7)(C)

I just wanted to follow up on (b)(6);(b)(7)(C) email below related to installing (b)(7)(E) at the Wall Prototype site. Please advise....

Thanks,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Portfolio Manager

Mobile and Agent Centric Systems

Headquarters, United States Border Patrol

Office: (b)(6);(b)(7)(C) | Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, September 15, 2017 8:05 AM

To: (b)(6);(b)(7)(C)

Subject: FW: (b)(7)(E) at Prototype Site - Request

FYSA

(b)(6);(b)(7)(C) PMP

Program Manager, Cross Border Tunnel Threat &
Linear Ground Detection System

Headquarters, United States Border Patrol

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, September 15, 2017 8:05 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: (b)(7)(E) at Prototype Site - Request

(b)(6);(b)(7)(C)

(b) (5), (b) (7)(E)

I am headed out on AL and back on Oct. 1 but let me know and I'll be checking email today.

Thanks for the consideration,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) PMP

Program Manager, Cross Border Tunnel Threat &
Linear Ground Detection System

Headquarters, United States Border Patrol

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)


Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From:

To:

(b)(6);(b)(7)(C)



Cc:

(b)(6);(b)(7)(C)

Bcc:

Subject: RE: Border Wall Prototype Letter from Governor Edmund Brown

Date: Tue Sep 19 2017 15:17:50 EDT

Attachments: S1 Response to GOV BROWN re Wall Prototype Construction

Location_DRAFT_091917_IPL, USBP, OFAM CLEARED.docx

Yes! Thank you all for your review and comments. Attached is a clean version we're moving forward.

Thanks,

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 19, 2017 3:16 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Border Wall Prototype Letter from Governor Edmund Brown

Good catch

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 19, 2017 2:59 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Border Wall Prototype Letter from Governor Edmund Brown

Couple of suggested edits.

<< File: S1 Response to GOV BROWN re Wall Prototype Construction Location_DRAFT_091917_V2 (002)Edits.docx >>

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 19, 2017 2:37 PM

To:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Border Wall Prototype Letter from Governor Edmund Brown

Team -

Please find a revised draft attached for review and comment. Our suspense is 2:45 ET, we appreciate your quick review!

Thanks,

(b)(6);(b)(7)(C)

<< File: S1 Response to GOV BROWN re Wall Prototype Construction Location_DRAFT_091917_V2.docx >>

From: (b)(6);(b)(7)(C)

Sent: Monday, September 18, 2017 5:25 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Border Wall Prototype Letter from Governor Edmund Brown

Good evening -

Please find a draft response for tomorrow's discussion attached.

Thank you,

(b)(6); (b)(7)(C)

<< File: S1 Response to GOV BROWN re Wall Prototype Construction Location_DRAFT_091917.docx >>

-----Original Appointment-----

From: (b)(6);(b)(7)(C)

Sent: Monday, September 18, 2017 1:36 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Border Wall Prototype Letter from Governor Edmund Brown

When: Tuesday, September 19, 2017 1:00 PM-1:30 PM (UTC-05:00) Eastern Time (US & Canada).

Where: Conference number: (b)(6);(b)(7)(C) Participant code: (b) (7)(E)

<< File: 9182017_102906AM_17-5769 Brown 09.15.17.pdf >>

(b) (5)

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: (b)(7)(E) at Prototype Site - Request

Date: Tue Sep 19 2017 14:13:58 EDT

Attachments:

Thanks

(b)(6);(b)(7)(C)

Portfolio Manager

Mobile and Agent Centric Systems

Headquarters, United States Border Patrol

Office: (b)(6);(b)(7)(C) | Mobile: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 19, 2017 2:13 PM

To: (b)(6);(b)(7)(C) (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

Subject: RE: (b)(7)(E) at Prototype Site - Request

(b)(6);(b)(7)(C): relayed to (b)(6);(b)(7)(C) that after the testing is complete, (b)(5), (b)(7)(E)
Believe that given the current timing, that should be done around
end of December this year

(b)(6);(b)(7)(C)

BPAM Project Manager

LMI Contractor

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Tuesday, September 19, 2017 2:09 PM
To: (b)(6);(b)(7)(C)
Subject: FW: (b)(7)(E) at Prototype Site - Request

Good afternoon (b)(6);(b)(7)(C)

I just wanted to follow up on (b)(6);(b)(7)(C) email below related to installing (b)(7)(E) at the Wall Prototype site.
Please advise....

Thanks,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Portfolio Manager

Mobile and Agent Centric Systems

Headquarters, United States Border Patrol

Office: (b)(6);(b)(7)(C) | Mobile: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Friday, September 15, 2017 8:05 AM
To: (b)(6);(b)(7)(C)
Subject: FW: (b)(7)(E) at Prototype Site - Request

FYSA

(b)(6);(b)(7)(C) PMP

Program Manager, Cross Border Tunnel Threat &

Linear Ground Detection System

Headquarters, United States Border Patrol

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, September 15, 2017 8:05 AM

To: (b)(6);(b)(7)(C)

Subject: (b)(7)(E) at Prototype Site - Request

(b)(6);(b)(7)(C)

(b) (5), (b) (7)(E)

I am headed out on AL and back on Oct. 1 but let me know and I'll be checking email today.

Thanks for the consideration,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) PMP

Program Manager, Cross Border Tunnel Threat &

Linear Ground Detection System

Headquarters, United States Border Patrol

U.S. Customs and Border Protection

Office: (b)(6);(b)(7)(C)

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Bcc:

Subject: RE: Border Wall Prototype Letter from Governor Edmund Brown

Date: Tue Sep 19 2017 07:54:43 EDT

Attachments:

Good morning folks. A good OFO POC for Trade and Commerce is (b)(6);(b)(7)(C) I've copied him on this email so he can be looped in (b)(6);(b)(7)(C)

(b)(6); (b)(7)(C)

Regards,

(b)(6);(b)(7)(C)

Deputy Chief - LEOD / Operations

U.S. Border Patrol Headquarters

(b)(6);(b)(7)(C) (office)
(b)(6);(b)(7)(C) (cell)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 19, 2017 7:26 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Border Wall Prototype Letter from Governor Edmund Brown

All - Given that Gov. Brown's letter specifically references the Otay POE and trade. Would it be wise to also ask someone from OFO to join us on the letter discussion today at 1PM? I put that out there because I don't know who that right person would be, but with the brain trust on this email, I am confident someone does.

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, September 18, 2017 5:25 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Border Wall Prototype Letter from Governor Edmund Brown

Good evening -

Please find a draft response for tomorrow's discussion attached.

Thank you,

(b)(6); (b)(7)(C)

<< File: S1 Response to GOV BROWN re Wall Prototype Construction Location_DRAFT_091917.docx >>

-----Original Appointment-----

From (b)(6);(b)(7)(C)

Sent: Monday, September 18, 2017 1:36 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Border Wall Prototype Letter from Governor Edmund Brown

When: Tuesday, September 19, 2017 1:00 PM-1:30 PM (UTC-05:00) Eastern Time (US & Canada).

Where: Conference number: (b)(6);(b)(7)(C) Participant code: (b)(7)(E)

<< File: 9182017_102906AM_17-5769 Brown 09.15.17.pdf >>

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: (b)(7)(E) foot tower

Date: Tue Sep 19 2017 07:44:46 EDT

Attachments:

Great-hopefully still ^{10/1/17}ft (b)(7)(E) or close to it

(b)(6);(b)(7)(C) P.E., PMP, Chief Engineer

Border Patrol & Air and Marine (BPAM) PMO

LMI Contractor

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, September 18, 2017 2:41 PM

To: (b)(6);(b)(7)(C)

Cc:

Subject: RE: (b)(7)(E) foot tower

OK. (b)(6);(b)(7)(C) spoke up and said that the (b)(7)(E) team agreed to a (b)(7)(E) I'll try to close the loop by tomorrow. I would like to be on the call with Dr. Unni, and I'm interested what he may want to discuss. Baker confirmed they have been working with them throughout the design process.

(b)(6);(b)(7)(C) P.E. LEED AP BD+C

Program Manager

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, September 18, 2017 1:53 PM

To: (b)(6);(b)(7)(C)

Cc:

Subject: RE: (b)(7)(E) foot tower

(b) (5), (b) (7)(E)

As an aside, Dr Unni (IBWC) just reached out to me wanting to discuss the RGV projects today or tomorrow. I gave him some times I'm available and will include you on the invite when the meeting is scheduled. I'm not sure what he wants to discuss. Copying (b)(6);(b)(7)(C) for situational awareness since he is heading to ELP today.

(b)(6);(b)(7)(C) P.E., PMP, Chief Engineer

Border Patrol & Air and Marine (BPAM) PMO

LMI Contractor

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, September 18, 2017 1:24 PM

To: (b)(6);(b)(7)(C)

Subject: FW (b)(7)(E) foot tower

We're being asked to accommodate the attached tower footprint (b)(7)(E) (b)(7)(E) for the (b)(7)(E) towers, do you know the minimum dimension we need to keep to meet IBWC maintenance requirements?

(b)(6);(b)(7)(C) P.E. LEED AP BD+C

Program Manager

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Wednesday, September 13, 2017 2:40 PM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: (b)(7)(E) foot tower

(b)(6);(b)(7)(C)

Attached is the (b)(7)(E) tower design for the RGV towers that we will be deploying thru out RGV.

(b) (5), (b) (7)(E)

r/

(b)(6);(b)(7)(C)

From:

To:

Cc:

Bcc:

Subject: RE: (b)(7)(E) foot tower

Date: Tue Sep 19 2017 07:38:35 EDT

Attachments:

He is going to call my cell phone today at a time TBD. I will try to conference you in via (b)(6);(b)(7)(C) old cell phone

(b)(6);(b)(7)(C) P.E., PMP, Chief Engineer
Border Patrol & Air and Marine (BPAM) PMO
LMI Contractor
Mobile: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

-----Original Message-----

From: (b)(6);(b)(7)(C)

Sent: Monday, September 18, 2017 7:05 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: (b)(7)(E) foot tower

Copy

From: (b)(6);(b)(7)(C)

Sent: Monday, September 18, 2017 2:41:21 PM

To: (b)(6);(b)(7)(C)

Cc:

Subject: RE: (b)(7)(E) foot tower

OK. (b)(6);(b)(7)(C) spoke up and said that the (b)(7)(E) team agreed to a (b)(7)(E) I'll try to close the loop by tomorrow. I would like to be on the call with Dr. Unni, and I'm interested what he may want to discuss. Baker confirmed they have been working with them throughout the design process.

(b)(6);(b)(7)(C) P.E. LEED AP BD+C

Program Manager

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, September 18, 2017 1:53 PM

To: (b)(6);(b)(7)(C)

Cc:

Subject: RE: (b)(7)(E) foot tower

(b) (5), (b) (7)(E)

As an aside, Dr Unni (IBWC) just reached out to me wanting to discuss the RGV projects today or tomorrow. I gave him some times I'm available and will include you on the invite when the meeting is scheduled. I'm not sure what he wants to discuss. Copying (b)(6);(b)(7)(C) for situational awareness since he is heading to ELP today.

(b)(6);(b)(7)(C) P.E., PMP, Chief Engineer Border Patrol & Air and Marine (BPAM) PMO LMI Contractor

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, September 18, 2017 1:24 PM

To: (b)(6);(b)(7)(C)

Subject: FW: (b)(7)(E) foot tower

We're being asked to accommodate the attached tower footprint (b)(7)(E)

(b)(7)(E) for the (b)(7)(E) towers, do you know the minimum dimension we need to keep to meet IBWC maintenance requirements?

(b)(6);(b)(7)(C) P.E. LEED AP BD+C

Program Manager

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Wednesday, September 13, 2017 2:40 PM

To: (b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

Subject: (b)(7)(E) foot tower

(b)(6);(b)(7)(C)

Attached is the (b)(7)(E) tower design for the RGV towers that we will be deploying thru out RGV.

(b)(7)(E)

r/


(b)(6);(b)(7)(C)

From:

To:

Cc:

(b)(6);(b)(7)(C)



(b)(6);(b)(7)(C)

Bcc:
Subject: RE: Border Wall Prototype Letter from Governor Edmund Brown
Date: Tue Sep 19 2017 07:30:38 EDT
Attachments:

I would recommend engaging (b)(6);(b)(7)(C) If it isn't her, she can point us in the right direction.

(b)(6);(b)(7)(C)

Associate Chief
Operational Requirements Management Branch
U.S. Border Patrol Headquarters

(b)(6);(b)(7)(C)

Office (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 19, 2017 7:26 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Border Wall Prototype Letter from Governor Edmund Brown

All - Given that Gov. Brown's letter specifically references the Otay POE and trade. Would it be wise to also ask someone from OFO to join us on the letter discussion today at 1PM? I put that out there because I don't know who that right person would be, but with the brain trust on this email, I am confident someone does.

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, September 18, 2017 5:25 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Border Wall Prototype Letter from Governor Edmund Brown

Good evening -

Please find a draft response for tomorrow's discussion attached.

Thank you,

(b)(6); (b)(7)(C)

<< File: S1 Response to GOV BROWN re Wall Prototype Construction Location_DRAFT_091917.docx
>>

-----Original Appointment-----

From: (b)(6);(b)(7)(C)

Sent: Monday, September 18, 2017 1:36 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Border Wall Prototype Letter from Governor Edmund Brown

When: Tuesday, September 19, 2017 1:00 PM-1:30 PM (UTC-05:00) Eastern Time (US & Canada).

Where: Conference number: (b)(6);(b)(7)(C) Participant code: (b)(7)(E)

<< File: 9182017_102906AM_17-5769 Brown 09.15.17.pdf >>

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: FW: Wall (b)(7)(E) Report Out

Date: Mon Sep 18 2017 22:58:10 EDT

Attachments: Final Brief_DRAFT_v004.pptx

(b)(7)(E) Final Report_31AUG2017_v01.docx

Do not forward

From: (b)(6);(b)(7)(C)

Sent: Saturday, September 16, 2017 2:06:05 PM

To: (b)(6);(b)(7)(C)

Subject: FW: Wall (b)(7)(E) Report Out

Enjoy

From: (b)(6);(b)(7)(C) <(b)(7)(E)> Final Report_31AUG2017_v01.docx>> IN E

Sent: Saturday, September <<Final Brief_DRAFT_v004.pptx>> 16, 2017 7:29:05 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: RE: Wall (b)(7)(E) Report Out

All,

Please find attached the read-aheads that will be used on Monday morning for the Wall (b)(7)(E) Report out. Hard copies will be provided for those in the room and there will be a call-in number for those that cannot make it in person. Due to the content of the information we will not be posting it to the invitation.

Thanks,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

-----Original Appointment-----

From: (b)(6);(b)(7)(C)

Sent: Thursday, August 31, 2017 2:45 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Wall (b)(7)(E) Report Out

When: Monday, September 18, 2017 9:00 AM-10:00 AM (UTC-05:00) Eastern Time (US & Canada).

Where: PR-1340/Call-In (b)(6);(b)(7)(C) PIN (b)(7)(E) (Host Code: (b)(7)(E))

Read-aheads will be sent to the group prior to meeting

Purpose of Meeting: To review Wall (b)(7)(E) report out and conclusions

BORDER WALL SYSTEM (b)(7)(E)

U.S. Department of Homeland
Customs and Border Protection

S



U.S. Customs and
Border Protection

Pre-Decisional
~~For Official Use Only (FOUO)~~

(b) (5)



U.S. Customs and
Border Protection

Pre-Decisional
For Official Use Only (FOUO)

(b) (5), (b) (6)



U.S. Customs and
Border Protection

Pre-Decisional
~~For Official Use Only (FOUO)~~

(b) (5)



U.S. Customs and
Border Protection

Pre-Decisional
~~For Official Use Only (FOUO)~~

(b) (5)



U.S. Customs and
Border Protection

~~Pre-Decisional~~
~~For Official Use Only (FOUO)~~

(b) (5)



U.S. Customs and
Border Protection

~~Pre-Decisional~~
~~For Official Use Only (FOUO)~~

(b) (5)



U.S. Customs and
Border Protection

~~Pre-Decisional~~
~~For Official Use Only (FOUO)~~

(b) (5)



U.S. Customs and
Border Protection

~~Pre-Decisional~~
~~For Official Use Only (FOUO)~~

(b) (5)



U.S. Customs and
Border Protection

~~Pre-Decisional~~
~~For Official Use Only (FOUO)~~

(b) (5)



U.S. Customs and
Border Protection

~~Pre-Decisional~~
~~For Official Use Only (FOUO)~~

(b) (5)



U.S. Customs and
Border Protection

~~Pre-Decisional~~
~~For Official Use Only (FOUO)~~

Backup Slides



~~Pre-Decisional~~
~~For Official Use Only (FOUO)~~

(b) (5)

~~For Official Use Only (FOUO)~~

(b) (5)



U.S. Customs and
Border Protection

~~Pre-Decisional~~
~~For Official Use Only (FOUO)~~

(b) (5)



~~For Official Use Only (FOUO)~~

(b) (5)



U.S. Customs and
Border Protection

~~Pre-Decisional~~
~~For Official Use Only (FOUO)~~



Customs and Border Protection

Border Wall System (b)(7)(E)

Final Report

September 2017

~~PRE-DECISIONAL~~
~~FOR OFFICIAL USE ONLY (FOUO)~~

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5), (b) (6)




(b) (5)

(b) (5)

(b) (5)


~~PRE-DECISIONAL~~
~~FOR OFFICIAL USE ONLY (FOUO)~~

(b) (5), (b) (7)(E)



(b) (5)

(b) (5), (b) (7)(E)



(b) (5)


(b) (5)

X

~~PRE-DECISIONAL~~
~~FOR OFFICIAL USE ONLY (FOUO)~~


BW23 FOIA CBP 011706

(b) (5), (b) (7)(E)




(b) (5)

(b) (5), (b) (7)(E)



(b) (5)

(b) (5), (b) (7)(E)



(b) (5)

~~PRE-DECISIONAL~~
~~FOR OFFICIAL USE ONLY (FOUO)~~

(b) (5)

(b) (5)

(b) (5)

(b) (5)

XX

~~PRE-DECISIONAL~~
~~FOR OFFICIAL USE ONLY (FOUO)~~

BW23 FOIA CBP 011716

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

XXV

~~PRE-DECISIONAL~~

~~FOR OFFICIAL USE ONLY (FOUO)~~

BW23 FOIA CBP 011721


(b) (7) (E)



(b) (7) (E)

(b) (7) (E)

(b) (5), (b) (7)(E)



(b) (5)

XXX

~~PRE-DECISIONAL~~
~~FOR OFFICIAL USE ONLY (FOUO)~~

BW23 FOIA CBP 011726

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

~~PRE-DECISIONAL~~
~~FOR OFFICIAL USE ONLY (FOUO)~~

(b) (5)

(b) (5)

From: (b)(6);(b)(7)(C)
To: (b)(6);(b)(7)(C)
Cc:
Bcc:
Subject: I told (b)(6);(b)(7)(C) to talk to you
Date: Wed Sep 13 2017 15:42:34 EDT
Attachments:

(b) (5), (b)(6);(b)(7)(C)

Also-your out of office email is still on.

(b)(6);(b)(7)(C) P.E., PMP, Chief Engineer
(b)(7)(C)
Border Patrol & Air and Marine (BPAM) PMO

LMI Contractor

Mobile: (b)(7)(C), (b)(6)

(b)(6);(b)(7)(C)
(b)(6)

From: (b) (6), (b) (7)(C) (CTR)

Sent: Thursday, September 07, 2017 2:50 PM

To: (b) (6)

(b)(6);(b)(7)(C)

(b) (6)

(b)(6);(b)(7)(C)
(b) (6)

(b)(6);(b)(7)(C)

(b) (6)

(b)(6);(b)(7)(C)

(b) (6)

(b)(6);(b)(7)(C)
(b) (6)

Subject: 20170907_Border Wall T&E Strategy_no backup_FOUC.pptx

T&E IPT,

Attached are slides that will be presented at the next C2 brief, next week. Please review and if you have questions, comments, or updates please provide NLG Tuesday, 12 Sep.

v/r,

(b) (6) (MITRE)

Acting Technical Director

Land Systems Operational Test Authority (LSOTA)

(b)(6);(b)(7)(C)

(b) (6), (b) (7)(C)

Development Institute (HSSDI)

(b) (6)

(b) (6), (b) (7)(C)

From:

(b)(7)(E)

To:

(b) (6)

Cc:

(b) (6)

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Bcc:

Subject:

RE: Wall Schedules - 13 Sep 17

Date:

Mon Sep 18 2017 09:28:42 EDT

Attachments:

Thanks, (b) (6)

(b)(6); (b)(7)(C)

-----Original Message-----

From:

(b) (6)

Sent: Monday, September 18, 2017 9:27 AM

To:

(b)(6); (b)(7)(C)

Cc:

(b) (6)

(b)(6); (b)(7)(C)

Subject: FW: Wall Schedules - 13 Sep 17

(b)(6); (b)(7)(C)

We did not send an update on RGV (b)(6) last week because we need to work the logic to show AUG construction start. We'll get that done this week and be sure to include (b)(7)(E) in this week's push.

Thank you,

(b) (6)

(b) (6)

PMP

Deputy for Programs

USACE - Border Infrastructure PMO

(b) (6)

BB:

(b) (6)

NOTICE: Do not release under the Freedom of Information Act, 5 U.S.C. § 552 (FOIA). This message [or document] contains personal and confidential information for the intended recipients and contains pre-decisional advice or information which is protected from disclosure under FOIA. Do not copy or release without prior authorization from the originator. Any review or distribution without consent is strictly prohibited. If you have received this information in error, please notify the sender immediately.

-----Original Message-----

From: (b)(6); (b)(7)(C)
Sent: Monday, September 18, 2017 7:36 AM
To: (b)(6)
Subject: [EXTERNAL] RE: Wall Schedules - 13 Sep 17

(b)(6)

Can you please send the RGV (b)(7)(E) schedule?

(b)(6); (b)(7)(C)

-----Original Message-----

From: (b)(6)
Sent: Friday, September 15, 2017 5:20 PM
To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C) (b)(6) (b)(6)
(b)(6); (b)(7)(C) (b)(6) (b)(6)
(b)(6); (b)(7)(C) (b)(6)
(b)(6); (b)(7)(C) (b)(6)
(b)(6); (b)(7)(C) (b)(6)

Subject: Wall Schedules - 13 Sep 17

All,

Attached are the latest schedules for both the FY17 & 18 Program.

Thank you,
(b)(6)
Program Specialist
CESWF-PM-PMO
W (b)(6)
F: (b)(6)

From:

(b)(6); (b)(7)(C)

To:

(b)(6)

(b)(6); (b)(7)(C)

(b)(6)

Cc:

(b)(6)

(b)(6)

(b)(6); (b)(7)(C)

(b)(6)

(b)(6)

(b)(6)

(b)(6); (b)(7)(C)

(b)(6)

Bcc:

Subject:

RE: ELP (b)(7)(E)mi Fence Replacement-Automated Vehicle Gates

Date:

Mon Sep 18 2017 08:52:21 EDT

Attachments:

Thanks (b)(6)

(b)(6); (b)(7)(C)

Chief, Portfolio Management and Analysis (PMA) Branch

Border Patrol & Air and Marine Program Management Office

Mobile: (b)(6); (b)(7)(C)

Office: (b)(6); (b)(7)(C)

PMA Sharepoint Site:

(b)(7)(E)

From:

(b)(6)

Sent: Monday, September 18, 2017 7:48 AM

To:

(b)(6); (b)(7)(C)

(b)(6)

(b) (6)
Cc: (b) (6)
(b)(6); (b)(7)(C) (b) (6)
(b) (6) (b) (6)
(b)(6); (b)(7)(C)
(b) (6)

Subject: RE: ELP (b) (7)(E) mi Fence Replacement-Automated Vehicle Gates

(b)(6); (b)(7)(C)

As I understand it, this is a change back to the gate configuration that Baker had previously.

(b) (6) told me they were clear and knew what to do to finish their updates.

If anyone is uncomfortable or if there is confusion, we can definitely have a quick team huddle.

(b) (6)

(b) (6)

Tactical Infrastructure Program Manager

ECSO, TI Branch

USACE Fort Worth District

office (b) (6)

bb (b) (6)

NOTICE: Do not release under the Freedom of Information Act, 5 U.S.C. § 552 (FOIA). This message [or document] contains personal and confidential information for the intended recipients and contains pre-decisional advice or information which is protected from disclosure under FOIA. Do not copy or release without prior authorization from the originator. Any review or distribution without consent is strictly prohibited. If you have received this information in error, please notify the sender immediately.

From: (b)(6); (b)(7)(C)

Sent: Sunday, September 17, 2017 12:28 PM

To: (b)(6); (b)(7)(C) (b)(6)
(b)(6)
Cc: (b)(6) (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C) (b)(6)
(b)(6); (b)(7)(C) (b)(6)

Subject: [EXTERNAL] RE: ELP (b)(7)(E) mi Fence Replacement-Automated Vehicle Gates

Thanks (b)(6); (b)(7)(C)

(b)(6) let me know if you want to tag up on this Monday AM.

(b)(6); (b)(7)(C)

Chief, Portfolio Management and Analysis (PMA) Branch

Border Patrol & Air and Marine Program Management Office

Mobile (b)(6); (b)(7)(C)

Office:

PMA Sharepoint Site: (b)(7)(E)

From: (b)(6); (b)(7)(C)

Sent: Friday, September 15, 2017 8:13 PM

To: (b)(6); (b)(7)(C) (b)(6)
(b)(6); (b)(7)(C) (b)(6)
(b)(6); (b)(7)(C) (b)(6)


Subject: ELP (b)(7)(E) mi Fence Replacement-Automated Vehicle Gates

(b)(6); (b)(7)(C)

I was reviewing the "issued for bid" design drawings for the ^{(b)(7)}mi ELP ^{(b)(7)(E)}RF project and realized that the hardware (motor, controls, etc.) associated with the proposed automated vehicle gate(s) at ^{(b)(5), (b)(7)(E)}

 Sorry for the miss-fire on my part and any inconvenience I caused.

Best,



(b)(6); (b)(7)(C)

P.E., PMP, Chief Engineer

Border Patrol & Air and Marine (BPAM) PMO

LMI Contractor

Mobile: (b)(6); (b)(7)(C)


(b)(6); (b)(7)(C)

From:

To:

Cc:

(b)(6); (b)(7)(C)

Bcc:

Subject: RE: ILSP submission for signature

Date: Sun Sep 17 2017 18:47:42 EDT

Attachments: image001.png

(b)(6); (b)(7)(C) – we need a meeting please. I fear that if we don't get on the calendar we won't have this discussion.

(b)(6); (b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Friday, September 15, 2017 5:28 PM

To:

Cc:

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: ILSP submission for signature

Let discuss next week

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Tuesday, September 12, 2017 8:58 AM

To: (b)(6); (b)(7)(C)

Cc:

(b)(6); (b)(7)(C)

Subject: FW: ILSP submission for signature

(b)(6); (b)(7)(C) - Need your help with this one.

DHS/PARM is requesting a LRFP along with an LMS. This is not a requirement per say, but being that it is coming from PARM, I want to elevate to you for a decision. (b) (5), (b)(6); (b)(7)(C)

Their comments on the LRFP are as follows:

(b) (5)

Comments on the LMS are:

(b) (5)

(b)(6); (b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Friday, September 08, 2017 1:45 PM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: ILSP submission for signature

(b)(6); (b)(7)(C) as (b)(6); (b)(7)(C) mentioned earlier today, we have received additional feedback on the draft ILSP. DHS has reviewed and their comments have been added to the current adjudicated comments. These new comments need adjudication.

To summarize, the IMS didn't get attached as promised in the adjudication;
they present a case for an LRFP-extrapolated from known CTIMR contracts;
A request for an LMS,
and another take on the (b)(7)(E)/IT Technologies question.

Please take a look at the new comments (appended to the bottom) and adjudicate. When you're done, please edit the ILSP accordingly, add appendices and update the signature page – see comment nr. 6 with the recommendations if you agree.

Please let me know if you have any questions on this. I'll be right with you till we get this to signature.

And no, we don't expect any more comments in at this stage.

V/R

(b)(6); (b)(7)(C)

PMP

(Contractor, ManTech Team)

Senior Subject Matter Expert III

Supporting the Office of Acquisition

U.S. Customs and Border Protection

Office: (b)(6); (b)(7)(C)

Mobile

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Wednesday, September 6, 2017 10:06 AM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: ILSP submission for signature

Hey (b)(6); (b)(7)(C)

Hope all is well.

So (b)(6); (b)(7)(C) and I touched base and at this time we are not incorporating the TI piece.

Technology will be incorporated at a later date outside the (b)(6); (b)(7)(C) RGV miles (which is our current requirement for ADE2).

Please let us know if any further action is required from BPAM, otherwise tag you're it.

(b)(6); (b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6); (b)(7)(C)

Cell: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b)(6); (b)(7)(C)

Sent: Tuesday, September 05, 2017 12:19 PM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: FW: ILSP submission for signature

(b)(6); (b)(7)(C)


See comments here and also attached revisions.

Please let us know if you need anything additional.

Overall: where the comments are in the form of a question and you are answering the question, suggest closing the loop on adjudication by adding the notation "No change to the document required" or some equivalent, to your response. This helps remove any potential ambiguity. Examples are comments 7, 11, 12, 18, 19 etc. updated

Going down the attached comment form in order:

(b) (5), (b) (7)(E)



And...one for the calculator: Updated

(b)(6); (b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Friday, September 01, 2017 3:52 PM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: FW: ILSP submission for signature

FYI

From: (b)(6); (b)(7)(C)

Sent: Friday, September 01, 2017 11:03:23 AM

To: (b)(6); (b)(7)(C)

Cc:

Subject: RE: ILSP submission for signature

Thanks (b)(6); (b)(7)(C) and I went over the adjudication and we would like to note just a few issues and offer some suggestions for resolution before we finalize.

Overall: where the comments are in the form of a question and you are answering the question, suggest closing the loop on adjudication by adding the notation "No change to the document required" or some equivalent, to your response. This helps remove any potential ambiguity. Examples are comments 7, 11, 12, 18, 19 etc.

Going down the attached comment form in order:

(b) (5)

(b) (5), (b) (7)(E)

And...one for the calculator:

- Subtotal error on the LCCE:

o In both tables 4 and 5, the total column (last column) - the 2.2 subtotal is incorrect. Strangely, this does not affect the grand totals. However, if someone independently adds the subtotals to check the grand total, they do not add up because the 2.2 subtotal is incorrect.

o Table 4 – 2.2 Subtotal is (b) (5) If you sum all of 2.2 it should actually be (b) (5) which gets us to the correctly depicted grand total.

o Table 5 – 2.2 Subtotal is (b) (5) If you sum all of 2.2 it should actually be (b) (5) which gets us the correctly depicted grand total.

Please let me know if you have any questions or need any assistance at all.

V/R

(b)(6); (b)(7)(C)

PMP

(Contractor, ManTech Team)

Senior Subject Matter Expert III

Supporting the Office of Acquisition

U.S. Customs and Border Protection

Office: (b)(6); (b)(7)(C)

Mobile

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Wednesday, August 30, 2017 2:13 PM

To: (b)(6); (b)(7)(C)

Cc:

(b)(6); (b)(7)(C)

Subject: RE: ILSP submission for signature

(b)(6); (b)(7)(C)

Attached is the revised ILSP, accepted comments have been incorporated.

Document has been signed by our PMO.

Please assist with obtaining additional signatures.

Thank you,

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6); (b)(7)(C)

Cell: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b)(6); (b)(7)(C)

Sent: Friday, August 25, 2017 2:42 PM

To:

(b)(6); (b)(7)(C)

Cc:

(b)(6); (b)(7)(C)

Subject: RE: ILSP submission for signature

(b)(6); (b)(7)(C)

Here are the comments on the ILSP

R

(b)(6); (b)(7)(C)

Division Director

Acquisition Policy and Oversight (APO)

Office of Acquisition (OA)/AGO

(b)(6); (b)(7)(C)(office)

(cell)

(fax)

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Thursday, August 03, 2017 2:35 PM

To: (b)(6); (b)(7)(C)

Cc:

(b)(6); (b)(7)(C)

Subject: ILSP submission for signature

(b)(6); (b)(7)(C)

Attached is the final draft of the Wall ILSP.

It has been reviewed/approved by BPAM PMO.

Please let us know if you have any questions or comments on the attached document.

We greatly appreciate your support in getting the ILSP signed.

Thank you,

(b)(6); (b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6); (b)(7)(C)

Cell: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From:

To:

(b)(6); (b)(7)(C)

Cc:

Bcc:

Subject: RE: Possible Media Questions About the Prototypes

Date: Sun Sep 17 2017 18:43:41 EDT

Attachments: image001.jpg

image002.jpg

image003.jpg

image004.jpg

image005.jpg

image006.jpg

Got it – we will clean up and get it back to OPA manana.

(b)(6); (b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Sunday, September 17, 2017 2:23 PM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: FW: Possible Media Questions About the Prototypes

(b)(6); (b)(7)(C) are likely better and less caustic

From: (b)(6); (b)(7)(C)
Sent: Sunday, September 17, 2017 7:06:43 PM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: Possible Media Questions About the Prototypes

(b)(6); (b)(7)(C)

LMI
7940 Jones Branch Drive
Tysons, VA 22102
Cell: (b)(6); (b)(7)(C)

Complex Problems. Practical Solutions.
www.lmi.org

From: (b)(6); (b)(7)(C)
Sent: Friday, September 15, 2017 2:38 PM
To: (b)(6); (b)(7)(C)
Subject: [EXTERNAL] FW: Possible Media Questions About the Prototypes

From: (b)(6); (b)(7)(C)
Sent: Friday, September 15, 2017 5:56:09 PM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: FW: Possible Media Questions About the Prototypes

As discussed – see below. Added in some answers (the ones I know) in yellow. Can you pile on please? (b)(6); (b)(7)(C) – can you get this over the finish line please?

CC'ing (b)(6); (b)(7)(C) just as FYSA – so he can see some of the sausage making that has been going on.

(b)(6); (b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Friday, September 15, 2017 12:35 PM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: Possible Media Questions About the Prototypes

Good morning as we prepare for the construction of prototypes in San Diego, I asked my public affairs colleagues on the field to send me questions that they believe media can/would ask during the construction of the prototypes. The questions are below under the sections of Border Patrol Operations, Protest Operations and Prototype Construction and Testing.

As you'll see below I've divided the questions by section for to make them easier to manage. We are requesting that you review the question and provide the best possible answer that you have available at this point.

If possible we would like to have the answers by COB Tuesday, Sept 19. Once again thank you for your continued collaboration.

Also, please share with anybody that I might have missed.

Border Patrol Operations BP ANSWER

(b) (5)

(b) (5)

(b) (5)

(b)(6); (b)(7)(C)

(b) (5)

See above, TBD

Other questions

(b)(6); (b)(7)(C)

Southwest Border Branch Chief

Customs and Border Protection

Office of Public Affairs – Media Division

Office: (b)(6); (b)(7)(C)

Mobile: (b)(6); (b)(7)(C)

Email: (b)(6); (b)(7)(C)

From:

To:

Cc:

Bcc:

Subject: RE: Draft FME Initiatives 2018

Date: Fri Sep 15 2017 17:24:16 EDT

Attachments: image001.jpg

I am ok with the initiatives - (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Wednesday, September 13, 2017 11:40 AM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: FW: Draft FME Initiatives 2018

Importance: High

Good Morning,

The attached is provided. Please respond with your thoughts as soon as possible, I will compile and provide to (b)(6); (b)(7)(C)

Thank you,

(b)(6); (b)(7)(C)

Executive Assistant

Supporting US Customs and Border Protection,

Facilities Management & Engineering

BB: (b)(6); (b)(7)(C)

Email: (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Monday, September 11, 2017 1:46 PM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: Draft FME Initiatives 2018

(b)(6); (b)(7)(C)

Here are the drafts for the proposed 2018 initiatives. I understand they are due tomorrow. Just wanted to make sure you had the input you needed to discuss with (b)(6); (b)(7)(C) whenever might be convenient.

r/

(b)(6); (b)(7)(C)

From:

(b)(6); (b)(7)(C)

To:

(b)(6)

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Cc:

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b)(6)

(b)(6); (b)(7)(C)

Bcc:

Subject: RE: RGV Wall Weekly Update

Date: Fri Sep 15 2017 11:11:55 EDT

Attachments: Border Wall System High Level Schedule_20170809_80 percent CI_DHS Brief.pdf

High level overview – as (b)(6); (b)(7)(C) mentioned on the call.

<<Border Wall System High Level Schedule_20170809_80 percent CI_DHS Brief.pdf>>

(b)(6); (b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Friday, September 15, 2017 11:10 AM

To

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b)(6)

(b)(6)

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Cc:

(b)(6); (b)(7)(C)

(b)(6)

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: RGV Wall Weekly Update

Most up to date IMS.

<< File: Border Wall System IMS_Baselined_as of 20170911.pdf >>

(b)(6); (b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6); (b)(7)(C)

-----Original Appointment-----

From: (b)(6); (b)(7)(C)

Sent: Tuesday, August 15, 2017 12:45 PM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b) (6)

(b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

(b) (6)

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RGV Wall Weekly Update

When: Friday, September 15, 2017 10:30 AM-12:00 PM (UTC-05:00) Eastern Time (US & Canada).

Where: Conference access number: (b) (7)(E) , Participant code is: (b) (7)(E)

Topics for Discussion:

- PRD Status
- Schedule
- Cost estimate/Scope
- Acquisition
- Environmental
- Real Estate

Border Wall System High-Level Schedule

Status as of 9/22/2017

Border Wall System High Level Schedule	FY17			FY18				FY19				FY20				FY21				FY22						
	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2					
	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F
-ADE 2A/B																										
-Documentation & ADE 2A/B (ARB) Briefing																										
-Funding																										
-Wall Prototype (San Diego)																										
-RFP/Contract Award																										
-Prototype Construction																										
-Testing/Report																										
-Update of Design Standards																										
-San Diego (SDC Secondary Wall)																										
-A/E Award / Design																										
-RFP/Contract Award																										
-Design Development (100% Design)																										
-San Diego Border Wall Construction (14 miles)																										
-Rio Grande Valley (RGV) Sector																										
-RGV (b)(7)(E) Mile Segment (Levee Wall)																										
-RGV (b)(7)(E) Project - (b)(7)(E) Miles																										
-A/E Award																										
-Design and RFP Preparation																										
-RFP Release/Proposal Preparation																										
-Evaluations/Award																										
-(b)(7)(E) Construction on Federally Owned Land (b)(7)(E) miles)																										
-Environmental Waiver																										
(b)(7)(E) Private Land Option (Real Estate)																										
Border Wall Construction on Private Land (b)(7)(E) miles)																										
-RGV (b)(7)(E) Project - (b)(7)(E) Miles (Border Wall Construction)																										
-RGV Project - (b)(7)(E) Miles (Border Wall Construction)																										
-RGV Project - (b)(7)(E) Miles (Border Wall Construction)																										
-RGV (b)(7)(E) Mile Segment (Flood Plain)																										
-RGV (b)(7)(E) Project - (b)(7)(E) Miles (Border Wall Construction)																										
-RGV Project - (b)(7)(E) Miles (Border Wall Construction)																										
-RGV Project - (b)(7)(E) Miles (Border Wall Construction)																										
-RGV Project - (b)(7)(E) Miles (Border Wall Construction)																										
-RGV Project - (b)(7)(E) Miles (Border Wall Construction)																										
-RGV Project - (b)(7)(E) Miles (Border Wall Construction)																										
-RGV Project - (b)(7)(E) Miles (Border Wall Construction)																										

Task
(on Critical Path)Task
(Not on Critical Path)Task
(Completed)Milestone
(on Critical Path)Milestone
(Not on Critical Path)Milestone
(Completed)Future RGV
Levee Wall Project

BW23 FOIA b(7)(E) b(7)(F)

Future RGV
Flood Plain Project

From:

(b)(6); (b)(7)(C)

To:

Cc:

Bcc:

Tech for RGV b6 (b)7

Fri Sep 15 2017 10:49:30 EDT

Attachments: RGV b6 (b)7 Tech Issues.pptx

(b)(6); (b)(7)(C) and I have spitballed this as a starting point with PMOD.



(b)(6); (b)(7)(C)

BPAM Project Manager

LMI Contractor

(b)(6); (b)(7)(C)

Wall and Associated Technology

- BEZ
- Need to address each tech and what is funded, what \$ is needed and what needs to be integrated
- C2/control room
-  (b)(6); (b)(7)(C)
- 
- Microwave/backhaul

PRD Includes

- Purchase and Installation of (b)(6); (b)(7)(C)
- Purchase and Installation of (b)(6); (b)(7)(C)

In Addition to:

- Levee/Wall
- Gates
- Patrol Road
- Enforcement Zone Vegetation Removal

Not Included/Funded Through Levee/Wall

- Integration of Technology
- Microwave Backhaul (including tower) or (b)(6); (b)(7)(C)
- (b)(6); (b)(7)(C) Display and Space
- (b)(6); (b)(7)(C)
- Station Tower Space and Microwave as Needed
- Microwave Backhaul Path Analysis
- (b)(6); (b)(7)(C) Installation on Wall

Next Steps

(b) (5)

From:

(b)(6); (b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: TO 17 RGV (b)(6); (b)(7)(C) Floodwall Construction Project (b)(7)(E) Miles) 95% Design Review Conference

Date: Fri Sep 15 2017 10:36:49 EDT

Attachments:

copy

(b)(6); (b)(7)(C)

-----Original Message-----

From: (b)(6); (b)(7)(C)

Sent: Friday, September 15, 2017 10:34 AM

To: (b)(6); (b)(7)(C)

Subject: RE: TO 17 RGV (b)(6); (b)(7)(C) Floodwall Construction Project (b)(7)(E) Miles) 95% Design Review Conference

I'm not aware of any major issues with the design at this point. If my meeting with (b)(6) ends early I will call in otherwise I'll follow-up with (b)(6) this afternoon.

-----Original Message-----

From: (b)(6); (b)(7)(C)

Sent: Friday, September 15, 2017 10:21 AM

To: (b)(6); (b)(7)(C)

Subject: [EXTERNAL] RE: TO 17 RGV (b)(6); (b)(7)(C) Floodwall Construction Project (b)(7)(E) Miles) 95% Design Review Conference

Understand - but not being on the meeting causes friction =

(b)(6); (b)(7)(C)

-----Original Message-----

(b)(6); (b)(7)(C)

Sent: Friday, September 15, 2017 10:15 AM

To: (b)(6); (b)(7)(C)

Subject: RE: TO 17 RGV (b)(6); (b)(7)(C) Floodwall Construction Project (b)(7)(E) Miles) 95% Design Review Conference

I'm sorry-I have a meeting with our new CEO that I can't miss. I was not consulted as to the time of meeting prior to it being scheduled or I would have advised as to the conflict. I provided my review comments on time and don't believe any to be controversial.

-----Original Message-----

From: (b)(6); (b)(7)(C)

Sent: Friday, September 15, 2017 10:12 AM

To: (b)(6); (b)(7)(C)

Subject: [EXTERNAL] FW: TO 17 RGV (b)(7)(E) Floodwall Construction Project (b)(7)(E) Miles) 95% Design Review Conference

This is a problem

(b)(6); (b)(7)(C)

-----Original Message-----

From: (b) (6)

Sent: Friday, September 15, 2017 10:06 AM

To: (b)(6); (b)(7)(C)

Subject: FW: TO 17 RGV (b)(7)(E) Floodwall Construction Project (b)(7)(E) Miles) 95% Design Review Conference

Is his conflict doing something for you? This is why the team gets spun up...

-----Original Message-----

From: (b)(6); (b)(7)(C)

Sent: Friday, September 15, 2017 8:58 AM

To: (b) (6)

(b)(6); (b)(7)(C)

Cc: (b) (6) (b)(6); (b)(7)(C)

Subject: [EXTERNAL] RE: TO 17 RGV (b)(7)(E) Floodwall Construction Project (b)(7)(E) Miles) 95% Design Review Conference

(b) (6)

Unfortunately I have a conflict with this afternoon's comment review resolution meeting and likely won't be able to call in however I will be available after 2 pm est today to answer any engineering/design related questions if needed. Sorry for the inconvenience.

(b)(6); (b)(7)(C)

-----Original Appointment-----

From: (b) (6)

Sent: Monday, September 11, 2017 7:57 AM

To: (b) (6) (b)(6); (b)(7)(C) (b) (6)

(b)(6); (b)(7)(C) (b) (6) (b) (6) (b) (6)

(b) (6)

(b) (6)

(b)(6); (b)(7)(C)

Subject: [EXTERNAL] TO 17 RGV (b)(7)(E) Floodwall Construction Project (b)(7)(E) Miles) 95% Design Review Conference

When: Friday, September 15, 2017 11:00 AM-1:00 PM (UTC-06:00) Central Time (US & Canada),

Where: WebEx Conference Call

All,

Please provide comments by COB 13 Sept, 2017. Comments should be entered into Dr. Checks. If Dr. Checks is not available, you can enter your comments into the attached matrix and return to me by the deadline. 15 Sept, 2017 is scheduled for the design review conference call. Please distribute this meeting invite to whom you feel necessary.

DO NOT DELETE OR CHANGE ANY OF THE TEXT BELOW THIS LINE

(b) (6) has scheduled this WebEx meeting.

TO 17 RGV (b)(7)(E) Floodwall Construction Project (b)(7)(E) Miles) 95% Design Review Conference

Host: (b) (6)

When it's time, start or join the WebEx meeting from here:

(b) (7)(E)

Access Information

Meeting Number: (b) (7)(E)

Meeting Password: This meeting does not require a password.

Audio Connection

(b) (7)(E) (Cisco WebEx)

Access Code:

(b) (7)(E)

Hosts, need your host access code or key? Go to the meeting information page:

(b) (7)(E)

Delivering the power of collaboration

The meetings.mbakercorp.com team

Need help?

(b) (7)(E)

From:

To:

Cc:

(b)(6); (b)(7)(C)

Bcc:

Subject: RE: TO 17 RGV (b)(6); (b)(7)(C) Floodwall Construction Project (b)(7)(E) Miles) 95% Submittal Package

Date: Thu Sep 14 2017 10:39:17 EDT

Attachments:

Thanks (b)(6); (b)(7)(C)

From (b)(6); (b)(7)(C)

Sent: Thursday, September 14, 2017 10:26 AM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: TO 17 RGV (b)(6); (b)(7)(C) Floodwall Construction Project (b)(7)(E) Miles) 95% Submittal Package

Yes (b)(6); (b)(7)(C) I have (b)(6); (b)(7)(C) comments and plan to address the comments before the final RFP is released.

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Thursday, September 14, 2017 9:37:58 AM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: FW: TO 17 RGV (b)(7)(E) Floodwall Construction Project (b)(7)(E) Miles) 95% Submittal Package

(b)(6); (b)(7)(C)

It appears that 95% designs did not incorporate the 100% (b)(7)(E) tower designs that were provided to you. Please see (b)(6); (b)(7)(C) attached comments. Of particular concerns are:

(b) (5), (b) (7)(E)

Thanks,

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Wednesday, September 13, 2017 6:30 PM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: RE: TO 17 RGV (b)(7)(E) Floodwall Construction Project (b)(7)(E) Miles) 95% Submittal Package

(b)(6); (b)(7)(C) please find the attached review comments on floodwall 95% RFP and I may not be able to call in the meeting this Friday as I am traveling back from Brownsville to DC. I left a few comments from 65% RFP review into 95% RFP as these comments are still not resolved and addressed. Thanks. (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Monday, September 11, 2017 9:00 AM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: FW: TO 17 RGV (b)(7)(E) Floodwall Construction Project (b)(7)(E) Miles) 95% Submittal Package

Team,

Please see the link below for the 95% Submission on the RGV (b)(7)(E) Wall Project.

(b)(6); (b)(7)(C) P.E. LEED AP BD+C

Program Manager

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Mobile: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

From: (b)(6)

Sent: Monday, September 11, 2017 7:56 AM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b)(6)

(b)(6); (b)(7)(C)

(b)(6)

(b)(6); (b)(7)(C)

(b)(6)

Cc:

(b)(6)

(b)(6)

Subject: TO 17 RGV (b) (7)(E) Floodwall Construction Project (b) (7)(E) Miles) 95% Submittal Package

All,

The 95% RFP submittal for RGV (b) (7)(E) – Flood Wall Construction is available for your review and comment. You can download the RFP document, Drainage Reports, and HEC-RAS models by clicking the links below. The cross sections in the plan set are from the 65% submittal do to plotting issues. We will follow up with another email with the latest cross sections very soon.

RFP Document (includes plans, geotechnical):

(b) (7)(E)

Drainage Reports:

(b) (7)(E)

HEC-RAS models:

(b) (7)(E)

Please provide comments by COB 13 Sept 2017. Comments should be entered into Dr. Checks. If Dr. Checks is not available, you can enter your comments into the attached matrix and return to me by the deadline. 15 Sept 2017 is scheduled for the design review conference call. Details and number will follow.

USACE/CBP, please forward to stakeholders as you see fit.

Let me know if you have any questions or problems accessing the submittal.

Thank you,

(b) (6) PE | Civil Engineer III | Michael Baker International
1501 LBJ Fwy Suite 650 Dallas, TX 75234 | [O] 469-801-8521
(b) (6) www.mbakertnl.com

From:

To:

Cc:

(b)(6); (b)(7)(C)

Bcc:

Subject:
Package

FW: TO 17 RGV (b)(7)(E) Floodwall Construction Project (b)(7)(E) Miles) 95% Submittal

Date:

Thu Sep 14 2017 09:37:58 EDT

Attachments: RGV (b)(7)(E) Comments 95% (b)(6); (b)(7)(C) doc

(b)(6); (b)(7)(C)

It appears that 95% designs did not incorporate the 100% (b)(7)(E) tower designs that were provided to you. Please see (b)(6); (b)(7)(C) attached comments. Of particular concerns are:

(b) (5), (b) (7)(E)

(b) (5), (b) (7)(E)

Thanks,

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Wednesday, September 13, 2017 6:30 PM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: RE: TO 17 RGV (b)(7)(E) Floodwall Construction Project (b)(7)(E) Miles) 95% Submittal Package

(b)(6); (b)(7)(C) please find the attached review comments on floodwall 95% RFP and I may not be able to call in the meeting this Friday as I am traveling back from Brownsville to DC. I left a few comments from 65% RFP review into 95% RFP as these comments are still not resolved and addressed. Thanks. (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Monday, September 11, 2017 9:00 AM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: FW: TO 17 RGV (b)(7)(E) Floodwall Construction Project (b)(7)(E) Miles) 95% Submittal Package

Team,

Please see the link below for the 95% Submission on the RGV (b)(7)(E) Wall Project.

(b)(6); (b)(7)(C) P.E. LEED AP BD+C

Program Manager

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Mobile (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b) (6)

Sent: Monday, September 11, 2017 7:56 AM

To: (b)(6); (b)(7)(C)

(b) (6)

(b)(6); (b)(7)(C)

(b) (6)

(b)(6); (b)(7)(C)

(b) (6)
(b) (6)

Cc:

(b) (6)

(b) (6)

Subject: TO 17 RGV (b)(6) Floodwall Construction Project (b) (7)(E) Miles) 95% Submittal Package

All,

The 95% RFP submittal for RGV (b)(7)(E) Flood Wall Construction is available for your review and comment. You can download the RFP document, Drainage Reports, and HEC-RAS models by clicking the links below. The cross sections in the plan set are from the 65% submittal do to plotting issues. We will follow up with another email with the latest cross sections very soon.

RFP Document (includes plans, geotechnical):

(b) (7)(E)

Drainage Reports:

(b) (7)(E)

HEC-RAS models:

(b) (7)(E)

Please provide comments by COB 13 Sept 2017. Comments should be entered into Dr. Checks. If Dr. Checks is not available, you can enter your comments into the attached matrix and return to me by the deadline. 15 Sept 2017 is scheduled for the design review conference call. Details and number will follow.

USACE/CBP, please forward to stakeholders as you see fit.

Let me know if you have any questions or problems accessing the submittal.

Thank you,

(b) (6) | Civil Engineer III | Michael Baker International
1501 LBJ Fwy Suite 650 Dallas, TX 75234 | [O] 469-801-8521
(b) (6) | www.mbakertnl.com




US Army Corps
of Engineers

RFP REVIEW COMMENTS

(b) (5), (b) (7)(E)

(b) (5), (b) (7)(E)



From:

(b)(6); (b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: TO 17 RGV (b)(7)(E) Floodwall Construction Project (b)(7)(E) Miles) 95% Submittal Package

Date: Thu Sep 14 2017 08:56:40 EDT

Attachments:

thx

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Thursday, September 14, 2017 8:31 AM

To: (b)(6); (b)(7)(C)

Subject: RE: TO 17 RGV (b)(7)(E) Floodwall Construction Project (b)(7)(E) Miles) 95% Submittal Package

(b)(6); (b)(7)(C) does have some good points with the Baker design

(b) (5), (b) (7)(E)

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Thursday, September 14, 2017 7:58:40 AM

To: (b)(6); (b)(7)(C)

Subject: FW: TO 17 RGV (b)(7)(E) Floodwall Construction Project (b)(7)(E) Miles) 95% Submittal Package

What are the issues ?

From: (b)(6); (b)(7)(C)

Sent: Thursday, September 14, 2017 6:59:03 AM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: FW: TO 17 RGV (b)(7)(E) Floodwall Construction Project (b)(7)(E) Miles) 95% Submittal Package

(b)(6); (b)(7)(C) FYI. Plz note the engineering concerns (b)(7)(E)

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Chief Engineer and Lead Technical Authority (non-IT)

Office of Acquisition (Enterprise Services)

U.S. Customs and Border Protection (CBP)

1901 S. Bell St., Suite 827

Arlington VA 20598

Ofc: (b)(6); (b)(7)(C)

Cell:

Email: (b)(6); (b)(7)(C)

Note: The Contracting Officer is the sole individual authorized to make changes to the contract on behalf of the Government. The content of this email is not intended to change the existing scope of contract. If the Contractor considers any part of this communication to constitute a change in scope, the Contractor shall notify the Contracting Officer in accordance with FAR Clause 52.243-7, Notifications of Changes.

From: (b)(6); (b)(7)(C)

Sent: Wednesday, September 13, 2017 6:30 PM

To: (b)(6); (b)(7)(C)

Cc:

(b)(6); (b)(7)(C)

Subject: RE: TO 17 RGV (b)(7)(E) Floodwall Construction Project (b)(7)(E) Miles) 95% Submittal Package

(b)(6); (b)(7)(C) please find the attached review comments on floodwall 95% RFP and I may not be able to call in the meeting this Friday as I am traveling back from Brownsville to DC. I left a few comments from 65% RFP review into 95% RFP as these comments are still not resolved and addressed. Thanks. (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Monday, September 11, 2017 9:00 AM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: FW: TO 17 RGV (b)(7)(E) Floodwall Construction Project (b)(7)(E) Miles) 95% Submittal Package

Team,

Please see the link below for the 95% Submission on the RGV (b)(7)(E) Wall Project.

(b)(6); (b)(7)(C) P.E. LEED AP BD+C

Program Manager

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Mobile: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

From: (b) (6)

Sent: Monday, September 11, 2017 7:56 AM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b) (6)

(b) (6)
(b)(6); (b)(7)(C)
(b) (6)

(b) (6)

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)
(b) (6)

(b) (6)

Cc: (b) (6)

(b) (6)

Subject: TO 17 RGV- (b)(6) Floodwall Construction Project (b)(7)(E) Miles) 95% Submittal Package

All,

The 95% RFP submittal for RGV (b)(6) – Flood Wall Construction is available for your review and comment. You can download the RFP document, Drainage Reports, and HEC-RAS models by clicking the links below. The cross sections in the plan set are from the 65% submittal do to plotting issues. We will follow up with another email with the latest cross sections very soon.

RFP Document (includes plans, geotechnical):

(b) (7)(E)

Drainage Reports:

(b) (7)(E)

HEC-RAS models:

(b) (7)(E)

Please provide comments by COB 13 Sept 2017. Comments should be entered into Dr. Checks. If Dr. Checks is not available, you can enter your comments into the attached matrix and return to me by the deadline. 15 Sept 2017 is scheduled for the design review conference call. Details and number will follow.

USACE/CBP, please forward to stakeholders as you see fit.

Let me know if you have any questions or problems accessing the submittal.

Thank you,

(b) (6), PE | Civil Engineer III | Michael Baker International
1501 LBJ Fwy Suite 650 Dallas, TX 75234 | [O] 469-801-8521

(b) (6)

From:

(b)(6); (b)(7)(C)

To:

(b) (6)

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b) (6)

(b) (6)

(b)(6); (b)(7)(C)

(b) (6)

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b) (6)

Cc:

(b) (6)

Bcc:

Subject:

RE: TO 17 RGV (b)(7)(C) Floodwall Construction Project (b) (7)(E) Miles) 95% Submittal Package

Date:

Wed Sep 13 2017 16:14:06 EDT

Attachments:

RGV (b)(7)(C) Comments_95% (b)(6); (b)(7)(C) doc

(b)(6); (b)(7)(C)

My comments are reflected in the attached document. Please let me know if you have any questions.

Best,

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C) P.E., PMP, Chief Engineer

Border Patrol & Air and Marine (BPAM) PMO

LMI Contractor

Mobile: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

From: (b) (6)

Sent: Monday, September 11, 2017 7:56 AM

To:

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b) (6)

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)
(b) (6)

I

(b) (6)

(b)(6); (b)(7)(C)

(b) (6)

(b) (6)

Cc:

(b) (6)

(b) (6)

Subject: TO 17 RGV (b)(7)(E) Floodwall Construction Project (b)(7)(E) Miles) 95% Submittal Package

All,

The 95% RFP submittal for RGV (b)(7)(E) Flood Wall Construction is available for your review and comment. You can download the RFP document, Drainage Reports, and HEC-RAS models by clicking the links below. The cross sections in the plan set are from the 65% submittal do to plotting issues. We will follow up with another email with the latest cross sections very soon.

RFP Document (includes plans, geotechnical):

(b) (7)(E)

Drainage Reports:

(b) (7)(E)

HEC-RAS models:

(b) (7)(E)

Please provide comments by COB 13 Sept 2017. Comments should be entered into Dr. Checks. If Dr. Checks is not available, you can enter your comments into the attached matrix and return to me by the deadline. 15 Sept 2017 is scheduled for the design review conference call. Details and number will follow.

USACE/CBP, please forward to stakeholders as you see fit.

Let me know if you have any questions or problems accessing the submittal.

Thank you,

(b) (6) PE | Civil Engineer III | Michael Baker International
1501 LBJ Fwy Suite 650 Dallas, TX 75234 | [O] 469-801-8521
(b) (6) | www.mbakertnl.com



US Army Corps
of Engineers

RFP REVIEW COMMENTS

(b) (5), (b)(6); (b)(7)(C); (b)(7)(E)

(b) (5)

From:

(b)(6); (b)(7)(C)

To:

Cc:

Bcc:

Subject: FW: (b)(7)(E) Fence Replacement

Date: Wed Sep 13 2017 16:05:42 EDT

Attachments: image001.jpg

FYSA

(b)(6); (b)(7)(C) P.E., PMP, Chief Engineer

Border Patrol & Air and Marine (BPAM) PMO

LMI Contractor

Mobile (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Thursday, September 7, 2017 4:56 PM

To: (b)(6); (b)(7)(C)

Cc: (b)(6)

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: (b)(7)(E) Fence Replacement

(b)(6); (b)(7)(C)

I was in (b)(7)(E) on Wednesday and reviewed the RFP concept plans in the field. Overall they look great. The only potential substantive observations I had are:

(b) (5)

(b) (5)

Please let me know if you have any questions.

Best,

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Wednesday, September 6, 2017 5:55 PM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C) (b)(6); (b)(7)(C) (b)(6)

Subject: RE: (b) (7)(E) Crossing

Hi (b)(6); (b)(7)(C)

(b) (6) has a question that I am hoping you might be able to answer:

(b) (5), (b) (7)(E)

Thank you for your help.

Best Regards,

(b)(6); (b)(7)(C) PMP

Program Manager, Energy Initiatives

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management and Engineering

24000 Avila Road Suite 5020

Laguna Niguel, CA 92677

Office (b)(6); (b)(7)(C)

BB: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Excel as a trusted strategic partner enhancing Border Patrol's proud legacy

From: (b)(6); (b)(7)(C)

Sent: Wednesday, September 06, 2017 2:26 PM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C) (b)(6)

(b)(6) (b)(6); (b)(7)(C)

Subject: RE: (b)(7)(E) Crossing

Hi (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C) may be the best to obtain those answers on depth etc. (b)(5), (b)(7)(E)

Regards,

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Facilities and Infrastructure Manager, El Centro Sector
Border Patrol & Air and Marine Program Management Office
Facilities Management & Engineering

ELC Office (b)(6);(b)(7)(C)

Cel (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Excel as a trusted strategic partner enhancing Border Patrol's proud legacy.

From: (b)(6); (b)(7)(C)

Sent: Wednesday, September 06, 2017 1:21:13 PM

To:

Cc: (b)(6); (b)(7)(C)

Subject: RE: (b)(7)(E) Crossing

Hi (b)(6); (b)(7)(C)

Who would be the best person to answer (b)(6) question below?

Best Regards,

(b)(6); (b)(7)(C) PMP

Program Manager, Energy Initiatives

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management and Engineering

24000 Avila Road Suite 5020

Laguna Niguel, CA 92677

Office (b)(6); (b)(7)(C)

BB: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Excel as a trusted strategic partner enhancing Border Patrol's proud legacy

-----Original Message-----

From: (b)(6)

Sent: Wednesday, September 06, 2017 12:02 PM

To:

Cc: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: Re: (b)(7)(E) Crossing

(b)(6); (b)(7)(C) am asking about existing structure - can someone look at it?

Thank you

(b)(6)

----- Original Message -----

From: (b)(6); (b)(7)(C)

Sent: Wednesday, September 06, 2017 02:57 PM

To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: (b)(7)(E) Crossing

Good afternoon (b)(6)

I would refer to (b)(6); (b)(7)(C) the PM on the POE project. That was part of their construction effort.

Sorry I can't be of more help.

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Assistant Chief Patrol Agent

CONFIDENTIALITY: This email and attachments are intended for the above name only and are confidential. If you are not the intended addressee, or the person responsible for delivering it to the intended addressee, you may not copy, disseminate, or distribute it to anyone else or use it in any unauthorized manner. Doing so is strictly prohibited and may be unlawful. If you receive this email by mistake, please advise the sender immediately by using the reply function in your mail software and delete it from your computer.

-----Original Message-----

From: (b)(6)

Sent: Wednesday, September 6, 2017 11:54 AM

To:

(b)(6); (b)(7)(C)

Cc:

(b)(6); (b)(7)(C)

Subject: (b)(7)(E) Crossing

Hi

(b)(6); (b)(7)(C)

(b)(5)

(b)(5)

Thank you

(b)(6)

From:

(b)(6); (b)(7)(C)

To:

Cc:

Bcc:

Subject: FW: EPT (b)(7)(E) RF - El Paso Fence Replacement Project

Date: Wed Sep 13 2017 15:47:37 EDT

Attachments: image001.png

Below is my email with comments and station/sector's responses in red.

(b)(6); (b)(7)(C) P.E., PMP, Chief Engineer

Border Patrol & Air and Marine (BPAM) PMO

LMI Contractor

Mobile (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Tuesday, August 29, 2017 4:45 PM

To: (b)(6); (b)(7)(C)

Subject: FW: EPT (b)(7)(E) RF - El Paso Fence Replacement Project

Importance: High

(b)(6); (b)(7)(C)

Given the station's response, are we good to proceed? I had a talk with the station, and they understand the challenges associated with the (b)(7)(E). Everything else is in their comments.

V/R,

(b)(6); (b)(7)(C)

Operations Officer

El Paso Sector | Program Management Office

Office: (b)(6); (b)(7)(C)

iPhone: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Tuesday, August 29, 2017 10:54 AM

To:

(b)(6); (b)(7)(C)

(b)(6)

(b)(6)

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b)(6)

(b)(6); (b)(7)(C)

Subject: RE: EPT (b)(6); (b)(7)(C) RF - El Paso Fence Replacement Project

Good morning,

(b)(6); (b)(7)(C)

Station has provided comments in red below. Please let me know if there are any questions.

Thank you,

From: (b)(6); (b)(7)(C)

Sent: Tuesday, August 29, 2017 5:49 AM

To:

(b)(6)

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b)(6)

(b)(6)

(b)(6); (b)(7)(C)

Subject: RE: EPT (b)(6); (b)(7)(C) RF - El Paso Fence Replacement Project

All

Yesterday (b) (6) and myself conducted a comprehensive "plans-in-hand" review of the latest version of the 30% design. Our comments were annotated on drawings that we will distribute shortly (need to convert them to pdf). In the meantime, provided below is a summary of our observations. Baker is planning to update the drawings before they are released for bid later this week.

(b) (5), (b) (7)(E)

(b) (5), (b) (7)(E)

We can discuss the above on Thursday's call but we'd like feedback from Border Patrol on item #1 soonest.

Best,

(b)(6); (b)(7)(C)

-----Original Message-----

From: (b) (6)

Sent: Tuesday, August 22, 2017 12:23 PM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: FW: EPT (b)(6); (b)(7)(C) RF - El Paso Fence Replacement Project Corrected Final Submittal (UNCLASSIFIED)

CLASSIFICATION: UNCLASSIFIED

All,

Once you have reviewed the Corrected Final RFP from Michael Baker Corporation for the El Paso Replacement Fence Project please let me know what comments I can close out for you in the Draft 35% review and which have not been addressed and need to remain open.

Thanks,

(b) (6) PMP

Military and Operations Project Manager

USACE-ABQ District

4101 Jefferson Plaza

Albuquerque, NM 87109

Desk: (b) (6)

BB: (b) (6)

E-mail: (b) (6)

-----Original Message-----

From (b) (6)

Sent: Tuesday, August 22, 2017 12:18 AM

To: (b)(6); (b)(7)(C) (b) (6)
(b) (6) (b)(6); (b)(7)(C)
(b) (6) (b) (6)
(b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
(b) (6) (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
(b) (6) (b)(6); (b)(7)(C)

Cc (b) (6)

Subject: [Non-DoD Source] EPT (b) (7)(E) RF - El Paso Fence Replacement Project Corrected Final Submittal

All,

The Corrected Final RFP submittal for EPT (b) (7)(E) RF - El Paso Fence Replacement RFP is available. You can download the RFP document and HEC-RAS models and by clicking the links below.

RFP Document (includes plans, geotechnical and drainage reports):

(b) (7)(E)

HEC-RAS models:

(b) (7)(E)

Flowmaster Files:

(b) (7)(E)

Let me know if you have any questions or problems accessing the submittal.

Thank you,

(b) (6)

(b) (6) P.E., LEED-AP | Senior Associate | Michael Baker International
2929 N. Central Avenue, Suite 800 | Phoenix, AZ 85012 | d: (b) (6)
(b) (6) | Blockedwww.mbakerial.com
<Blockedhttp://www.mbakerial.com/>

<Blockedhttp://projects.mbakerial.com/sigimg/MBI-email-sig-block-72dpi.png> <Blockedhttp://projects.mbakerial.com/sigimg/MBI-email-sig-Base_72dpi.png>

CLASSIFICATION: UNCLASSIFIED

From:

(b)(6); (b)(7)(C)

To:

Cc:

Bcc:

Subject: FW: CCB Weekly Update

Date: Tue Sep 12 2017 12:54:34 EDT

Attachments: FY17 Project Change Control Board Brief 08312017 v2.pptx

<<FY17 Project Change Control Board Brief 08312017 v2.pptx>>

(b)(6); (b)(7)(C) PE

LMI Contractor

BPAM Chief Engineer

(b)(6); (b)(7)(C)

Sent from Samsung Galaxy

From: (b)(6); (b)(7)(C) on behalf of (b)(6); (b)(7)(C)

Sent: Tuesday, September 12, 2017 12:50:05 PM

To: (b)(6); (b)(7)(C)

Subject: CCB Weekly Update

When: Tuesday, September 12, 2017 1:00 PM-1:45 PM.

Where: NP Wall Room Phone: (b)(7)(E) Pin: (b)(7)(E)

Weekly Agenda

- Fiscal Health (b)(6); (b)(7)(C)
- Risks (b)(6); (b)(7)(C)
- Pending/Submitted CRs by Project
 - o San Diego (b)(6); (b)(7)(C)
 - o (b)(6); (b)(7)(C); (b)(7)(E)
 - o
 - o

FY17 Replacement Projects

Funding


Description	RWA/IAA	LI	Received	Obligations	Expenditures	Commitments	Available
FY18 Planning	HSBP1017X00059	(b) (5)					
FY17 Replacement	HSBP1017X00059						
RGV Gates	HSBP1017X00059						
Total	HSBP1017X00059						

Project Breakdown

Project	P2	Budget	On P2	Obligated	Expenditures	Commitments	Obligation %
SDC (b) (7)(E)	(b) (5), (b) (7)(E)						
ELC (b) (7)(E)							
EPT (b) (7)(E)							
EPT (b) (7)(E)							
Total							

Funding Received:	\$290,500,000
Project Budget (Total)	(b) (5)
CMR Available (Received – Project Budget):	
Pending CRs:	
Pending CRs (Options):	
Pending Risk:	

USBP Options

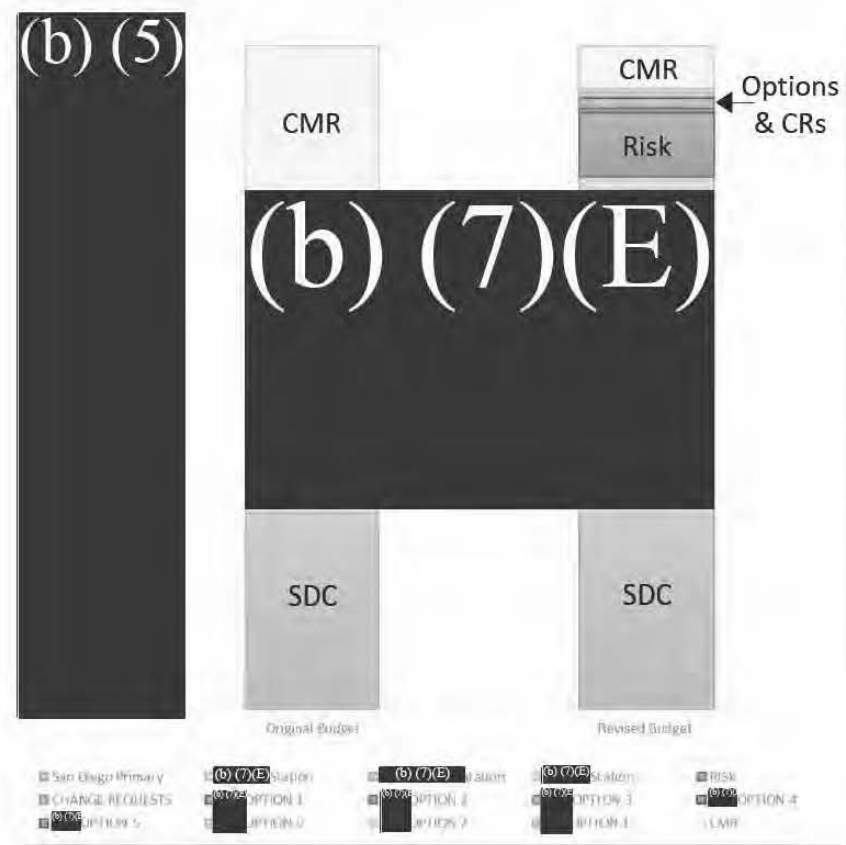

	Original Budget	Revised Budget	Balance
Funded Amount	\$ 290,500,000.00	\$ 290,500,000.00	\$ 290,500,000.00
San Diego Primary	\$		
(b) (7)(E) Station	\$		
(b) (7)(E) Station	\$		
(b) (7)(E) Station	\$		
Subtotal	\$		
Risk Remaining			
Pending Change Requests			
Subtotal	\$		
(b) (7)(E) Option 1 additional (b) (7)(E) miles			
(b) (7)(E) Option 2 (b) (7)(E)			
(b) (7)(E) Option 3 (b) (7)(E)			
(b) (7)(E) Option 4 (b) (7)(E)			
(b) (7)(E) Option 5 (b) (7)(E)			
(b) (7)(E) Option 6 (b) (7)(E)			
(b) (7)(E) Option 7 (b) (7)(E)			
(b) (7)(E) Option 1 (b) (7)(E)			
Subtotal	\$		
Change Management	\$		

SDC Replace Pedestrian Fence – 14 miles

Project	P2	Budget	On P2	Obligated	Expenditures	Commitments	Obligation %
SDC (b) (7)(E)				(b) (5)			

CR Summary:

Submission Date	Change Request Status	Description of Change	Change Requests
8/15/2017	Technical Review	(b) (5), (b) (7)(E)	
8/25/2017	Review		

Risk Change Summary:

Initial Risk Estimate	Risk Category	Current Risk Estimate
(b) (5)	Construction	\$ (b) (5)
	Contractor Performance	\$ (b) (5)
	Design	\$ (b) (5)
	Environmental	\$ (b) (5)
	External Entity Compliance	\$ (b) (5)
	Latent Conditions	\$ (b) (5)
	Real Estate	\$ (b) (5)
	Scope	\$ (b) (5)
	Grand Total	\$ (b) (5)

Construction Estimates:

(b) (5)

ELC (b) (7)(E) Replace Pedestrian Fence – (b) (7)(E) miles

Project	P2	Budget	On P2	Obligated	Expenditures	Commitments	Obligation %
ELC (b) (7)(E)				(b) (5)			

CR Summary:

Submission Date	Change Request Status	Description of Change	Change Requests
7/24/2017	Technical Review	(b) (5), (b) (7)(E)	

Risk Change Summary:

Initial Risk Estimate
(b) (5)

Risk Category	Current Risk Estimate
Construction	\$ (b) (5)
Contractor Performance	\$ (b) (5)
Design	\$ (b) (5)
Environmental	\$ (b) (5)
External Entity Compliance	\$ (b) (5)
Latent Conditions	\$ (b) (5)
Real Estate	\$ (b) (5)
Scope	\$ (b) (5)
Grand Total	\$ (b) (5)

Construction Estimates:

(b) (5)

EPT (b) (7)(E) Replace Vehicular Fence – (b) (7)(E) miles

Project	P2	Budget	On P2	Obligated	Expenditures	Commitments	Obligation %
EPT (b) (7)(E)				(b) (7)(E)			

CR Summary: *None*

Risk Change Summary:

Initial Risk Estimate	Risk Category	Current Risk Estimate
\$ (b) (7)(E)	Construction	\$ (b) (5)
	Contractor Performance	\$ (b) (5)
	Design	\$ (b) (5)
	Environmental	\$ (b) (5)
	External Entity Compliance	\$ (b) (5)
	Latent Conditions	\$ (b) (5)
	Real Estate	\$ (b) (5)
	Scope	\$ (b) (5)
	Grand Total	\$ (b) (5)

Construction Estimates:

(b) (5)

EPT (b) (7)(E) Replace Pedestrian Fence – (b) (7)(E) miles

Project	P2	Budget	On P2	Obligated	Expenditures	Commitments	Obligation %
EPT (b) (7)(E)				(b) (5)			

CR Summary:

Submission Date	Change Request Status	Description of Change	Change Requests
8/14/2017	Review	(b) (5), (b) (7)(E)	
8/14/2017	Draft		

Risk Change Summary:

Initial Risk Estimate	Risk Category	Current Risk Estimate
(b) (5)	Construction	\$ (b) (5)
	Contractor Performance	\$ (b) (5)
	Design	\$ (b) (5)
	Environmental	\$ (b) (5)
	External Entity Compliance	\$ (b) (5)
	Latent Conditions	\$ (b) (5)
	Real Estate	\$ (b) (5)
	Scope	\$ (b) (5)
	Grand Total	\$ (b) (5)

Construction Estimates:

(b) (5)

From:

(b)(6); (b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: Change control board

Date: Tue Sep 12 2017 12:51:22 EDT

Attachments:

Added.

(b)(6); (b)(7)(C)

-----Original Message-----

From: (b)(6); (b)(7)(C)

Sent: Tuesday, September 12, 2017 12:47 PM

To:

(b)(6); (b)(7)(C)

Cc:

Subject: Change control board

(b)(6); (b)(7)(C) -can I get invited to the CCB meetings for the wall?

Thanks

(b)(6); (b)(7)(C) PE

LMI Contractor

BPAM Chief Engineer

(b)(6); (b)(7)(C)

Sent from Samsung Galaxy

From:

(b)(6); (b)(7)(C)

To:

Cc:

Bcc:

Subject: FW: Meet & greet w/ LMI's new CEO (b) (6)

Date: Tue Sep 12 2017 11:10:19 EDT

Attachments: image001.png
image002.gif
image003.gif
image004.gif

The 19th is one of the days (b) (6) wants you to travel to El Paso. Still waiting on specifics from him. Want me to schedule this anyways?

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Tuesday, September 12, 2017 11:08 AM

To:

(b)(6); (b)(7)(C)

Cc:

Subject: RE: Meet & greet w/ LMI's new CEO (b) (6)

Hi (b)(6); (b)(7)(C) says he isn't traveling and is available to meet (b) (6) Can we get this meeting on Karl and (b)(6);(b)(7)(C) calendar for 9:15-9:45 am on Sept 19th and meet in Karl's conference room?

Much appreciated!

(b) (6), (b) (7)(C)

From: (b)(6); (b)(7)(C)

Sent: Friday, September 8, 2017 11:24 AM

To: CALVO, KARL H. (b)(6); (b)(7)(C)

Cc:

(b)(6); (b)(7)(C)

Subject: [EXTERNAL] RE: Meet & greet w/ LMI's new CEO (b) (6)

Good morning (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C) has potential travel on the 19th, but I need to confirm with him when he returns from leave. I will get back to you after speaking with him.

(b)(6); (b)(7)(C)

From: CALVO, KARL H.

Sent: Friday, September 08, 2017 11:14 AM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: RE: Meet & greet w/ LMI's new CEO (b) (6)

(b)(6); (b)(7)(C)

(b) (6) is my EA. Sept 19th could work for me. Thx.

From: (b)(6); (b)(7)(C)

Sent: Friday, September 08, 2017 11:05:17 AM

To: (b)(6); (b)(7)(C) CALVO, KARL H.

Subject: Meet & greet w/ LMI's new CEO (b) (6)

Karl (b)(6); (b)(7)(C)

LMI has a new CEO named (b) (6). He started on Sept 1st and is anxious to meet our staff and customers. He is hosting a meeting with LMI/DC employees on the morning of Sept 19th at the City Club and I was wondering if there was any way I could bring him over to National Place around 9 am and have him meet you two for no than 30 minutes. Please let me know if you can do it (Karl-I don't know your AA so sorry for going direct to you.)

Thanks

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C) PE

Program Director, Infrastructure, Energy & Environment

7940 Jones Branch Drive, Tysons, VA 22102

Office (b)(6); (b)(7)(C) | Cell: (b)(6); (b)(7)(C)

Learn more at www.lmi.org or follow us on: | |

From:

(b)(6); (b)(7)(C)

To:

[Redacted]

(b) (6)

(b) (6) (b)(6); (b)(7)(C)

(b) (6)

(b)(6); (b)(7)(C)

Cc:

Bcc:

Subject: RE: CCB Weekly Update

Date: Tue Sep 12 2017 10:01:50 EDT

Attachments: FY17 Project Change Control Board Brief 08312017 v2.pdf

Some folks are having issues with the PPT so here it is in PDF <<FY17 Project Change Control Board

(b)(6); (b)(7)(C)

Chief, Portfolio Management and Analysis (PMA) Branch

Border Patrol & Air and Marine Program Management Office

Mobile: (b)(6); (b)(7)(C)

Office: (b)(6); (b)(7)(C)

(b) (7)(E)

From: (b)(6); (b)(7)(C)

Sent: Monday, September 11, 2017 7:49 PM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b) (6)

(b)(6); (b)(7)(C)

(b) (6)
(b)(6); (b)(7)(C)

Subject: RE: CCB Weekly Update

Hello everyone,

Since we haven't had any new CRs and we haven't received a new budget update (every 2 weeks), please use the same report I sent last week for tomorrow's meeting.

Thanks! << File: FY17 Project Change Control Board Brief 08312017 v2.pptx >>

(b)(6); (b)(7)(C)

Chief, Portfolio Management and Analysis (PMA) Branch

Border Patrol & Air and Marine Program Management Office

Mobile: (b)(6); (b)(7)(C)

Office: (b)(6); (b)(7)(C)

(b) (7)(E)

-----Original Appointment-----

From: (b)(6); (b)(7)(C)

Sent: Wednesday, August 16, 2017 10:05 AM

To:

(b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)

(b) (6)

(b) (6)
(b)(6); (b)(7)(C) (b) (6)
(b)(6); (b)(7)(C)

Subject: CCB Weekly Update

When: Tuesday, September 12, 2017 1:00 PM-2:30 PM (UTC-05:00) Eastern Time (US & Canada).

Where: NP Wall Room Phone (b) (7)(E) Pin (b) (7)(E)

Weekly Agenda

- * Fiscal Health (b)(6); (b)(7)(C)
- * Risks (b)(6); (b)(7)(C)
- * Pending/Submitted CRs by Project
 - o San Diego (b)(6); (b)(7)(C)
 - o (b)(6); (b)(7)(C); (b)(7)(E)
 - o [REDACTED]
 - o [REDACTED]

FY17 Replacement Projects

Funding


Description	RWA/IAA	LI	Received	Obligations	Expenditures	Commitments	Available
FY18 Planning	HSBP1017X00059	(b) (5)					
FY17 Replacement	HSBP1017X00059						
RGV Gates	HSBP1017X00059						
Total	HSBP1017X00059						

Project Breakdown

Project	P2	Budget	On P2	Obligated	Expenditures	Commitments	Obligation %
SDC (b) (7)(E)	(b) (5), (b) (7)(E)						
ELC (b) (7)(E)							
EPT (b) (7)(E)							
EPT (b) (7)(E)							
Total							

Funding Received:	\$290,500,000
Project Budget (Total)	(b) (5)
CMR Available (Received – Project Budget):	
Pending CRs:	
Pending CRs (Options):	
Pending Risk:	

USBP Options

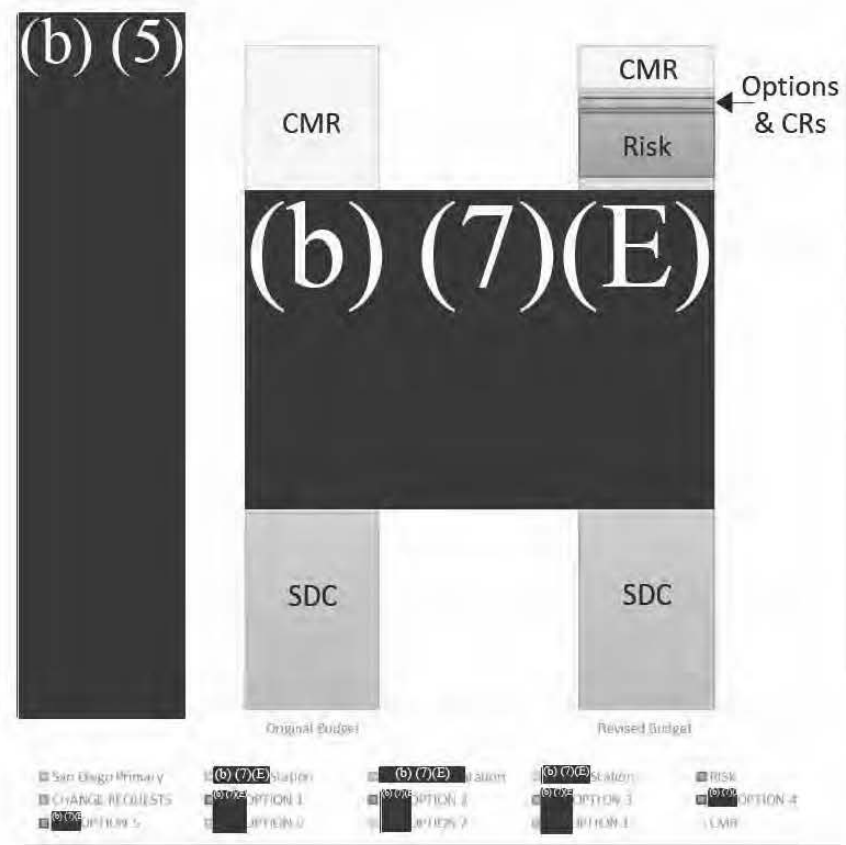

	Original Budget	Revised Budget	Balance
Funded Amount	\$ 290,500 000.00	\$ 290,500,000.00	\$ 290,500,000.00
San Diego Primary	\$	(b) (5)	
(b) (7)(E) Station	\$		
(b) (7)(E) Station	\$		
(b) (7)(E) Station	\$		
Subtotal	\$		
Risk Remaining			
Pending Change Requests			
Subtotal	\$		
(b) (7)(E) Option 1 additional (b) (7)(E) miles			
(b) (7)(E) Option 2 (b) (7)(E)			
(b) (7)(E) Option 3 (b) (7)(E)			
(b) (7)(E) Option 4 (b) (7)(E)			
(b) (7)(E) Option 5 (b) (7)(E)			
(b) (7)(E) Option 6 (b) (7)(E)			
(b) (7)(E) Option 7 (b) (7)(E)			
(b) (7)(E) Option 1 (b) (7)(E)			
Subtotal	\$		
Change Management	\$		

Note: Chart is pending input for (b) (7)(E) and SDC options (b) (7)(E) Options 4 and 6 are pending revision.

BW23 FOIA CBP 011822

SDC Replace Pedestrian Fence – 14 miles

Project	P2	Budget	On P2	Obligated	Expenditures	Commitments	Obligation %
SDC (b) (7)(E)				(b) (5)			

CR Summary:

Submission Date	Change Request Status	Description of Change	Change Requests
8/15/2017	Technical Review	(b) (5), (b) (7)(E)	
8/25/2017	Review		

Risk Change Summary:

Initial Risk Estimate	Risk Category	Current Risk Estimate
(b) (5)	Construction	\$ (b) (5)
	Contractor Performance	\$ (b) (5)
	Design	\$ (b) (5)
	Environmental	\$ (b) (5)
	External Entity Compliance	\$ (b) (5)
	Latent Conditions	\$ (b) (5)
	Real Estate	\$ (b) (5)
	Scope	\$ (b) (5)
	Grand Total	\$ (b) (5)

Construction Estimates:

(b) (5)

ELC (b) (7)(E) Replace Pedestrian Fence – (b) (7)(E) miles

Project	P2	Budget	On P2	Obligated	Expenditures	Commitments	Obligation %
ELC (b) (7)(E)				(b) (5)			

CR Summary:

Submission Date	Change Request Status	Description of Change	Change Requests
7/24/2017	Technical Review	(b) (5), (b) (7)(E)	

Risk Change Summary:

Initial Risk Estimate
(b) (5)

Risk Category	Current Risk Estimate
Construction	\$ (b) (5)
Contractor Performance	\$ (b) (5)
Design	\$ (b) (5)
Environmental	\$ (b) (5)
External Entity Compliance	\$ (b) (5)
Latent Conditions	\$ (b) (5)
Real Estate	\$ (b) (5)
Scope	\$ (b) (5)
Grand Total	\$ (b) (5)

Construction Estimates:

(b) (5)

EPT (b) (7)(E) Replace Vehicular Fence – (b) (7)(E) miles

Project	P2	Budget	On P2	Obligated	Expenditures	Commitments	Obligation %
EPT (b) (7)(E)				(b) (7)(E)			

CR Summary: *None*

Risk Change Summary:

Initial Risk Estimate	Risk Category	Current Risk Estimate
\$ (b) (7)(E)	Construction	\$ (b) (5)
	Contractor Performance	\$ (b) (5)
	Design	\$ (b) (5)
	Environmental	\$ (b) (5)
	External Entity Compliance	\$ (b) (5)
	Latent Conditions	\$ (b) (5)
	Real Estate	\$ (b) (5)
	Scope	\$ (b) (5)
	Grand Total	\$ (b) (5)

Construction Estimates:

(b) (5)

EPT (b) (7)(E) Replace Pedestrian Fence – (b) (7)(E) miles

Project	P2	Budget	On P2	Obligated	Expenditures	Commitments	Obligation %
EPT (b) (7)(E)				(b) (5)			

CR Summary:

Submission Date	Change Request Status	Description of Change	Change Requests
8/14/2017	Review	(b) (5), (b) (7)(E)	
8/14/2017	Draft		

Risk Change Summary:

Initial Risk Estimate	Risk Category	Current Risk Estimate
(b) (5)	Construction	\$ (b) (5)
	Contractor Performance	\$ (b) (5)
	Design	\$ (b) (5)
	Environmental	\$ (b) (5)
	External Entity Compliance	\$ (b) (5)
	Latent Conditions	\$ (b) (5)
	Real Estate	\$ (b) (5)
	Scope	\$ (b) (5)
	Grand Total	\$ (b) (5)

Construction Estimates:

(b) (5)

From:

(b)(6); (b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: Initial Draft SELC TP

Date: Tue Sep 12 2017 08:12:35 EDT

Attachments:

Thank you (b)(6); (b)(7)(C)

Working w OA to obtain the editable version.

More to follow,

(b)(6); (b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6); (b)(7)(C)

Cell: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b)(6); (b)(7)(C)
Sent: Monday, September 11, 2017 9:48 AM
To: (b)(6); (b)(7)(C)

Subject: RE: Initial Draft SELC TP

All,

Attached is my first pass at completing the tailored SELC plan for the Border Wall System Program. Please note that we need to get an "editable" version of Figure 14 of the guidelines to tailor the required graphic for our plan. Please send to me when available and I'll modify.

Please let me know if you have any questions.

Best,

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C) P.E., PMP, Chief Engineer

Border Patrol & Air and Marine (BPAM) PMO

LMI Contractor

Mobile: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, August 8, 2017 4:19 PM
To: (b)(6); (b)(7)(C)
Subject: FW: Initial Draft SELC TP

Hey (b)(6); (b)(7)(C)

So attached word document is nothing but a “shell”

Only incorporated program scope, very basic.

But we can clean up as we go and add language from other documents to tailor.

Does this at a min. get the ball rolling?

(b)(6); (b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6); (b)(7)(C)

Cell: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b) (7)(E)

From (b)(6); (b)(7)(C)
Sent: Thursday, July 27, 2

From:

To:

Cc:

(b)(6); (b)(7)(C)

Bcc:

Subject: RE: Mr. Calvo Prototype Meeting Talking Points

Date: Mon Sep 11 2017 15:45:48 EDT

Attachments:

Great – got it, thank you.

(b)(6); (b)(7)(C) – Can you attach to the invite please? 1pm EST tomorrow.

(b)(6); (b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Monday, September 11, 2017 3:45 PM

To:

Cc:

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: Mr. Calvo Prototype Meeting Talking Points

(b)(6); (b)(7)(C)

Here are the talking point we can go through tomorrow:

***** Project Planning / Execution

***** Kickoff Meetings

***** Contractor Submittal Review

***** Notice to Proceed

***** Period Of Performance Begins

***** Site Hours of Operation

***** Daily Tailgate Meetings

***** Site Safety

***** Daily Contract Management

Respectfully,

(b)(6); (b)(7)(C)

Eastern Corridors Division Director

Border Patrol and Air Marine Operations Program Management Office

Facilities Management and Engineering

Mobile: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

From:

To:

Cc:

Bcc:

Subject: RE: NTP Meetings

Date: Mon Sep 11 2017 15:44:47 EDT

Attachments: Concrete Prototype Kickoff Meeting.docx

Agenda is attached. Key takeaways are as follows:

- The official kick off meeting is a contractual obligation that must take place before the project begins.
- Attendees included: BPAM PMO, USBP, Procurement and the selected companies.
- Project definition, requirements and roles and responsibilities were discussed, including that only the Project Management team can give direction to the selected companies and their personnel.
- After the formal meeting, a site visit took place to allow the selected companies the opportunity to see the location where they will be constructing the prototypes.
- During the site visit, it was discussed that the north areas of the prototype site (private land) will be completely fenced off by the Sheriff's Department to keep protestors off the private property and also to ensure no protestors can gain access to the construction site.
- The contract kick off for 'other materials' is still on schedule for September 18.
- Construction for both, concrete and 'other', is still on schedule for September 26.

(b)(6); (b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Monday, September 11, 2017 2:16 PM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: RE: NTP Meetings

Actually, I'm going to defer to (b)(6); (b)(7)(C) on this one on how she wants to handle. For future, all these asks will go to her to keep me out of the middle.

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Monday, September 11, 2017 2:14 PM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: RE: NTP Meetings

(b)(6); (b)(7)(C)

How about a phone call to walk you through.

We could be available in an hour.

From: (b)(6); (b)(7)(C)

Sent: Monday, September 11, 2017 2:07:27 PM

To: (b)(6); (b)(7)(C)

Cc:

Subject: FW: NTP Meetings

Since she's looking for something for C1 today, I think we can feed the beast if someone can just send me the agenda. We'll still need to provide a read out on the meeting, but if one of you can just ship me the agenda for the kick-off meeting, I can use that to buy us until tomorrow on the read out.

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

From: CALVO, KARL H.

Sent: Monday, September 11, 2017 10:15 AM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: FW: NTP Meetings

(b)(6); (b)(7)(C)

Can you provide me an update by COB today wrt your prototype site/ NTP meetings (when/ where) for both concrete and other? Agenda highlights would also be helpful. Thx.

Karl H. Calvo, CFM, PMP

Assistant Commissioner

Office of Facilities & Asset Management

(b)(6); (b)(7)(C) (cell)

From: KOLBE, KATHRYN

Sent: Monday, September 11, 2017 10:11 AM

To: CALVO, KARL H. (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: NTP Meetings

Karl/ (b)(6); (b)(7)(C) When & where are the NTP meetings this week with the prototype companies?

Appreciate a detailed readout when complete. Thank you...VR, KK

Kathryn L. Kolbe

Executive Assistant Commissioner

Enterprise Services

U.S. Customs and Border Protection

Office (b)(6); (b)(7)(C)

Cell (b)(6); (b)(7)(C)

Concrete Prototype Kickoff Meeting

(b) (7)(E)

Agenda:

9:00	Introductions
9:05	Contracting Officer's Comments
9:20	Project Manager's Comments
9:45	Border Patrol and Law Enforcement Comments
10:00	Project Director's Expectations
10:10	Contracting Officer's Representative's Comments
10:15	Questions

From:

(b)(6); (b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: NTP Meetings

Date: Mon Sep 11 2017 14:20:36 EDT

Attachments:

Cool beans. Will be back at Pogo Row in an hourish.

From: (b)(6); (b)(7)(C)

Sent: Monday, September 11, 2017 2:18:03 PM

To:

(b)(6); (b)(7)(C)

Cc:

Subject: RE: NTP Meetings

(b)(6); (b)(7)(C) – Just give me a ring when you guys have a free sec.

(b)(6); (b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Monday, September 11, 2017 2:16 PM

To:

(b)(6); (b)(7)(C)

Cc:

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)
Subject: RE: NTP Meetings

Actually, I'm going to defer to (b)(6); (b)(7)(C) on this one on how she wants to handle. For future, all these asks will go to her to keep me out of the middle.

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Monday, September 11, 2017 2:14 PM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: NTP Meetings

(b)(6); (b)(7)(C)

How about a phone call to walk you through.

We could be available in an hour.

From: (b)(6); (b)(7)(C)
Sent: Monday, September 11, 2017 2:07:27 PM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: FW: NTP Meetings

Since she's looking for something for C1 today, I think we can feed the beast if someone can just send me the agenda. We'll still need to provide a read out on the meeting, but if one of you can just ship me the agenda for the kick-off meeting, I can use that to buy us until tomorrow on the read out.

(b)(6); (b)(7)(C)

From: CALVO, KARL H.
Sent: Monday, September 11, 2017 10:15 AM

To: [REDACTED] (b)(6); (b)(7)(C)

Cc: [REDACTED] (b)(6); (b)(7)(C)

Subject: FW: NTP Meetings

[REDACTED] (b)(6); (b)(7)(C)

Can you provide me an update by COB today wrt your prototype site/ NTP meetings (when/ where) for both concrete and other? Agenda highlights would also be helpful. Thx.

Karl H. Calvo, CFM, PMP

Assistant Commissioner

Office of Facilities & Asset Management

[REDACTED] (b)(6); (b)(7)(C) (cell)

From: KOLBE, KATHRYN

Sent: Monday, September 11, 2017 10:11 AM

To: CALVO, KARL H. [REDACTED] (b)(6); (b)(7)(C)

[REDACTED] (b)(6); (b)(7)(C)

Subject: NTP Meetings

Kar [REDACTED] (b)(6); (b)(7)(C) When & where are the NTP meetings this week with the prototype companies?

Appreciate a detailed readout when complete. Thank you...VR, KK

Kathryn L. Kolbe

Executive Assistant Commissioner

Enterprise Services

U.S. Customs and Border Protection

Office [REDACTED] (b)(6); (b)(7)(C)

Cell (b)(6); (b)(7)(C)

From:

(b)(6); (b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: NTP Meetings

Date: Mon Sep 11 2017 14:19:41 EDT

Attachments:

OK

We are here to help, was thinking it would be easier with a phone call.

From: (b)(6); (b)(7)(C)

Sent: Monday, September 11, 2017 2:16:02 PM

To: (b)(6); (b)(7)(C)

Cc:

Subject: RE: NTP Meetings

Actually, I'm going to defer to (b)(6); (b)(7)(C) on this one on how she wants to handle. For future, all these asks will go to her to keep me out of the middle.

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Monday, September 11, 2017 2:14 PM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: RE: NTP Meetings

(b)(6); (b)(7)(C)

How about a phone call to walk you through.

We could be available in an hour.

From: (b)(6); (b)(7)(C)
Sent: Monday, September 11, 2017 2:07:27 PM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: FW: NTP Meetings

Since she's looking for something for C1 today, I think we can feed the beast if someone can just send me the agenda. We'll still need to provide a read out on the meeting, but if one of you can just ship me the agenda for the kick-off meeting, I can use that to buy us until tomorrow on the read out.

(b)(6); (b)(7)(C)

From: CALVO, KARL H.
Sent: Monday, September 11, 2017 10:15 AM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: FW: NTP Meetings

(b)(6); (b)(7)(C)

Can you provide me an update by COB today wrt your prototype site/ NTP meetings (when/ where) for both concrete and other? Agenda highlights would also be helpful. Thx.

Karl H. Calvo, CFM, PMP

Assistant Commissioner

Office of Facilities & Asset Management

(b)(6); (b)(7)(C) (cell)

From: KOLBE, KATHRYN

Sent: Monday, September 11, 2017 10:11 AM

To: CALVO, KARL H. (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: NTP Meetings

Karl (b)(6); (b)(7)(C) When & where are the NTP meetings this week with the prototype companies?

Appreciate a detailed readout when complete. Thank you...VR, KK

Kathryn L. Kolbe

Executive Assistant Commissioner

Enterprise Services

U.S. Customs and Border Protection

Office (b)(6); (b)(7)(C)

Cell (b)(6); (b)(7)(C)

From:

To:

Cc:

Bcc:

Subject: RE: T&E Deck for IPT
Date: Mon Sep 11 2017 11:43:21 EDT
Attachments:

Great news

From: (b)(6); (b)(7)(C)
Sent: Monday, September 11, 2017 11:02:32 AM
To: (b)(6); (b)(7)(C)
Cc:
Subject: FW: T&E Deck for IPT

Confirmed – (b)(6); (b)(7)(C) is presenting

(b)(6); (b)(7)(C)
Director, Business Operations Division
Border Patrol & Air and Marine Program Management Office
Facilities Management and Engineering
Office of Facilities and Asset Management
Mobile: (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Monday, September 11, 2017 11:00 AM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: T&E Deck for IPT

(b)(6); (b)(7)(C)

Good morning... yes I can submit my final deck by noon tomorrow, Tuesday, 9/12.

OS will be briefing, specifically me. I reside in OS > PARE > CRD > LSOTA.

Thank you and let me know if there is anything else you need.

r/

(b)(6); (b)(7)(C)

MITRE/LSOTA

(b)(6); (b)(7)(C)(O)
(M)

From: (b)(6); (b)(7)(C)

Sent: Monday, September 11, 2017 10:46 AM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: T&E Deck for IPT

(b)(6); (b)(7)(C)

I'm consolidating the IPT slides for Thursday's meeting. Can you please submit your final deck by noon tomorrow (Tuesday)?

EAC Kolbe requests that we submit these ahead of time. We'll keep your deck separate and we're happy to bring along copies for the attendees.

Also, we're assuming that this will be briefed by OS, correct?

Thanks,

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Special Projects Analyst

Agile Group

Office of Facilities and Asset Management

U.S. Customs and Border Protection

Mobile: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Thursday, September 07, 2017 3:44 PM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: FW: 20170907_Border Wall T&E Strategy_no backup_FOUC.pptx

FYI

(b)(6); (b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b) (7)(E)

From:

(b)(6); (b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: Initial Draft SELC TP

Date: Mon Sep 11 2017 09:47:32 EDT

Attachments: DHS SELC_Project_Tailoring_Plan_Border Wall System.doc

All,

Attached is my first pass at completing the tailored SELC plan for the Border Wall System Program. Please note that we need to get an "editable" version of Figure 14 of the guidelines to tailor the required graphic for our plan. Please send to me when available and I'll modify.

Please let me know if you have any questions.

Best,

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C) P.E., PMP, Chief Engineer

Border Patrol & Air and Marine (BPAM) PMO

LMI Contractor

Mobile (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Tuesday, August 8, 2017 4:19 PM

To: (b)(6); (b)(7)(C)

Subject: FW: Initial Draft SELC TP

Hey (b)(6); (b)(7)(C)

So attached word document is nothing but a “shell”

Only incorporated program scope, very basic.

But we can clean up as we go and add language from other documents to tailor.

Does this at a min. get the ball rolling?

(b)(6); (b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6); (b)(7)(C)

Cell: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b) (7)(E)

From: (b)(6); (b)(7)(C)
Sent: Thursday, July 27, 2

Border Wall System Program

SELC TAILORING PLAN



DEPARTMENT OF HOMELAND SECURITY

Border Wall System Program (BWS P)

~~For Official Use Only (FOFU)~~

Doc No:

08/08/2017

Developed By:

Border Patrol Air & Marine Program Management Office (BPAM),
Facilities Management & Engineering (FM&E)
1331 Pennsylvania Ave NW
Washington DC 20002

UNCLASSIFIED / ~~FOUO~~

BW23 FOIA CBP 011848

(b) (5)

0. Revision History

Revision Number	Revision Date	Changes
1.0	08/08/2017	

SELC Tailoring Plan Template
Signature Page

[REDACTED] System Program

Submitted By: _____

(b)(6); (b)(7)(C) Date
Program Manager, Acquisition Program
Manager

Endorsed By: _____

Chief Scott Luck Date
Lead Business Authority

Approved By: _____

(b)(6); (b)(7)(C) Date
Lead Technical Authority (Non- IT)

Approved By: _____

Mark S. Borkowski Date
Component Acquisition Executive

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

From:

(b)(6); (b)(7)(C)

To:

Cc:

Bcc:

Subject: FW: FM&E Priority 1 Audit: GAO's 2018 Assessment of Select DHS Acquisition Programs (101940) - Wall

Date: Mon Sep 11 2017 08:40:15 EDT

Attachments: G2.20_Mod_Signed.pdf

FYSA – HH mod to the contract.

(b)(6); (b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Friday, September 08, 2017 4:28 PM

To:

(b)(6); (b)(7)(C)

Subject: RE: FM&E Priority 1 Audit: GAO's 2018 Assessment of Select DHS Acquisition Programs (101940) - Wall

Attached is the A/E Baker contract awarded yesterday by USACE.

(b)(6); (b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6); (b)(7)(C)

Cell: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

[Click Here](#) to view the FMB team listed with areas of responsibility.

[Click Here](#) to view the PRR tracker.

[Click Here](#) to view the IAA Tracker

From: (b)(6); (b)(7)(C)

Sent: Thursday, September 07, 2017 4:11 PM

To: BPAM PMO TASKS (b)(7)(E) | (b)(6); (b)(7)(C)

Subject: RE: FM&E Priority 1 Audit: GAO's 2018 Assessment of Select DHS Acquisition Programs (101940) - Wall

Womp Womp

- Slide deck from the ARB presentation that served as the Capability Development Plan BPAM (check with (b)(6); (b)(7)(C) - attached)
- Acquisition Plan, once approved BPAM (check with (b)(6); (b)(7)(C) - under internal review, attached should have NLT 9/15)
- Copies of any contract awards, once made, including (just awarded today, email attached. Requested documents from procurement 9/7)
 - o RGV hydraulic study, expected in August BPAM- (pending response from USACE. Should have NLT 9/20)

(b)(6); (b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6); (b)(7)(C)

Cell: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

[Click Here](#) to view the FMB team listed with areas of responsibility.

[Click Here](#) to view the PRR tracker.

[Click Here](#) to view the IAA Tracker

From: (b)(6); (b)(7)(C) On Behalf Of BPAM PMO TASKS

Sent: Thursday, September 07, 2017 4:01 PM

To: (b)(6); (b)(7)(C)

Subject: FW: FM&E Priority 1 Audit: GAO's 2018 Assessment of Select DHS Acquisition Programs (101940) - Wall

Hi All,

Shortly after this task was assigned we received notice it would be postponed. We just got word this deliverable is still active. As it turns out, only part of the request was pushed out to the end of FY17 (the staffing plan assessment). Audit is still looking for the remaining items, listed below, per the email thread below. OFAM is requesting documents referenced below in red. If the signed document is not available, please provide an ETA that I can pass along.

- Slide deck from the ARB presentation that served as the Capability Development Plan BPAM (check with (b)(6); (b)(7)(C))
- Acquisition Plan, once approved BPAM (check with (b)(6); (b)(7)(C))
- Copies of any contract awards, once made, including (but not limited to)
 - o RGV hydraulic study, expected in August BPAM

Let me know if you have any questions!

Thanks,

(b)(6); (b)(7)(C)

Communications Specialist, Business Operations Division

Strategic Analysis, Inc.

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Mobile: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Excel as a trusted strategic partner enhancing Border Patrol's proud legacy.

From: OFAM-TASKINGS

Sent: Thursday, September 07, 2017 3:29 PM

To: FMEEXECSUPPORT (b) (7)(E) BPAM PMO TASKS

(b) (7)(E)

Cc

(b)(6); (b)(7)(C)

(b) (7)(E)

Subject: RE: FM&E Priority 1 Audit: GAO's 2018 Assessment of Select DHS Acquisition Programs (101940) - Wall

FME/BPAM,

Update to my previous email- I checked w/ (b)(6); (b)(7)(C) and most of the items on this list are not ours. Please provide the documents where referenced in RED below. If the signed document is not available please provide an ETA. Thank you!!

- Impedance and Denial Capability Analysis Report (CAR) and Mission Need Statement (MSN) (March 16,2017) USBP
- JRC's response to the Impedance and Denial CAR and MNS USBP
- Copies of the Requests for Proposals and Solicitations for the Prototypes OA
- Slide deck from the ARB presentation that served as the Capability Development Plan BPAM (check with (b)(6); (b)(7)(C))
- Current organizational chart OES/HRM? (not OFAM)
- A point of contact for the DHS study in response to the Executive Order DHS USM Office
- Acquisition Plan, once approved BPAM (check with (b)(6); (b)(7)(C))
- Border Patrol analysis of prioritization of wall segments – expected at the end of August or early September USBP
- Staffing plan – once signed by the CAE (OA will forward the plans to GAO as they are signed.)
- Copies of any contract awards, once made, including (but not limited to)
 - o Prototyping, expected end of Aug/early Sept pending bid protest result OA
 - o RGV hydraulic study, expected in August BPAM

(b)(6); (b)(7)(C)

Senior Task Manager

Agile Group

Office of Facilities and Asset Management

U.S. Customs and Border Protection

Mobile: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

From: OFAM-TASKINGS

Sent: Thursday, September 07, 2017 10:50 AM

To: (b)(6); (b)(7)(C) FMEEEXECSUPPORT
(b) (7)(E)

Cc: OFAM-TASKINGS (b) (7)(E); (b)(6);(b)(7)(C) (b)(6); (b)(7)(C)
OFAM Business Operations Program Accountability Executive Support (b) (7)(E)
OFAM Business Operations Executive Support (b) (7)(E)
Subject: RE: FM&E Priority 1 Audit: GAO's 2018 Assessment of Select DHS Acquisition Programs
(101940) - Wall

Hi (b)(6); (b)(7)(C)

We just got word this deliverable is still active. As it turns out, only part of the request was pushed out to the end of FY17 (the staffing plan assessment). Audit is still looking for the remaining items, listed below, per the attached email. If the documents are not yet signed, please state so to that effect and provide an expected completion date (ECD). We have requested an extension, since this is now overdue, and will let you know as soon as we hear back. Let us know if any questions. Thank you!

- Impedance and Denial Capability Analysis Report (CAR) and Mission Need Statement (MSN) (March 16,2017)
- JRC's response to the Impedance and Denial CAR and MNS
- Copies of the Requests for Proposals and Solicitations for the Prototypes
- Slide deck from the ARB presentation that served as the Capability Development Plan
- Current organizational chart
- A point of contact for the DHS study in response to the Executive Order
- Acquisition Plan, once approved
- Border Patrol analysis of prioritization of wall segments – expected at the end of August or early September
- Staffing plan – once signed by the CAE (OA will forward the plans to GAO as they are signed.)
- Copies of any contract awards, once made, including (but not limited to)
 - o Prototyping, expected end of Aug/early Sept pending bid protest result
 - o RGV hydraulic study, expected in August

(b)(6); (b)(7)(C)

Senior Task Manager

Agile Group

Office of Facilities and Asset Management

U.S. Customs and Border Protection

Mobile: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C) On Behalf Of OFAM-TASKINGS

Sent: Wednesday, August 23, 2017 2:19 PM

To: (b)(6); (b)(7)(C)

Cc: FMEEEXCSUPPORT (b)(7)(E) OFAM-TASKINGS

(b)(7)(E)

Subject: FW: FM&E Priority 1 Audit: GAO's 2018 Assessment of Select DHS Acquisition Programs (101940) - Wall

Audit has decided to push this back closer to the end of FY2017.

(b)(6); (b)(7)(C)

Task Manager

Agile Group

Office of Facilities and Asset Management

U.S. Customs and Border Protection

Mobile: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C) On Behalf Of OFAM Business Operations Program Accountability Executive Support

Sent: Wednesday, August 23, 2017 2:10 PM

To: OFAM Business Operations Program Accountability Executive Support (b)(7)(E)

(b)(7)(E) OFAM-TASKINGS (b)(7)(E) FMEEEXCSUPPORT

(b)(7)(E)

Cc: (b)(6); (b)(7)(C) OFAM Business Operations Executive Support

(b)(7)(E)

Subject: RE: FM&E Priority 1 Audit: GAO's 2018 Assessment of Select DHS Acquisition Programs

(101940) - Wall

Hi guys!

Just heard back from Audit.

Per Audit- this tasker is going to be kicked out to a later time, sounding like the end of FY17. According to the email OA sent to Audit: "The staffing assessments for the ten CBP programs covered under this review are not yet approved. We expect that they will be approved by the end of FY17. We will provide them to you as soon as they are signed."

Sincerely,

(b)(6); (b)(7)(C)

Agile Group
Business Operations Executive Support

Office of Facilities and Asset Management (OFAM)
DHS | CBP | Enterprise Services
Cell (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C) On Behalf Of OFAM Business Operations Program Accountability Executive Support

Sent: Wednesday, August 23, 2017 11:58 AM

To: OFAM-TASKINGS (b)(7)(E); FMEEXECUSUPPORT

(b)(7)(E)
Cc: (b)(7)(E) OFAM Business Operations Executive Support
(b)(7)(E) OFAM Business Operations Program Accountability Executive Support
(b)(7)(E)

Subject: RE: FM&E Priority 1 Audit: GAO's 2018 Assessment of Select DHS Acquisition Programs
(101940) - Wall

Hi everyone!

FYSA- it looks like OA has cancelled this deliverable. According to the Audit Team: "OA reached out to GAO, and let them know that "the staffing assessments for the ten CBP programs covered under this review are not yet approved. We expect that they will be approved by the end of FY17. We will provide them to you as soon as they are signed."

I am waiting for final confirmation from Audit that nothing further is needed from us at this time, but wanted to give you all a heads up!

Sincerely,

(b)(6); (b)(7)(C)

Agile Group
Business Operations Executive Support

Office of Facilities and Asset Management (OFAM)
DHS | CBP | Enterprise Services
Cell: (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C) On Behalf Of OFAM Business Operations Program Accountability Executive Support
Sent: Tuesday, August 22, 2017 3:57 PM
To: OFAM-TASKINGS (b)(7)(E)
Cc: OFAM Business Operations Program Accountability Executive Support (b)(7)(E)
(b)(6); (b)(7)(C) OFAM Business Operations Executive Support (b)(6); (b)(7)(C)
Subject: FW: FM&E Priority 1 Audit: GAO's 2018 Assessment of Select DHS Acquisition Programs (101940) - Wall
Importance: High

Good afternoon,

Please see below, we have a PRIORITY 1 deliverable to be sent to FM&E. This needs to be turned back in to OA by 4PM on Friday, September 1. I would advise a due date for FM&E by Monday, August 28 or Tuesday, August 29. Please let me know if you have any questions.

Thank you,

(b)(6); (b)(7)(C)

Communications

Business Operations

Program Accountability Branch

Bayfirst Solutions, LLC

6650 Telecomm Dr. Indianapolis, IN 46278

Work (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C) On Behalf Of OFAM AUDIT PROGRAM MANAGEMENT

Sent: Tuesday, August 22, 2017 3:36 PM

To: OFAM Business Operations Program Accountability Executive Support (b) (7)(E)

Subject: FM&E Priority 1 Audit: GAO's 2018 Assessment of Select DHS Acquisition Programs (101940)

- Wall

Importance: High

Good afternoon (b)(6); (b)(7)(C)

We have a deliverable to be sent to FM&E (APM: (b)(6); (b)(7)(C) Below are the details!

Note: This audit is priority 1 audit. It does require BOD Director and OFAM CoS review and concurrence along with FM&E's feedback.

- Deliverable Name: GAO: GAO's 2018 Assessment of Select DHS Acquisition Programs (101940)
- Wall

- Deliverable Description: Pursuant to Monday August 21, 2017 meeting with GAO and Wall program officials, GAO is requesting the documents listed below.

- Please provide completed documents to the OA Audit Team and we will forward to GAO; we will follow the same process we used for the DCI.

- If the documents are not yet signed, please state so to that effect and provide an expected completion date (ECD). Once the documents are signed, please forward to the OA Audit Team, and we will forward to GAO.

- o Impedance and Denial Capability Analysis Report (CAR) and Mission Need Statement (MSN) (March 16,2017)

- o JRC's response to the Impedance and Denial CAR and MNS

- o Copies of the Requests for Proposals and Solicitations for the Prototypes

- o Slide deck from the ARB presentation that served as the Capability Development Plan

- o Current organizational chart

- o A point of contact for the DHS study in response to the Executive Order
- o Acquisition Plan, once approved
- o Border Patrol analysis of prioritization of wall segments – expected at the end of August or early September
- o Staffing plan – once signed by the CAE
- o Copies of any contract awards, once made, including (but not limited to)
- § Prototyping, expected end of Aug/early Sept pending bid protest result
- § RGV hydraulic study, expected in August
- Assign To: FM&E (APM: (b)(6); (b)(7)(C) and FME Exec Support)
- Due Dates
- FME Due Date: To be determined by OFAM Business Operations Program Accountability Executive Support
- Complete Priority 1 Review by BOD and OFAM CoS: To be determined by OFAM Business Operations Program Accountability Executive Support
- To OA: 4:00 pm, Friday September 1, 2017
- Guidance and Notes: N/A
- Background: N/A
- Task POC: OFAM APM (b)(6); (b)(7)(C)
- OA POC: (b)(6); (b)(7)(C)

OFAM Audit Program Management

(b) (7)(E)

Business Operations Division (BOD)

Office of Facilities & Asset Management (OFAM)

From (b)(6); (b)(7)(C)

Sent: Tuesday, August 22, 2017 12:54 PM

To (b)(6); (b)(7)(C)

Cc (b)(6); (b)(7)(C)

Subject: RE: GAO's 2018 Assessment of Select DHS Acquisition Programs (101940) - Wall

OFAM Audit Team,

Pursuant to yesterday's meeting with GAO and Wall program officials, GAO is requesting the documents listed below. Please provide completed documents to the OA Audit Team and we will forward to GAO; we will follow the same process we used for the DCI.

If the documents are not yet signed, please state so to that effect and provide an expected completion date (ECD). Once the documents are signed, please forward to the OA Audit Team, and we will forward to GAO.

- Impedance and Denial Capability Analysis Report (CAR) and Mission Need Statement (MSN) (March 16, 2017)
- JRC's response to the Impedance and Denial CAR and MNS
- Copies of the Requests for Proposals and Solicitations for the Prototypes
- Slide deck from the ARB presentation that served as the Capability Development Plan
- Current organizational chart
- A point of contact for the DHS study in response to the Executive Order
- Acquisition Plan, once approved
- Border Patrol analysis of prioritization of wall segments – expected at the end of August or early September
- Staffing plan – once signed by the CAE
- Copies of any contract awards, once made, including (but not limited to)
 - o Prototyping, expected end of Aug/early Sept pending bid protest result
 - o RGV hydraulic study, expected in August

Please note that GAO is requesting a response by COB 1 September. Thank you.

V/R,

AMENDMENT OF SOLICITATION/MODIFICATION OF CONTRACT				1 CONTRACT ID CODE		PAGE OF PAGES 1 114	
2 AMENDMENT/MODIFICATION NO		3 EFFECTIVE DATE 07-Sep-2017		4 REQUISITION/PURCHASE REQ NO W45XMA71592962		5 PROJECT NO (If applicable)	
6 ISSUED BY US ARMY ENGINEER DISTRICT, FORT WORTH ATTN: CESWF-CT 819 TAYLOR ST, ROOM 2A17 FORT WORTH TX 76102-0300		CODE W9126G		7 ADMINISTERED BY (If other than item 6) US ARMY CORPS OF ENGINEERS FORT WORTH 819 TAYLOR ST, RM 2A17 FORT WORTH TX 76102-0300		CODE W9126G	
8. NAME AND ADDRESS OF CONTRACTOR (No., Street, County, State and Zip Code) MICHAEL BAKER INTERNATIONAL, INC. (b) (6) 2929 N CENTRAL AVE STE 800 PHOENIX AZ 85012-2794				9A. AMENDMENT OF SOLICITATION NO.			
				9B. DATED (SEE ITEM 11)			
				X 10A. MOD. OF CONTRACT/ORDER NO. W9126G17F0015			
				X 10B. DATED (SEE ITEM 13) 13-Jun-2017			
CODE 028J5		FACILITY CODE					
11. THIS ITEM ONLY APPLIES TO AMENDMENTS OF SOLICITATIONS							
<input type="checkbox"/> The above numbered solicitation is amended as set forth in Item 14. The hour and date specified for receipt of Offer <input type="checkbox"/> is extended, <input type="checkbox"/> is not extended Offer must acknowledge receipt of this amendment prior to the hour and date specified in the solicitation or as amended by one of the following methods: (a) By completing Items 8 and 15, and returning _____ copies of the amendment; (b) By acknowledging receipt of this amendment on each copy of the offer submitted; or (c) By separate letter or telegram which includes a reference to the solicitation and amendment numbers. FAILURE OF YOUR ACKNOWLEDGMENT TO BE RECEIVED AT THE PLACE DESIGNATED FOR THE RECEIPT OF OFFERS PRIOR TO THE HOUR AND DATE SPECIFIED MAY RESULT IN REJECTION OF YOUR OFFER. If by virtue of this amendment you desire to change an offer already submitted, such change may be made by telegram or letter, provided each telegram or letter makes reference to the solicitation and this amendment, and is received prior to the opening hour and date specified.							
12. ACCOUNTING AND APPROPRIATION DATA (If required) See Schedule							
13. THIS ITEM APPLIES ONLY TO MODIFICATIONS OF CONTRACTS/ORDERS. IT MODIFIES THE CONTRACT/ORDER NO. AS DESCRIBED IN ITEM 14.							
A. THIS CHANGE ORDER IS ISSUED PURSUANT TO: (Specify authority) THE CHANGES SET FORTH IN ITEM 14 ARE MADE IN THE CONTRACT ORDER NO. IN ITEM 10A.							
B. THE ABOVE NUMBERED CONTRACT/ORDER IS MODIFIED TO REFLECT THE ADMINISTRATIVE CHANGES (such as changes in paying office, appropriation date, etc.) SET FORTH IN ITEM 14, PURSUANT TO THE AUTHORITY OF FAR 43.103(B).							
X C. THIS SUPPLEMENTAL AGREEMENT IS ENTERED INTO PURSUANT TO AUTHORITY OF: 52.243-1, Changes.							
D. OTHER (Specify type of modification and authority)							
E. IMPORTANT: Contractor <input type="checkbox"/> is not, <input checked="" type="checkbox"/> is required to sign this document and return <u>1</u> copies to the issuing office.							
14. DESCRIPTION OF AMENDMENT/MODIFICATION (Organized by UCF section headings, including solicitation/contract subject matter where feasible.) Modification Control Number: m2ct9drc171696 The purpose of this modification is to revise the SOW to incorporate an additional (b) (6) miles of hydraulic analysis. This additional effort will increase the total obligation amount by \$ (b) (4). This modification is IAW FAR 52.243-1, Changes. All other terms and conditions remain unchanged.							
Except as provided herein, all terms and conditions of the document referenced in Item 9A or 10A, as heretofore changed, remains unchanged and in full force and effect.							
15A. NAME AND TITLE OF SIGNER (Type or print) (b) (6) Associate Vice President				16A. NAME AND TITLE OF CONTRACTING OFFICER (Type or print) T (b) (6) EMAIL: (b) (6)			
15B. CONTRACTOR/OFFEROR (b) (6) (Signature of person authorized to sign)		15C. DATE SIGNED 9/7/2017		16B. UNITED STATES OF AMERICA BY (Signature of Contracting Officer)		16C. DATE SIGNED	

SECTION SF 30 BLOCK 14 CONTINUATION PAGE

SUMMARY OF CHANGES

SECTION SF 30 - BLOCK 14 CONTINUATION PAGE

The following have been added by full text:

REVISED SOW

**A-E TASK ORDER - STATEMENT OF
WORK**

Task Order under Contract No. W9126G-15-D-0009 - Michael Baker &
Associates Architect and Engineer Services for the Design of Floodwall,
Fence, Roads, Drainage, & Lights at Rio Grande Valley & San
Diego FY17, P2 465132, ATS: SWF-17-0799

Date: 17 May 2017

Modification 1: 11 August 2017

(b) (5), (b) (7)(E)

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b) (6)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b)(6); (b)(7)(C)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b)(6); (b)(7)(C)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b)(6); (b)(7)(C)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b)(6); (b)(7)(C)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b)(6); (b)(7)(C)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5), (b)(6); (b)(7)(C)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

Appendix A

Project Execution Within Rio Grande Valley Sector


(b) (7)(E)

(b) (7)(E) Station - Zone (b) (7)(E)

(b) (7)(E)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

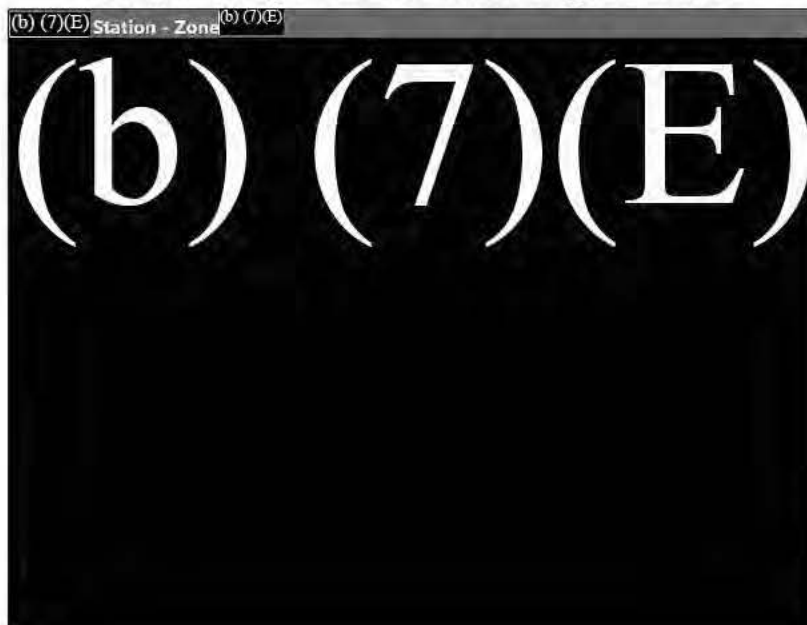

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (7)(E) Station - Zone (b) (7)(E)
(b) (7)(E)

(b) (7)(E) Station - Zone (b) (7)(E)
(b) (7)(E)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (7)(E) Station - Zone (b) (7)(E)
(b)(6); (b)(7)(C)

(b) (7)(E) Station - Zone (b) (7)(E)
(b)(6); (b)(7)(C)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (7)(E) Station - Zone (b) (7)(E)
(b) (7)(E)



(b) (7)(E) Station - Zone (b) (7)(E)
(b) (7)(E)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


Appendix B

SDC BIS Primary Fence Replacement Map (~14 miles)

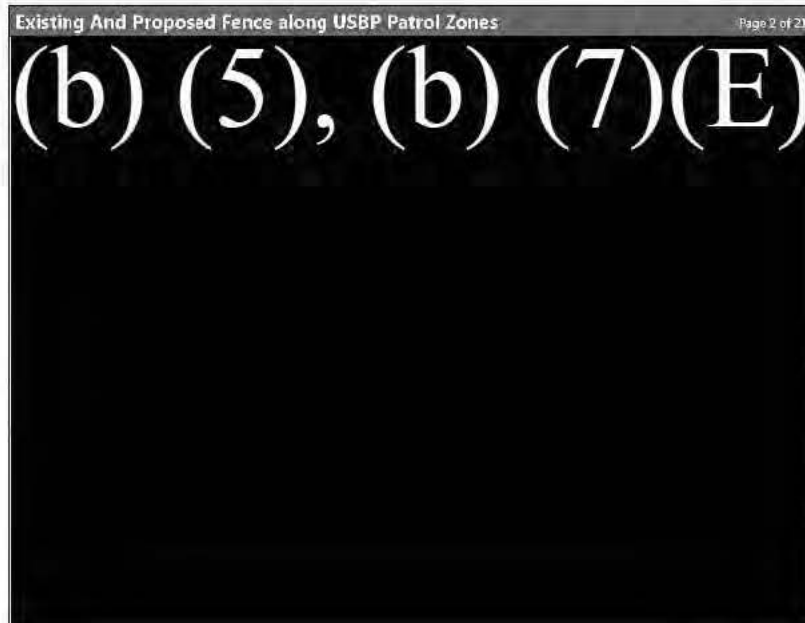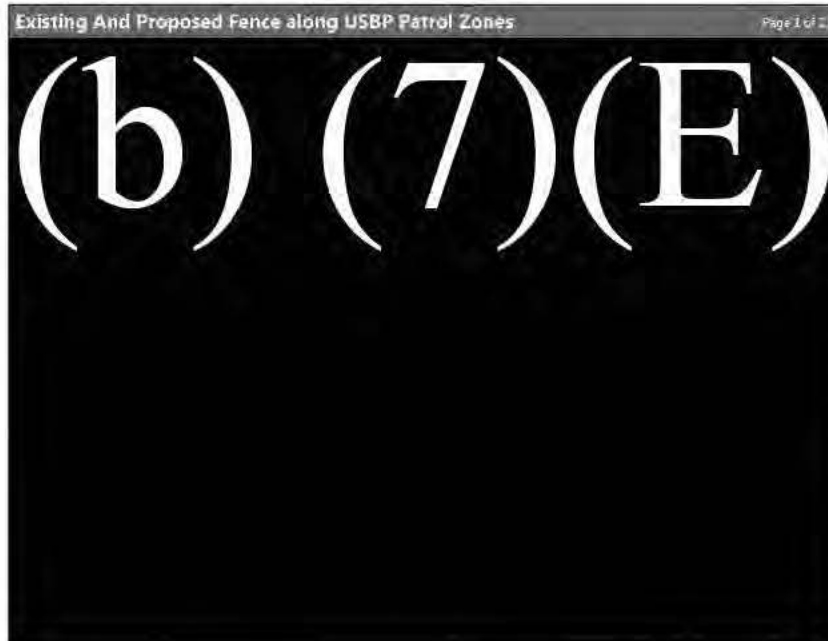


A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

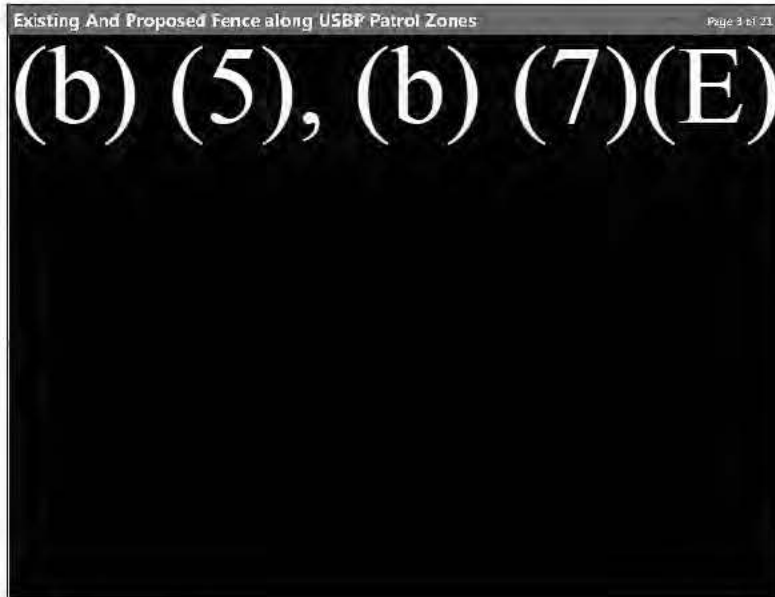


ELC (b) (7)(E) SDC (b) (7)(E) Primary Fence Replacement Map (b) (7)(E) miles)

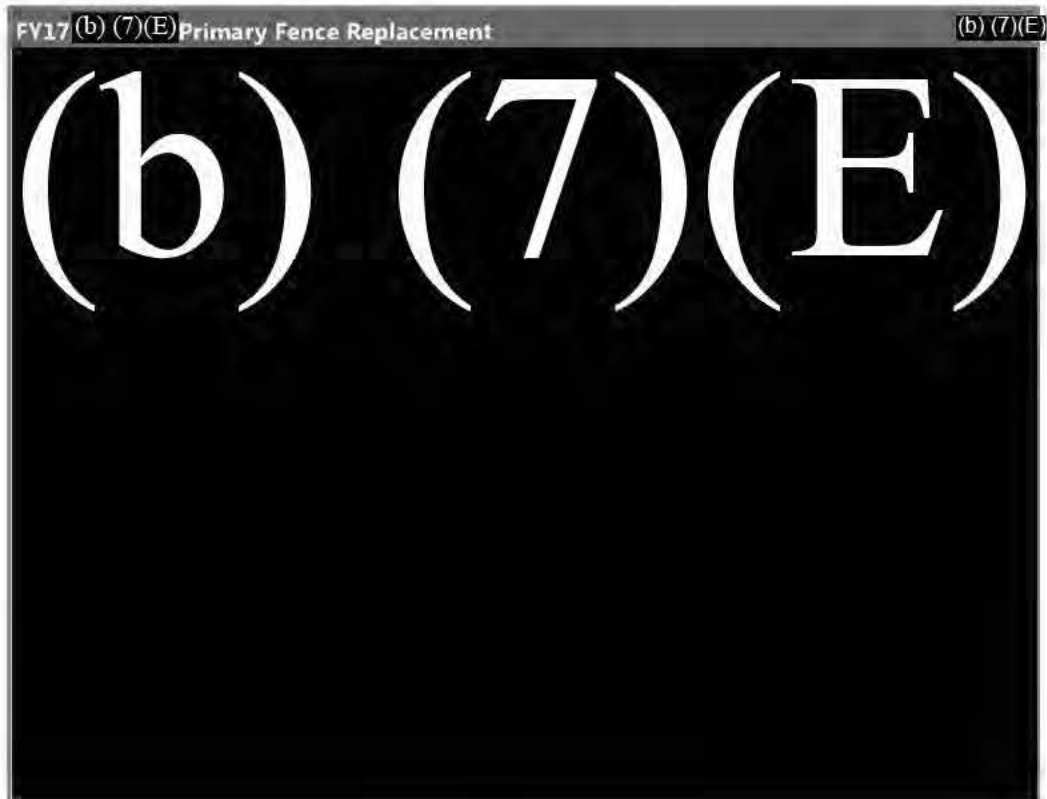

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,



ELP (b) (7)(E) Primary Fence Replacement Map (b) (7)(E) miles)

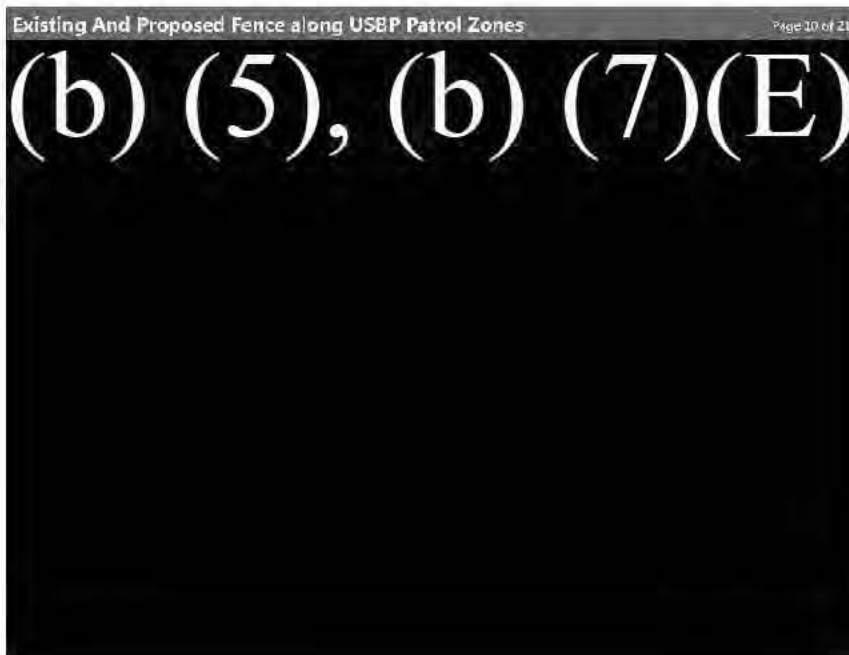

A-E TASK ORDER - STATEMENT OF WORK



Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

ELP Vehicle Fence to Primary Fence Replacement Map (b) (7)(E) miles)

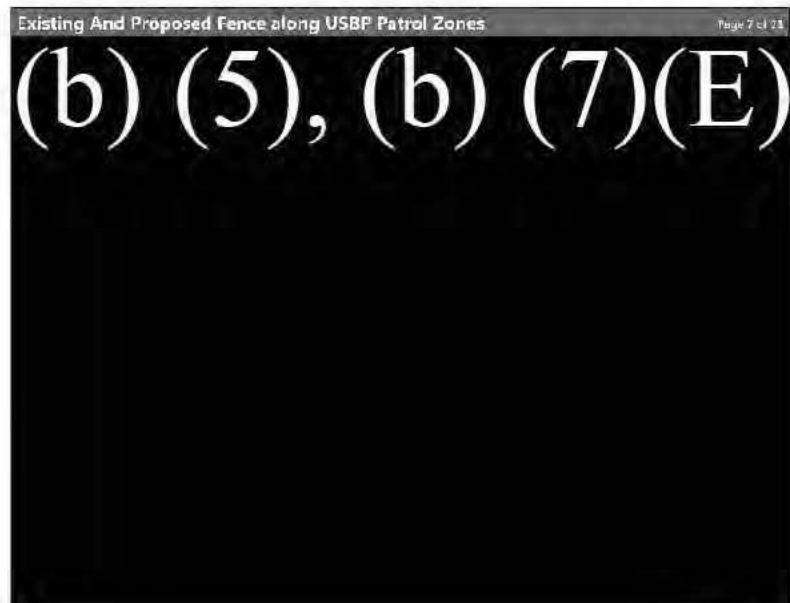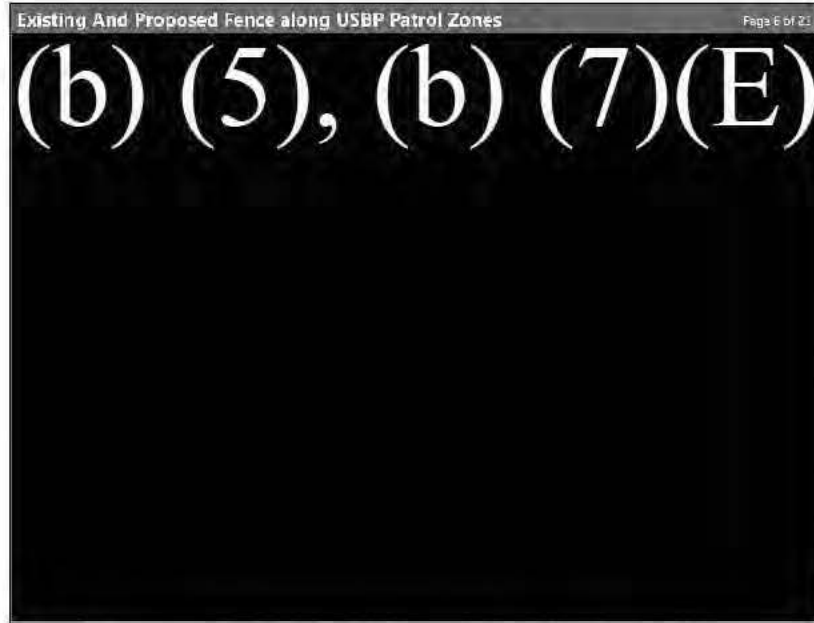

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

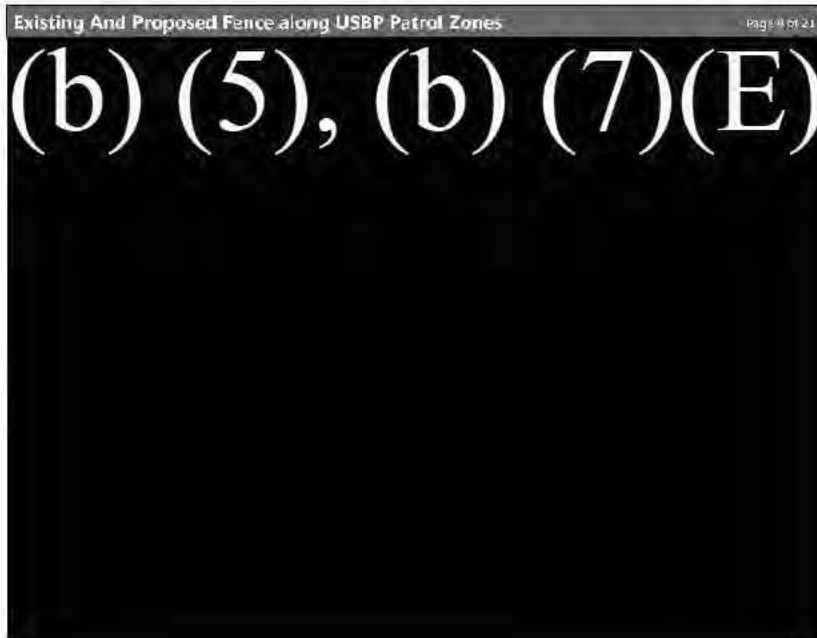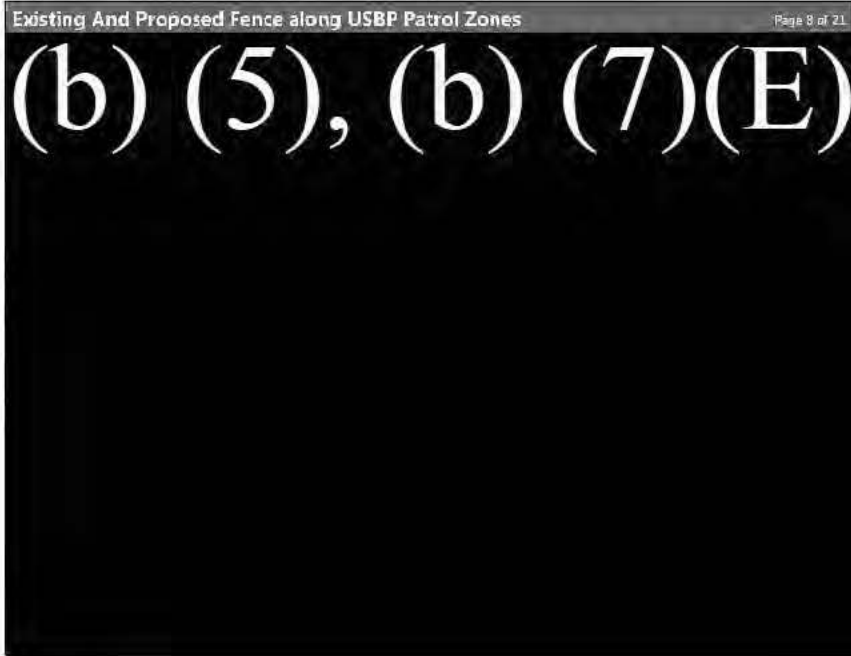


A-E TASK ORDER - STATEMENT OF WORK


Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

Appendix C

RGV (b) (7)(E) & RGV (b) (7)(E) Map

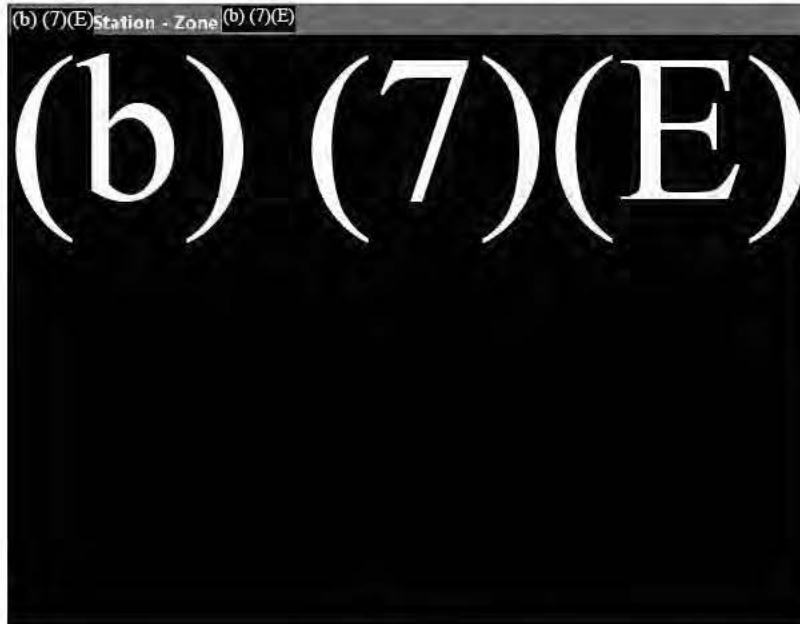

RGV (b) (7)(E) MAP

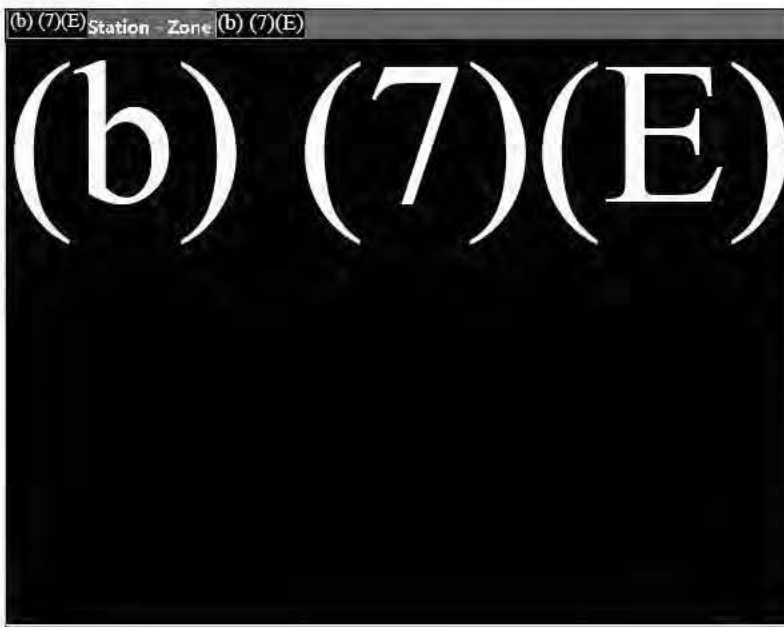

RGV-^{(b) (7)(E)} MAP

(b) (7)(E) Station - Zone (b) (7)(E)

(b) (7)(E)

(b) (5)

(b) (5), (b) (6)



(b) (5)

From:

(b)(6); (b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: T&E Deck for IPT

Date: Mon Sep 11 2017 08:30:56 EDT

Attachments:

Thx

From: (b)(6); (b)(7)(C)

Sent: Monday, September 11, 2017 8:26:49 AM

To: (b)(6); (b)(7)(C)

Cc:

Subject: T&E Deck for IPT

(b)(6); (b)(7)(C) – here's the deck that (b)(6); (b)(7)(C) was referencing this morning. See slide 8.

(b)(6); (b)(7)(C) – can you please print this for (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Special Projects Analyst

Agile Group

Office of Facilities and Asset Management

U.S. Customs and Border Protection

Mobile: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Friday, September 8, 2017 7:31 AM

To: (b)(6); (b)(7)(C)

Subject: FW: 20170907_Border Wall T&E Strategy_no backup_FOUO.pptx

FYSA –

C2 meeting = IPT?

(b)(6); (b)(7)(C) you got this one?

(b)(6); (b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Thursday, September 07, 2017 3:44 PM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: FW: 20170907_Border Wall T&E Strategy_no backup_FOUE.pptx

FYI

(b)(6); (b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)
Facilities Management & Engineering

Office: (b)(6); (b)(7)(C)

Cell: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b) (7)(E)

From: (b)(6); (b)(7)(C)

Sent: Thursday, September 07, 2017 2:50 PM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b)(6)

(b)(6); (b)(7)(C)

(b)(6)

(b)(6); (b)(7)(C)

(b)(6)

(b)(6); (b)(7)(C)

(b) (6)

(b)(6); (b)(7)(C)

(b) (6)

(b)(6); (b)(7)(C)

Subject: 20170907_Border Wall T&E Strategy_no backup_FOUO.pptx

T&E IPT,

Attached are slides that will be presented at the next C2 brief, next week. Please review and if you have questions, comments, or updates please provide NLG Tuesday, 12 Sep.

v/r,

(b)(6); (b)(7)(C) (MITRE)

Acting Technical Director

Land Systems Operational Test Authority (LSOTA)

(b)(6); (b)(7)(C)

Homeland Security Systems Engineering Development Institute (HSSEDI)

(b)(6); (b)(7)(C)

From:

To:

Cc:

(b)(6); (b)(7)(C)

Bcc:

Subject: T&E Deck for IPT

Date: Mon Sep 11 2017 08:26:49 EDT

Attachments: 20170907_Border Wall T&E Strategy_no backup_FOUO.pptx

(b)(6); (b)(7)(C) – here's the deck that (b)(6); (b)(7)(C) was referencing this morning. See slide 8.

(b)(6); (b)(7)(C) – can you please print this for (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Special Projects Analyst

Agile Group

Office of Facilities and Asset Management

U.S. Customs and Border Protection

Mobile: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Friday, September 8, 2017 7:31 AM

To: (b)(6); (b)(7)(C)

Subject: FW: 20170907_Border Wall T&E Strategy_no backup_FOUO.pptx

FYSA –

C2 meeting = IPT?

(b)(6); (b)(7)(C) – you got this one?

(b)(6); (b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Thursday, September 07, 2017 3:44 PM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: FW: 20170907_Border Wall T&E Strategy_no backup_1000.pptx

FYI

(b)(6); (b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Office: (b)(6); (b)(7)(C)

Cell: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

[Click Here](#) to view the FMB team listed with areas of responsibility.

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b)(6); (b)(7)(C)

Sent: Thursday, September 07, 2017 2:50 PM

To: (b)(6)

(b)(6)

(b)(6)

(b)(6); (b)(7)(C)

(b)(6)

(b)(6); (b)(7)(C)

(b)(6)

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b)(6)

Subject: 20170907_ (b)(6); (b)(7)(C) T&E Strategy_no backup_FOUO.pptx

T&E IPT,

Attached are slides that will be presented at the next C2 brief, next week. Please review and if you have questions, comments, or updates please provide NLG Tuesday, 12 Sep.

v/r,

(b)(6); (b)(7)(C) (MITRE)


Acting Technical Director

Land Systems Operational Test Authority (LSOTA)

(b)(6); (b)(7)(C)

Homeland Security Systems Engineering Development Institute (HSSEDI)

(b)(6); (b)(7)(C)



US Customs and Border Protection's Wall Program

Mockup and Prototype T&E Strategy Briefing



Homeland
Security

UNCLASSIFIED//~~FOUO~~

9/7/2017

BW23 FOIA CBP 012008

Page 1076 of 1174

(b) (5), (b) (7)(E)

UNCLASSIFIED//~~FOUO~~

BW23 FOIA CBP 012009

Page 1077 of 1174

Program Background

(b) (5), (b) (7)(E)

UNCLASSIFIED//~~FOUO~~

BW23 FOIA CBP 012010

Page 1078 of 1174

Program Overview

(b) (5), (b) (7)(E)

(b) (5), (b) (7)(E)

UNCLASSIFIED//~~FOUO~~

BW23 FOIA CBP 012012

Page 1080 of 1174

Impedance and Denial T&E Methodology

(b) (5), (b) (7)(E)



UNCLASSIFIED//~~FOUO~~

BW23 FOIA CBP 012013
6

Page 1081 of 1174

Overall I&D T&E Strategy

(b) (5), (b) (7)(E)

T&E Master Schedule

(b) (5), (b) (7)(E)



Individual T&E Event Descriptions

UNCLASSIFIED//~~FOUO~~

BW23 FOIA CBP 012016

Page 1084 of 1174

(b) (5), (b) (7)(E)

UNCLASSIFIED//~~FOUO~~

BW23 FOIA CBP 012017

16
Page 1085 of 1174

Mockup T&E

(b) (5), (b) (7)(E)

UNCLASSIFIED//~~FOUO~~

BW23 FOIA CBP 012018

Page 1086 of 1174

Prototype T&E

(b) (5), (b) (7)(E)


UNCLASSIFIED//~~FOUO~~

BW23 FOIA CBP 012019

Page 1087 of 1174

Mockup and Prototype Test Design - Preliminary

(b) (5), (b) (7)(E)



UNCLASSIFIED//~~FOUO~~

BW23 FOIA CBP 012020

Page 1088 of 1174

From:

To:

Cc:

Bcc:

Subject: RE: ADE-2A Weekly Meeting
Date: Mon Sep 11 2017 07:52:15 EDT
Attachments:

(b)(6); (b)(7)(C)

Thanks (b)(6); (b)(7)(C) we will keep an eye out for it.

(b)(6); (b)(7)(C)

Director, Business Operations Division
Border Patrol & Air and Marine Program Management Office
Facilities Management and Engineering
Office of Facilities and Asset Management
Mobile: (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Sunday, September 10, 2017 2:28 PM

To:

Cc:

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: ADE-2A Weekly Meeting

All-I finally got time to dive into this this weekend and have made good progress. I'll distribute the draft tomorrow AM. Sorry for the delay.

PS-Let me know if we need a Systems Engineer to be our lead for these kind of documents moving forward. I have a number of good ones.

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C), P.E., PMP, Chief Engineer
Border Patrol & Air and Marine (BPAM) PMO
LMI Contractor
Mobile: 202-306-7823
(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Wednesday, September 6, 2017 9:32 AM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: FW: ADE-2A Weekly Meeting

Hey (b)(6); (b)(7)(C) < Message: FW: Initial Draft SELC TP >>
Where are we with this?

(b)(6); (b)(7)(C)
Border Patrol & Air and Marine Program Management Office (BPAM PMO)
Facilities Management & Engineering

Office: (b)(6); (b)(7)(C)
Cell: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)
[Click Here to view the PRR tracker.](#)
[Click Here to view the IAA Tracker](#)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, September 05, 2017 11:54 AM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
755N-EXEC-CR-NP (b)(7)(E)
(b)(6); (b)(7)(C)
(b)(6); (b)(7)(C) (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: ADE-2A Weekly Meeting

(b)(6); (b)(7)(C)

What do we need to do to get the SELCTP moving???

R
(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)
Division Director
Acquisition Policy and Oversight (APO)
Office of Acquisition (OA)/AGO

(b)(6); (b)(7)(C) (office)
(b)(6); (b)(7)(C) (cell)
(b)(6); (b)(7)(C) (fax)
(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C) (CTR) On Behalf Of (b)(6); (b)(7)(C)
Sent: Thursday, August 31, 2017 9:04 AM
To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C) 755N-EXEC-CR-NP (b) (7)(E) (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C) I (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: RE: ADE-2A Weekly Meeting

Updated schedule attached.

<< File: ADE-2Schedule_08302017.xlsx >>

(b)(6); (b)(7)(C)

-----Original Appointment-----

From: (b)(6); (b)(7)(C) (CTR) On Behalf Of (b)(6); (b)(7)(C)
Sent: Friday, March 31, 2017 3:06 PM
To: (b)(6); (b)(7)(C)

755N-EXEC-CR-NP; (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: ADE-2A Weekly Meeting

When: Friday, September 01, 2017 11:30 AM-12:30 PM (UTC-05:00) Eastern Time (US & Canada).

Where: 775N CR0726 Phone: (b) (7)(E) Pin: (b) (7)(E)

From:

To:

Cc:

(b)(6); (b)(7)(C)

Bcc:

Subject: RE: ADE-2A Weekly Meeting
Date: Sun Sep 10 2017 14:27:38 EDT
Attachments:

All-I finally got time to dive into this this weekend and have made good progress. I'll distribute the draft tomorrow AM. Sorry for the delay.

PS-Let me know if we need a Systems Engineer to be our lead for these kind of documents moving forward. I have a number of good ones.

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C) P.E., PMP, Chief Engineer
Border Patrol & Air and Marine (BPAM) PMO
LMI Contractor
Mobile: (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Wednesday, September 6, 2017 9:32 AM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: FW: ADE-2A Weekly Meeting

Hey (b)(6); (b)(7)(C) << Message: FW: Initial Draft SELC TP >>
Where are we with this?

(b)(6); (b)(7)(C)
Border Patrol & Air and Marine Program Management Office (BPAM PMO)
Facilities Management & Engineering
Office: (b)(6); (b)(7)(C)

Cell: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b)(6); (b)(7)(C)

Sent: Tuesday, September 05, 2017 11:54 AM

To: (b)(6); (b)(7)(C)

755N-EXEC-CR-NP

(b) (7)(E)

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: RE: ADE-2A Weekly Meeting

(b)(6); (b)(7)(C)

What do we need to do to get the SELCTP moving???

R

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Division Director

Acquisition Policy and Oversight (APO)

Office of Acquisition (OA)/AGO

(b)(6); (b)(7)(C) (office)

(b)(6); (b)(7)(C) (cell)

(b)(6); (b)(7)(C) (fax)

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C) (CTR) On Behalf Of (b)(6); (b)(7)(C)

Sent: Thursday, August 31, 2017 9:04 AM

To: (b)(6); (b)(7)(C)

755N-EXEC-CR-NP

(b) (7)(E)

(b)(6); (b)(7)(C)

Cc: [REDACTED] (b)(6); (b)(7)(C)

Subject: RE: ADE-2A Weekly Meeting

Updated schedule attached.

<< File: ADE-2Schedule_08302017.xlsx >>

(b)(6); (b)(7)(C)

-----Original Appointment-----

From: [REDACTED] (b)(6); (b)(7)(C) On Behalf Of [REDACTED] (b)(6); (b)(7)(C)

Sent: Friday, March 31, 2017 3:06 PM

To: [REDACTED] (b)(6); (b)(7)(C)

755N-EXEC-CR-NP:

[REDACTED] (b)(6); (b)(7)(C)

Cc: [REDACTED] (b)(6); (b)(7)(C)

Subject: ADE-2A Weekly Meeting

When: Friday, September 01, 2017 11:30 AM-12:30 PM (UTC-05:00) Eastern Time (US & Canada).

Where: 775N CR0726 Phone: [REDACTED] (b) (7)(E) Pin: [REDACTED] (b) (7)(E)

From:

(b)(6); (b)(7)(C)

To:

Cc:

Bcc:

Subject: Updates while you were away

Date: Fri Sep 08 2017 16:18:32 EDT

Attachments: (b)(6); (b)(7)(C) Update 0825.docx

Hope you had a nice time and a happy birthday. Attached are updates I pulled from your email. If you read anything, read the ones in bold. Mainly these two weeks were focused on Hurricane efforts. Your flight is at 11:55am on Monday.

See you on Monday,

(b)(6); (b)(7)(C)

Executive Assistant

Strategic Analysis, Inc.

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Mobile: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C) Updates
25 August-8 September

Friday 25 August

- * IBWC planning to share San Diego, (b)(6); (b)(7)(C) submittals with the Mexican Section (email from Dr. Unni)
- * (b)(6); (b)(7)(C) emailed about analyst position with BPAM

Monday 28 August

- * (b)(6); (b)(7)(C) sent copy of updated AA Study Plan that was sent for approval and signature

Tuesday 29 August

- * (b)(6); (b)(7)(C) sent summary of observations from EPT site visit; Baker updated drawings before they are released for bid
- * EPT waiver most likely delayed for signature because of hurricane
- * Peaceful (b)(7)(E) Fence Protest, media was present (email from (b)(6); (b)(7)(C))
- * (b)(6); (b)(7)(C) is coordinating point for (b)(6); (b)(7)(C) from USACE regarding security

Wednesday 30 August

- * **RGV Stakeholders meeting 14 September canceled; not rescheduled yet**
 - o **Chief Padilla is overseeing CBP's Hurricane Response within Region 6**
- * Wall Program included in the MAOL (email from (b)(6); (b)(7)(C))
- * Email from (b)(6); (b)(7)(C) about Client Satisfaction Survey for (b)(6); (b)(7)(C)
- * Current travel authorizations can only run through 30 Sept
- * **Wall and TI Staffing plans signed and submitted to OA**
- * **Revised ILSP signed and resubmitted to OA**
- * (b)(6); (b)(7)(C) sent email asking about (b)(7)(E) space needed for the Fence team

Thursday 31 August

- * (b)(6); (b)(7)(C) on call with Kolbe:
Nothing really said...

1. Prototype sched.
2. our RFP release today (nothing said about press release)
3. (b)(6); (b)(7)(C) brought up announcing who is on the prequal list.
4. Lots of discussion about hurricanes...

That was it. Ended in 20 minutes.

- * (b)(6); (b)(7)(C) sent Baker Survey Work notice for RGV week of 2 Sept.
- * (b)(6); (b)(7)(C) was waived from SLT training (b)(6); (b)(7)(C) mailed (b)(6); (b)(7)(C) to get (b)(6); (b)(7)(C) training delayed.
(b)(6); (b)(7)(C) has sent it up to Karl

- * (b)(6); (b)(7)(C) is organizing Partnering Meeting, he suggested 13 Oct but I told him you are on leave
- * (b) (5), (b) (6)
- * El Centro Wall Replacement successfully solicited today, on schedule
- * USACE will not be renewing the contractor for paralegal support for SDTX when the contract expires on 12/31/17, (b)(6);(b)(7)(C) reaching out to (b)(6);(b)(7)(C) for next steps
- * Updated CEBD submitted to OA for signature
- * Chief Padilla met with farmers and ranchers to go over wall, email from (b)(6); (b)(7)(C)
- * (b)(6); (b)(7)(C) had positive meeting with El Paso Water District
- * (b)(6); (b)(7)(C) provided feedback from funding questions you and (b)(6); (b)(7)(C) had last week
- * Email from (b)(6); (b)(7)(C) with spots in RGV that DOJ LAS wants to visit while down there week of 11 Sept.
- * (b)(6); (b)(7)(C) not feeling well and in Emergency Room (b)(6); (b)(7)(C) to send updates
- * (b) (7)(E) successfully solicited

Friday 1 September

- * (b)(6); (b)(7)(C) listed you as the supervisor to recertify his security
- * (b)(6); (b)(7)(C) sent After Action Report for stakeholder meeting held 31 August
- * (b)(6); (b)(7)(C) starting to develop IMS based on our Wall Project IMS
- * Email from (b)(6); (b)(7)(C) asking to update FY17Q4 quad charts by 26 Sept (email is flagged)
- * (b)(6); (b)(7)(C) sent USACE security participation update, wants to bring (b)(6); (b)(7)(C) into the conversation
- * (b)(6); (b)(7)(C) sent updated IMS (b) (5)
- * (b)(6); (b)(7)(C) expected to be released tonight or tomorrow, cause of issues still unknown
- * (b) (5), (b)(6); (b)(7)(C)

Sunday 3 September

- * Contractor completed drilling at (b) (7)(E) with no incident or media presence

Tuesday 5 September

- * (b)(6); (b)(7)(C) approved and I signed the AA plan for RGV
- * (b)(6); (b)(7)(C) needs you to approve a 'Surge Capacity Registration Form' Email flagged
- * (b)(6); (b)(7)(C) has team prepping all personnel in Puerto Rico and their emergency contacts as well as lists and maps of all leases in preparation for Hurricane Irma
- * (b)(6); (b)(7)(C) emailed asking about what we need to do to get the "SELCTP moving" (b)(6); (b)(7)(C) following up)
- * (b)(6); (b)(7)(C) sent Draft slides for PARM IMS briefing on 9/13
- * Draft deck from (b)(6); (b)(7)(C) for Hoover brief on 13 September
- * Project codes for Hurricane Irma from (b)(6); (b)(7)(C)

- * (b)(6); (b)(7)(C) attended Prototype/ Unified Resolve Planning meeting (SDPD, Sheriff, and BP all working together to prep for expected extended protest response)

Wednesday 6 September

- * (b)(6); (b)(7)(C) has Eastern Corridor putting together Deployment teams for Ramey Sector and Florida for after Hurricane Irma hits
- * Borkowski plans to sign the planned awards for the "Other" prototypes by the end of the week
- * ELC waiver signed
- * Program Monthly Reporting Data Call- Due 9/15, email from CPIC flagged
- * Meeting 27 September to go over (b)(6); (b)(7)(C) reporting to you, (b)(6); (b)(7)(C) also want to discuss (b)(6); (b)(7)(C) role
- * (b)(7)(E)
- * Borkowski is having a meeting on 25 September with Tetra Tech to go over environmental planning in regards to the Wall, Calvo wants you, (b)(6); (b)(7)(C) at the meeting
- * (b)(6); (b)(7)(C) from Granite is visiting USACE in Ft. Worth next week, has meeting 20 September with California Senator to go over blacklisting
- * Dr. Unni sent over draft MOA, needs to be reviewed (email flagged)

Thursday 7 September

- * (b)(6); (b)(7)(C) sent you a Happy Birthday email
- * (b)(6); (b)(7)(C) coordinating with (b)(6); (b)(7)(C) to get legacy cost data for the AA
- * IMS Brief for 13 September sent to EAC Kolbe for review
- * FYI email from (b)(6); (b)(7)(C) about ANIMAS
- * (b)(6); (b)(7)(C) asking about (b)(7)(E) tower construction
- * (b)(6); (b)(7)(C) wants you to present with PMOD at the AUSA DHS Pavilion
- * Updated ADE to reflect 9/27 for ART
- * (b)(6); (b)(7)(C) sent you Happy Birthday email, wants to get coffee
- * (b)(6); (b)(7)(C) wants you at meeting on 19 September in El Paso
- * (b)(6); (b)(7)(C) sent Border Wall T&E Strategy deck
- * (b)(5), (b)(6); (b)(7)(C)
- * You need to approve (b)(6); (b)(7)(C) security recertification
- * Baker SOW awarded

Friday 8 September

- * Email from (b)(6); (b)(7)(C) and Karl about disconnect between schedules and CAD/the ICE. We have ARB 23 October and (b)(6); (b)(7)(C) has it 21 November, Borkowski says the ESC told team to maintain 16 October date and is not happy it is being pushed out

- * (b)(6); (b)(7)(C) emailed (b)(6); (b)(7)(C) about (b)(6); (b)(7)(C) reaching out to (b)(6); (b)(7)(C) about prototype help? (b)(6); (b)(7)(C) spoke with (b)(6); (b)(7)(C) and said he only asked about information, (b)(6); (b)(7)(C) set rule that anything prototype needs to go himself or (b)(6); (b)(7)(C)
- * (b)(6); (b)(7)(C) **wants to bring new LMI CEO to meet you and Karl on 19 September, but that is the same day (b)(6); (b)(7)(C) wants you in El Paso**
- * (b)(6); (b)(7)(C) can get you from the airport in McAllen on Monday
- * ELC Waiver, Monday/Tuesday sequence of events, PAG document in inbox
- * (b)(6); (b)(7)(C) wants you to participate in Border Wall Industry Day, I'm working with him to set up time to go over specifics

From:

(b) (6)

To:

(b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

Bcc:

Subject: Baker Mod Award Notification

Date: Thu Sep 07 2017 19:00:10 EDT

Attachments: G2.20_Mod_Signed.pdf

(b)(6);(b)(7)(C)

I am pleased to inform you that the modification to the Baker SOW was just awarded. I will coordinate with Baker to 1) update their schedules to reflect the additional/revised tasks and 2) set up a quick mini-kick off for the additional H&H and RGV-^{10/1/12} project. Please let me know if there is any other tasks that you would like me to add or information that you might need.

Thanks,

(b) (6) CEM

Chief, Business & Financial Management Section
Regional Planning & Environmental Center
Fort Worth District

Office: (b) (6)

BB: (b) (6)

CELL: (b) (6)

AMENDMENT OF SOLICITATION/MODIFICATION OF CONTRACT				1 CONTRACT ID CODE		PAGE OF PAGES 1 114	
2 AMENDMENT/MODIFICATION NO		3 EFFECTIVE DATE 07-Sep-2017		4 REQUISITION/PURCHASE REQ NO W45XMA71592962		5 PROJECT NO (If applicable)	
6 ISSUED BY US ARMY ENGINEER DISTRICT, FORT WORTH ATTN: CESWF-CT 819 TAYLOR ST, ROOM 2A17 FORT WORTH TX 76102-0300		CODE W9126G		7 ADMINISTERED BY (If other than item 6) US ARMY CORPS OF ENGINEERS FORT WORTH 819 TAYLOR ST, RM 2A17 FORT WORTH TX 76102-0300		CODE W9126G	
8. NAME AND ADDRESS OF CONTRACTOR (No., Street, County, State and Zip Code) MICHAEL BAKER INTERNATIONAL, INC. (b) (6) 2929 N CENTRAL AVE STE 800 PHOENIX AZ 85012-2794				9A. AMENDMENT OF SOLICITATION NO.			
				9B. DATED (SEE ITEM 11)			
				X 10A. MOD. OF CONTRACT/ORDER NO. W9126G17F0015			
				X 10B. DATED (SEE ITEM 13) 13-Jun-2017			
CODE 028J5		FACILITY CODE					
11. THIS ITEM ONLY APPLIES TO AMENDMENTS OF SOLICITATIONS							
<input type="checkbox"/> The above numbered solicitation is amended as set forth in Item 14. The hour and date specified for receipt of Offer <input type="checkbox"/> is extended, <input type="checkbox"/> is not extended Offer must acknowledge receipt of this amendment prior to the hour and date specified in the solicitation or as amended by one of the following methods: (a) By completing Items 8 and 15, and returning _____ copies of the amendment; (b) By acknowledging receipt of this amendment on each copy of the offer submitted; or (c) By separate letter or telegram which includes a reference to the solicitation and amendment numbers. FAILURE OF YOUR ACKNOWLEDGMENT TO BE RECEIVED AT THE PLACE DESIGNATED FOR THE RECEIPT OF OFFERS PRIOR TO THE HOUR AND DATE SPECIFIED MAY RESULT IN REJECTION OF YOUR OFFER. If by virtue of this amendment you desire to change an offer already submitted, such change may be made by telegram or letter, provided each telegram or letter makes reference to the solicitation and this amendment, and is received prior to the opening hour and date specified.							
12. ACCOUNTING AND APPROPRIATION DATA (If required) See Schedule							
13. THIS ITEM APPLIES ONLY TO MODIFICATIONS OF CONTRACTS/ORDERS. IT MODIFIES THE CONTRACT/ORDER NO. AS DESCRIBED IN ITEM 14.							
A. THIS CHANGE ORDER IS ISSUED PURSUANT TO: (Specify authority) THE CHANGES SET FORTH IN ITEM 14 ARE MADE IN THE CONTRACT ORDER NO. IN ITEM 10A.							
B. THE ABOVE NUMBERED CONTRACT/ORDER IS MODIFIED TO REFLECT THE ADMINISTRATIVE CHANGES (such as changes in paying office, appropriation date, etc.) SET FORTH IN ITEM 14, PURSUANT TO THE AUTHORITY OF FAR 43.103(B).							
X C. THIS SUPPLEMENTAL AGREEMENT IS ENTERED INTO PURSUANT TO AUTHORITY OF: 52.243-1, Changes.							
D. OTHER (Specify type of modification and authority)							
E. IMPORTANT: Contractor <input type="checkbox"/> is not, <input checked="" type="checkbox"/> is required to sign this document and return <u>1</u> copies to the issuing office.							
14. DESCRIPTION OF AMENDMENT/MODIFICATION (Organized by UCF section headings, including solicitation/contract subject matter where feasible.) Modification Control Number: m2ct9drc171696 The purpose of this modification is to revise the SOW to incorporate an additional (b) (7)(E) miles of hydraulic analysis. This additional effort will increase the total obligation amount by \$491,967.89. This modification is IAW FAR 52.243-1, Changes. All other terms and conditions remain unchanged.							
Except as provided herein, all terms and conditions of the document referenced in Item 9A or 10A, as heretofore changed, remains unchanged and in full force and effect							
15A. NAME AND TITLE OF SIGNER (Type or print) (b) (6) Associate Vice President				16A. NAME AND TITLE OF CONTRACTING OFFICER (Type or print) T (b) (6) EMAIL: (b) (6)			
15B. CO (b) (6) (Signature of person authorized to sign)		15C. DATE SIGNED 9/7/2017		16B. UNITED STATES OF AMERICA BY (Signature of Contracting Officer)		16C. DATE SIGNED	

SECTION SF 30 BLOCK 14 CONTINUATION PAGE

SUMMARY OF CHANGES

SECTION SF 30 - BLOCK 14 CONTINUATION PAGE

The following have been added by full text:

REVISED SOW

**A-E TASK ORDER - STATEMENT OF
WORK**

Task Order under Contract No. W9126G-15-D-0009 - Michael Baker &
Associates Architect and Engineer Services for the Design of Floodwall,
Fence, Roads, Drainage, & Lights at Rio Grande Valley & San
Diego FY17, P2 465132, ATS: SWF-17-0799

Date: 17 May 2017

Modification 1: 11 August 2017

(b) (5), (b) (7)(E)



(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK


Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)




A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

Architect and Engineer Services for the Design of Floodwall,

(b) (5)



A-E TASK ORDER - STATEMENT OF WORK


Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)



A-E TASK ORDER - STATEMENT OF WORK


Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)




A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

Architect and Engineer Services for the Design of Floodwall.


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK


Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

Architect and Engineer Services for the Design of Floodwall.


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK


Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)




t
a
r
c

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5), (b)(6);(b)(7)(C)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall.


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)




A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

Architect and Engineer Services for the Design of Floodwall.

(b) (5)




A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

Architect and Engineer Services for the Design of Floodwall.

(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall.

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK


Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)



A-E TASK ORDER - STATEMENT OF WORK


Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK


Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall.


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK


Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall.

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)




A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

Architect and Engineer Services for the Design of Floodwall,


(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK


Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)



A-E TASK ORDER - STATEMENT OF WORK


Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)



A-E TASK ORDER - STATEMENT OF WORK


Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)




A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

Architect and Engineer Services for the Design of Floodwall,

(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

Architect and Engineer Services for the Design of Floodwall,


(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

Architect and Engineer Services for the Design of Floodwall,

(b) (5), (b) (7)(E)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK


Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall.

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK


Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)




A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

Architect and Engineer Services for the Design of Floodwall,

(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009

Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,


(b) (5)



A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)



A-E TASK ORDER - STATEMENT OF WORK



Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (5)

A-E TASK ORDER - STATEMENT OF WORK


Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

Appendix A

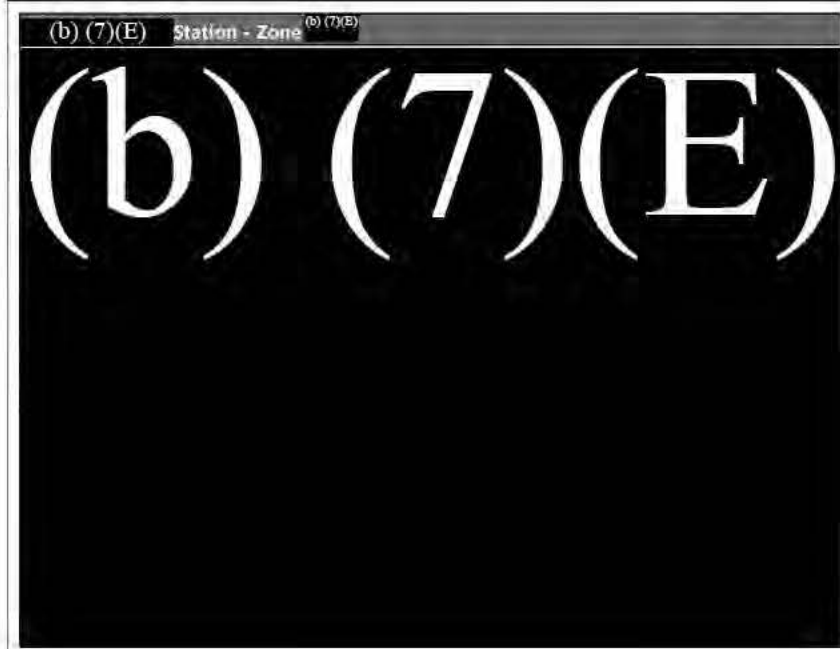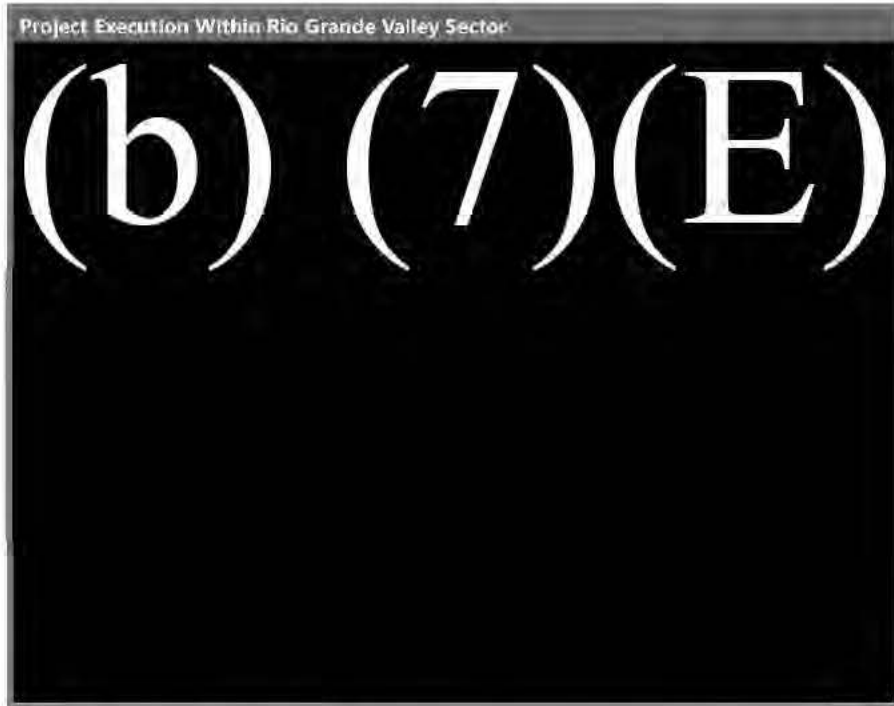

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall.

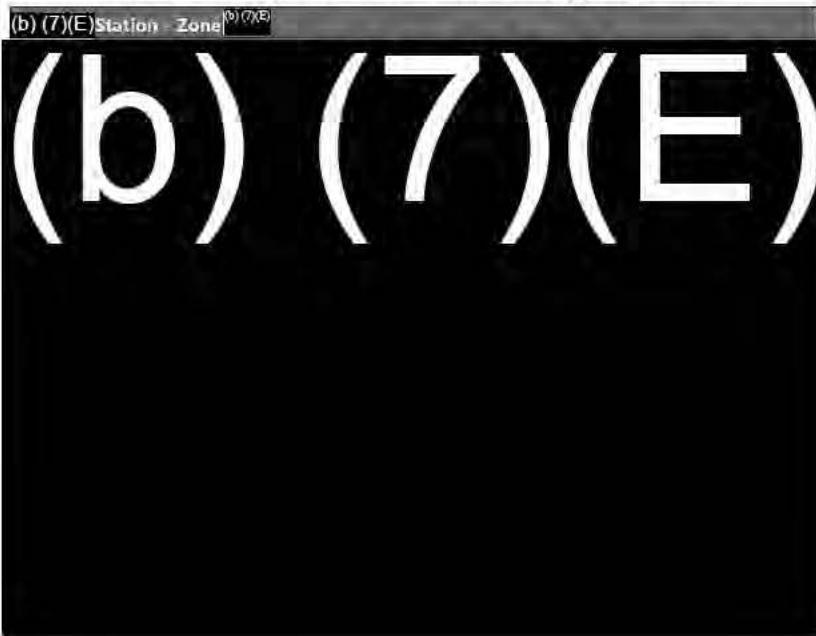

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

(b) (7)(E) Station - Zone (b) (7)(E)
(b) (7)(E)

(b) (7)(E) Station - Zone (b) (7)(E)
(b) (7)(E)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall.

(b) (7)(E) Station - Zone (b) (7)(E)
(b) (7)(E)

(b) (7)(E) Station - Zone (b) (7)(E)
(b) (7)(E)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall.

(b) (7)(E) Station - Zone (b) (7)(E)
(b) (7)(E)



(b) (7)(E) Station - Zone (b) (7)(E)
(b) (7)(E)

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall.


Appendix B

SDC BIS Primary Fence Replacement Map (~14 miles)

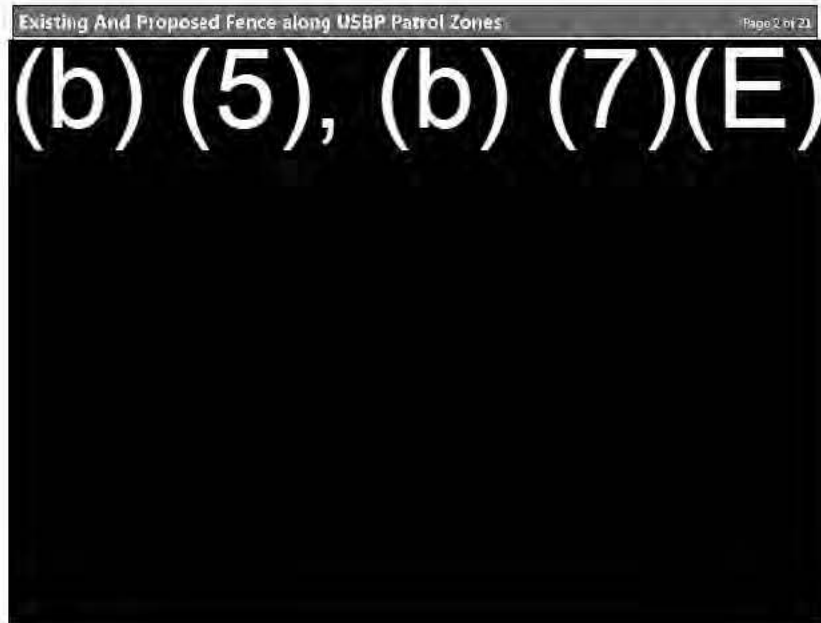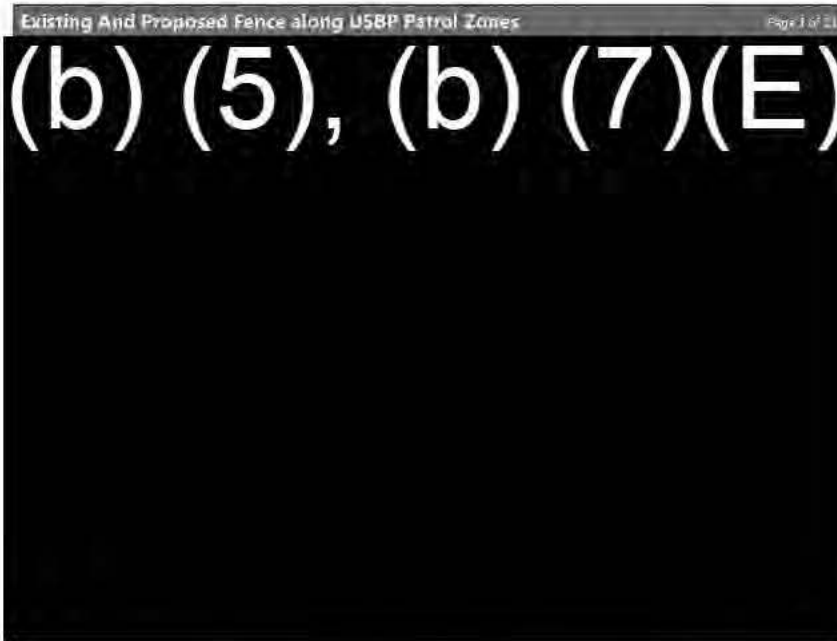


A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall.

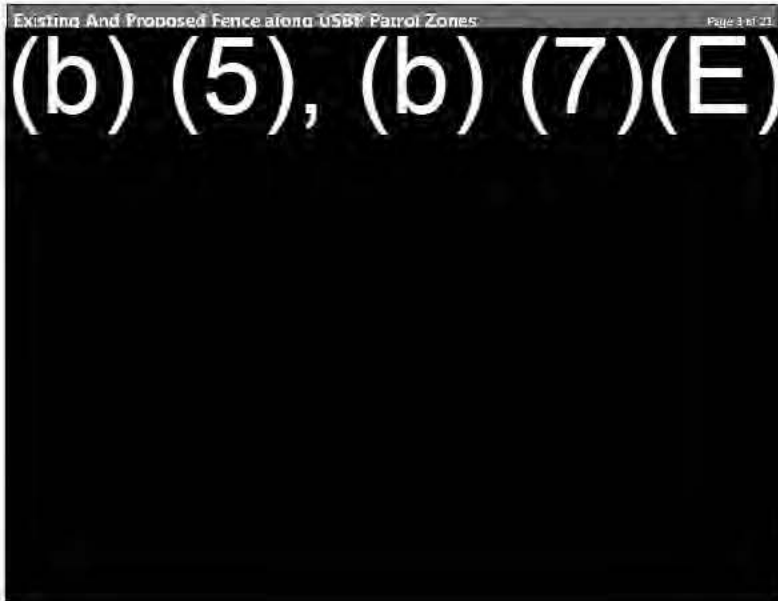


ELC (b) (7)(E) Primary Fence Replacement Map (b) (7)(E) miles)

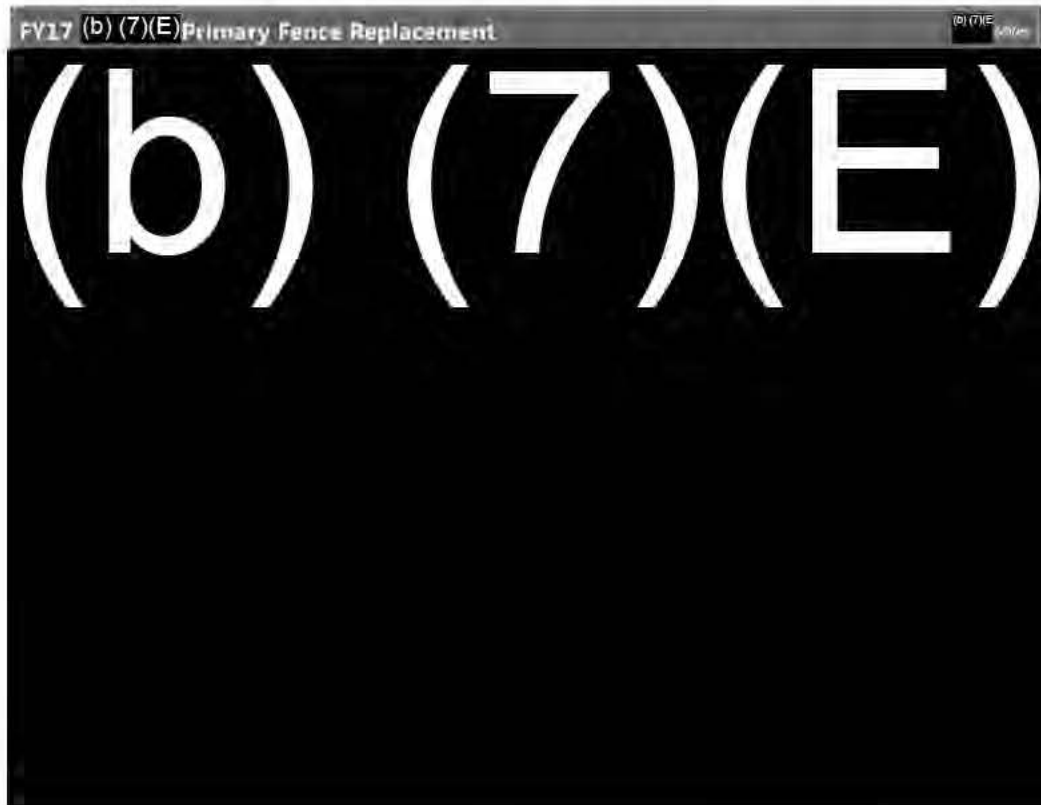

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,



ELP (b) (7)(E) Primary Fence Replacement Map ((b) (7)(E) miles)

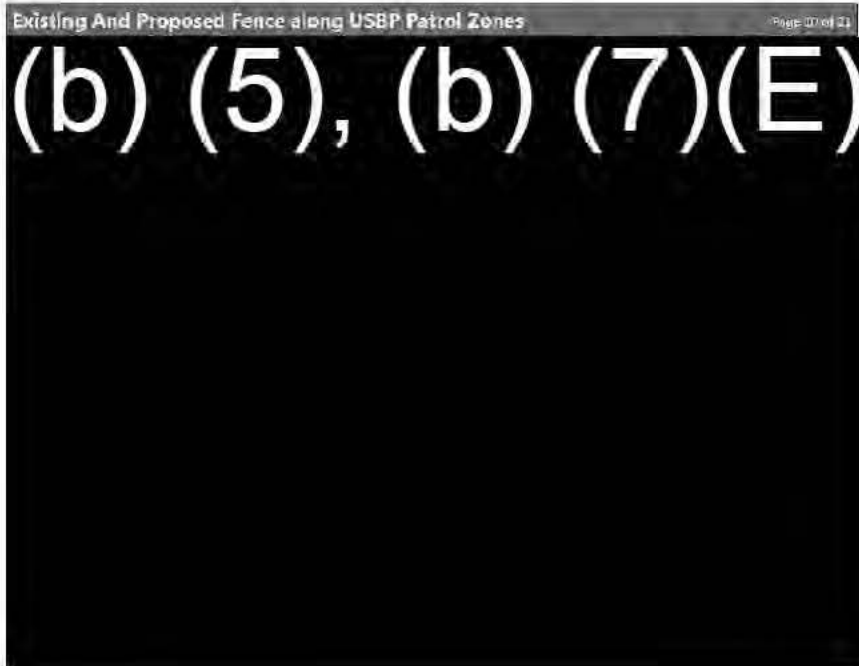

A-E TASK ORDER - STATEMENT OF WORK



Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall.

ELP Vehicle Fence to Primary Fence Replacement Map ((b) (7)(E) miles)

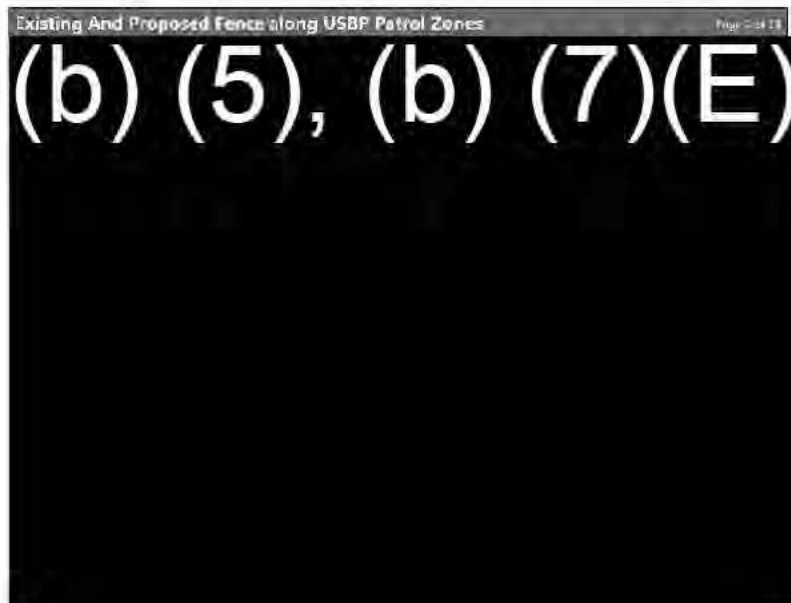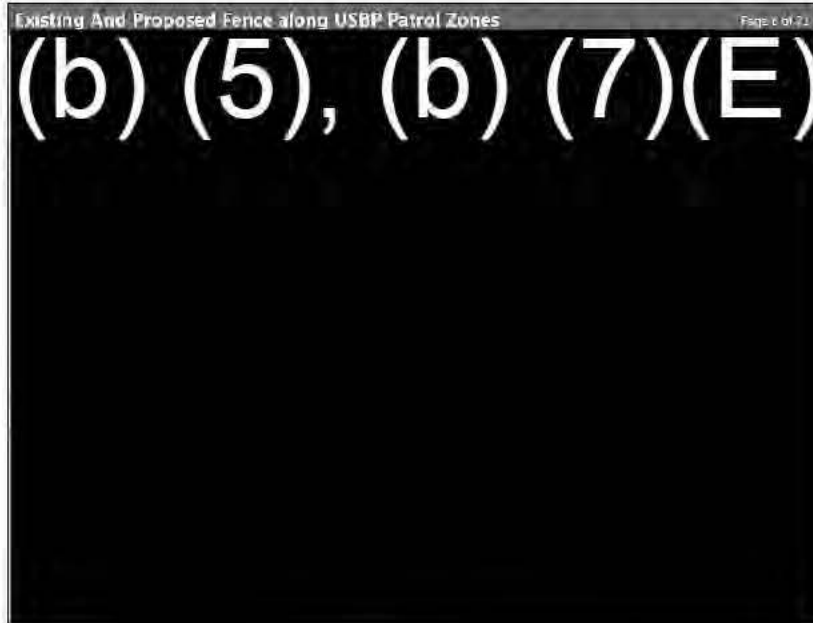

A-E TASK ORDER - STATEMENT OF WORK

Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall,

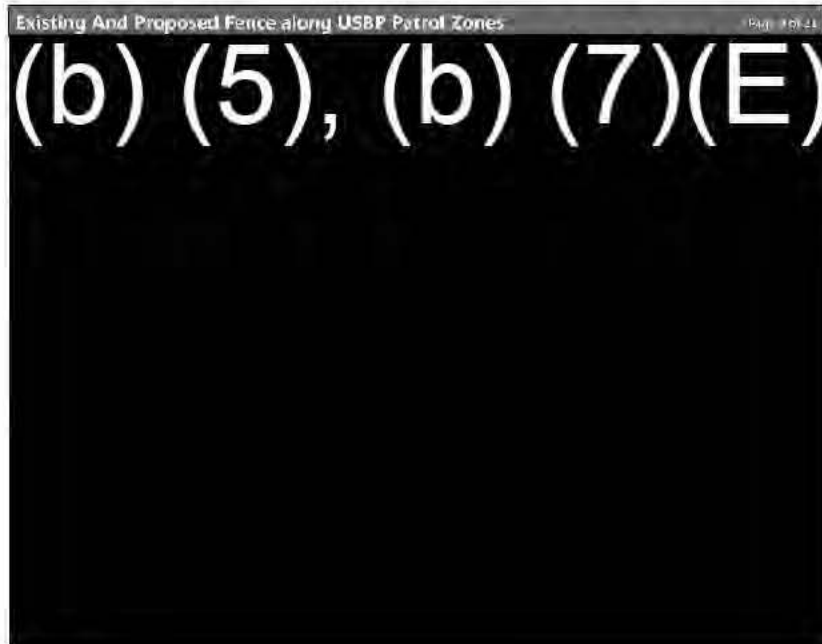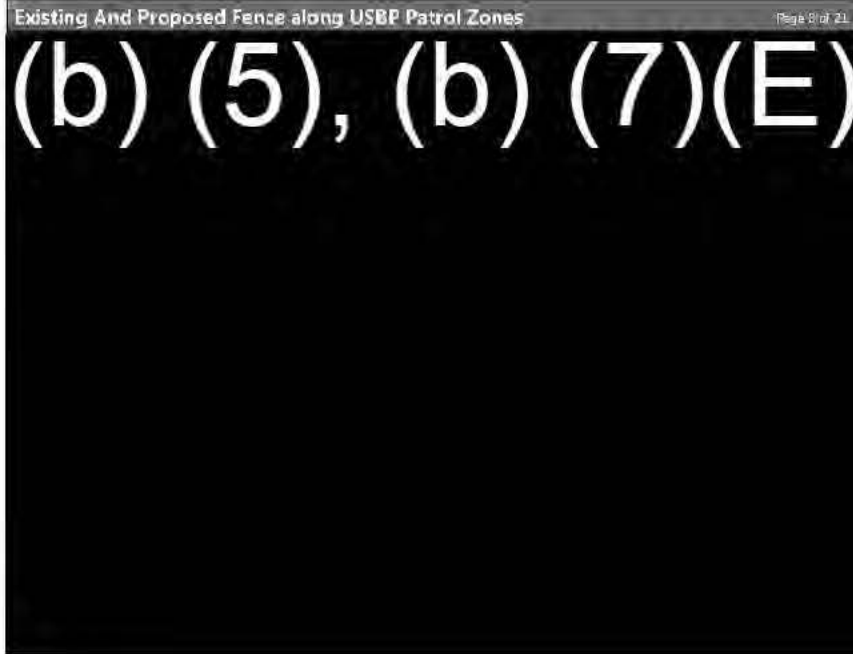


A-E TASK ORDER - STATEMENT OF WORK


Task Order under Contract No. W9126G-15-D-0009
Architect and Engineer Services for the Design of Floodwall.

Appendix C

RGV-^{(b) (7)(E)} & RGV-^{(b) (7)(E)} Map

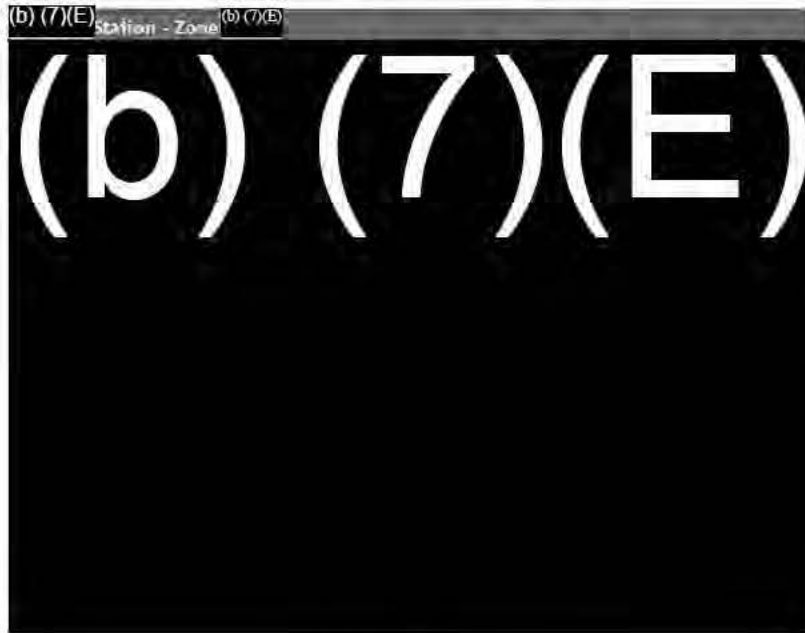

RGV-^{(b) (7)(E)} MAP

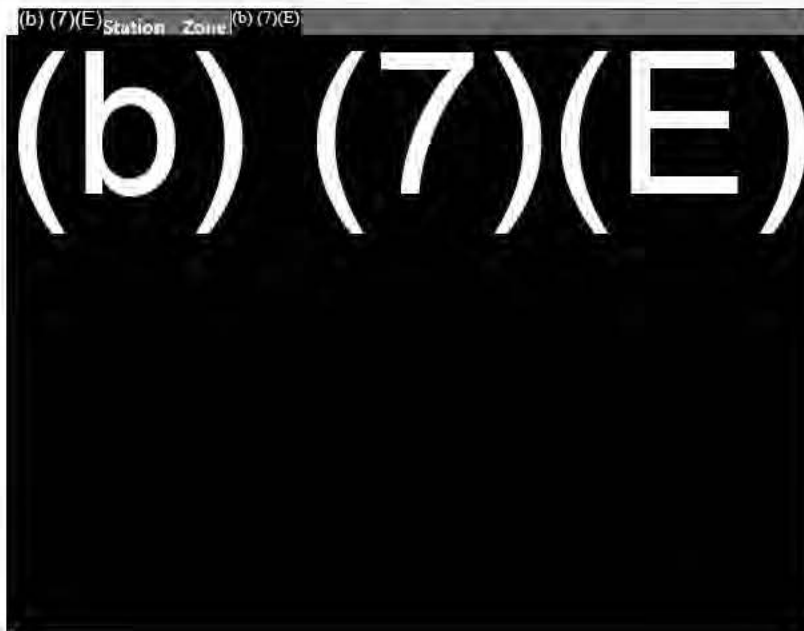


RGV (b) (7)(E) MAP

(b) (7)(E) Station - Zone (b) (7)(E)
(b) (7)(E)

(b) (5)

(b) (5)

(b) (5)



From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: Prototype Location Information for OTIA..

Date: Wed Sep 06 2017 09:09:29 EDT

Attachments: image001.jpg

Hello (b)(6);(b)(7)(C)

As for both the Prototype site and the SDC Fence Replacement project (~14 miles) moves forward, please ensure my PM, (b)(6);(b)(7)(C), and myself are the primary points of contact. Because of all of the moving parts communication has to be very clear, especially as it pertains to locations of this equipment. Most of the project (s) footprint is very tight and we need to avoid construction contractor conflicts with egress / ingress and work flow to avoid Government incurred delays.

Thanks and we will make sure we accommodate the equipment as requested.

Respectfully,

(b)(6);(b)(7)(C)

Eastern Corridors Division Director

Border Patrol and Air Marine Operations Program Management Office

Facilities Management and Engineering

Mobile: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 05, 2017 2:49 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Prototype Location Information for OTIA..

Thank you very much...

(b)(6);(b)(7)(C)

Acting Director

CBP/ES/OIT/WSPD

BB (b)(6);(b)(7)(C)

Office (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 5, 2017 2:31 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Re: Prototype Location Information for OTIA..

Here is google earth shot

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 5, 2017 2:12:03 PM

To: (b)(6);(b)(7)(C)

P.;

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [EXTERNAL] RE: Prototype Location Information for OTIA..

Are they in one location and stretched for 15 miles or just in a small tight location? Like maybe 5 miles total?

Thank you

(b)(6);(b)(7)(C)

Acting Director

CBP/ES/OIT/WSPD

BB (b)(6);(b)(7)(C)

Office (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 5, 2017 1:48 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Re: Prototype Location Information for OTIA..

The site is approximately 2 miles EAST of Otay port

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 5, 2017 12:24:07 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [EXTERNAL] RE: Prototype Location Information for OTIA..

All,

Just for a little background.

EAC Kolbe request a (b) (5), (b) (7)(E)

(b) (5), (b) (7)(E)

Thanks in advance.

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Acting Director
CBP/ES/OIT/WSPD
BB (b)(6);(b)(7)(C)
Office (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 5, 2017 12:14 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Prototype Location Information for OTIA..

Importance: High

Thanks Gents,

It's actually OIT, we have a data call request from the EAC where we need to know the location of the wall/fence prototypes.

The quicker we can get this info the better.

Thanks!

Respectfully,

(b)(6);(b)(7)(C)

Branch Director, Resource Logistics

Wireless Systems Program Division

Office of Information and Technology

Enterprise Services

Customs and Border Protection, DHS

(W) (b)(6);(b)(7)(C)

(C) (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 5, 2017 11:39 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Prototype Location Information for OTIA..

I'm also including (b)(6);(b)(7)(C) who should be able to help.

Thank you,

(b)(6);(b)(7)(C)

Property Analyst

E3 Federal Solutions

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering (FM&E)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 5, 2017 11:38 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Prototype Location Information for OTIA..

Importance: High

(b)(6);(b)(7)(C)

OTIA called asking for the location of the Prototype in San Diego.

I let them know that you would be able to answer the specific request.

(b)(6);(b)(7)(C) is on the email.

Please get with him with the specific information.

Regards,

(b)(6);(b)(7)(C) CBM, PMP

Director-Real Estate, Environmental and Leasing Services (REEL)

Border Patrol Air & Marine Program Management Office (BPAM PMO)

DHS-CBP-ES-FM&E

(b)(6);(b)(7)(C) (cell)

From:
To:

(b)(6);(b)(7)(C)

Cc:

Bcc:
Subject: Re: Prototype Location Information for OTIA..
Date: Tue Sep 05 2017 14:30:57 EDT
Attachments: image001.jpg
Photo 1.jpg

Here is google earth shot

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)
Sent: Tuesday, September 5, 2017 2:12:03 PM
To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Cc: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Subject: [EXTERNAL] RE: Prototype Location Information for OTIA..

Are they in one location and stretched for 15 miles or just in a small tight location? Like maybe 5 miles total?

Thank you

(b)(6);(b)(7)(C)
Acting Director
CBP/ES/OIT/WSPD
BB (b)(6);(b)(7)(C)
Office (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Tuesday, September 5, 2017 1:48 PM
To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Re: Prototype Location Information for OTIA..

The site is approximately 2 miles EAST of Otay port

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)
Sent: Tuesday, September 5, 2017 12:24:07 PM
To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)
Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [EXTERNAL] RE: Prototype Location Information for OTIA..

All,

Just for a little background.

EAC Kolbe request a (b) (5), (b) (7)(E)

(b) (5), (b) (7)(E)

Thanks in advance.

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Acting Director

CBP/ES/OIT/WSPD

BB (b)(6);(b)(7)(C)

Office (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 5, 2017 12:14 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Prototype Location Information for OTIA..

Importance: High

Thanks Gents,

It's actually OIT, we have a data call request from the EAC where we need to know the location of the wall/fence prototypes.

The quicker we can get this info the better.

Thanks!

Respectfully,

(b)(6);(b)(7)(C)

Branch Director, Resource Logistics

Wireless Systems Program Division

Office of Information and Technology

Enterprise Services

Customs and Border Protection, DHS

(W) (b)(6);(b)(7)(C)

(C) (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 5, 2017 11:39 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Prototype Location Information for OTIA..

I'm also including (b)(6);(b)(7)(C) who should be able to help.

Thank you,

(b)(6);(b)(7)(C)

Property Analyst

E3 Federal Solutions

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering (FM&E)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 5, 2017 11:38 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Prototype Location Information for OTIA..

Importance: High

(b)(6);(b)(7)(C)

OTIA called asking for the location of the Prototype in San Diego.

I let them know that you would be able to answer the specific request.

(b)(6); (b)(7)(C) is on the email.

Please get with him with the specific information.

Regards,

(b)(6);(b)(7)(C) CBM, PMP

Director-Real Estate, Environmental and Leasing Services (REEL)

Border Patrol Air & Marine Program Management Office (BPAM PMO)

DHS-CBP-ES-FM&E

(b)(6);(b)(7)(C)(cell)

Site Overview: Prototype Site

(b) (7)(E)

~~For Official Use Only (FOUO)~~

From:
To:

(b)(6);(b)(7)(C)

Cc:

Bcc:
Subject: Re: Prototype Location Information for OTIA..
Date: Tue Sep 05 2017 14:24:47 EDT
Attachments: image001.jpg

I'm in meeting but trying to find slide. They are all within 800' of each other

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)
Sent: Tuesday, September 5, 2017 2:12:03 PM
To: (b)(6);(b)(7)(C)
P.;
Cc: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Subject: [EXTERNAL] RE: Prototype Location Information for OTIA..

Are they in one location and stretched for 15 miles or just in a small tight location? Like maybe 5 miles total?

Thank you

(b)(6);(b)(7)(C)

Acting Director

CBP/ES/OIT/WSPD

BB (b)(6);(b)(7)(C)

Office (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 5, 2017 1:48 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Re: Prototype Location Information for OTIA..

The site is approximately 2 miles EAST of Otay port

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 5, 2017 12:24:07 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [EXTERNAL] RE: Prototype Location Information for OTIA..

All,

Just for a little background.

EAC Kolbe request (b) (5), (b) (7)(E)

(b) (5), (b) (7)(E)

Thanks in advance.

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Acting Director

CBP/ES/OIT/WSPD

BB (b)(6);(b)(7)(C)

Office (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 5, 2017 12:14 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Prototype Location Information for OTIA..

Importance: High

Thanks Gents,

It's actually OIT, we have a data call request from the EAC where we need to know the location of the wall/fence prototypes.

The quicker we can get this info the better.

Thanks!

Respectfully,

(b)(6);(b)(7)(C)

Branch Director, Resource Logistics

Wireless Systems Program Division

Office of Information and Technology

Enterprise Services

Customs and Border Protection, DHS

(W)(b)(6);(b)(7)(C)

(C)(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 5, 2017 11:39 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Prototype Location Information for OTIA..

I'm also including (b)(6);(b)(7)(C) who should be able to help.

Thank you,

(b)(6);(b)(7)(C)

Property Analyst

E3 Federal Solutions

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering (FM&E)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, September 5, 2017 11:38 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Prototype Location Information for OTIA..

Importance: High

(b)(6);(b)(7)(C)

OTIA called asking for the location of the Prototype in San Diego.

I let them know that you would be able to answer the specific request.

(b)(6);(b)(7)(C) is on the email.

Please get with him with the specific information.

Regards,

(b)(6);(b)(7)(C) CBM, PMP

Director-Real Estate, Environmental and Leasing Services (REEL)

Border Patrol Air & Marine Program Management Office (BPAM PMO)

DHS-CBP-ES-FM&E

(b)(6);(b)(7)(C)(cell)

From:

(b)(6);(b)(7)(C)

To:

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc:

Bcc:

Subject: RE: Sept 12 Proposed Agenda
Date: Thu Aug 31 2017 13:11:48 EDT

Attachments:

(b)(6);(b)(7)(C)

(b) (5)

(b)(6);(b)(7)(C)

Senior Attorney (Trade & Finance)

Office of Chief Counsel

U.S. Customs and Border Protection

1300 Pennsylvania Avenue, NW Room 4.4B

Washington, DC 20229

Tel: (b)(6);(b)(7)(C)

Fax: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

ATTORNEY-CLIENT PRIVILEGED/ATTORNEY WORK PRODUCT

~~This communication might contain communications between attorney and client, communications that are part of the agency deliberative process, or attorney work product, all of which are privileged and not subject to disclosure outside the agency or to the public. Please consult with the Office of Chief Counsel, U.S. Customs and Border Protection before disclosing any information contained in this email.~~

From (b)(6);(b)(7)(C)

Sent: Wednesday, August 23, 2017 6:50 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Sept 12 Proposed Agenda

Team,

Please find the attached proposed Agenda for your review and comment. Please let me know where the team would like to go for site visit(s) in the afternoon.

Respectfully,

(b)(6);(b)(7)(C) P.E. LEED AP BD+C

Program Manager

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

<< File: AGENDA_RGV Barrier Real Estate Planning_12SEP2017_V1.docx >>

From:

(b)(6);(b)(7)(C)

To:

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc:

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

Bcc:

Subject:

RE: CBP Meeting with BNSF - El Paso Fence Replacement

Date:

Thu Aug 31 2017 11:10:05 EDT

Attachments:

Just dialed in - set up on conference room

All times listed are in the following time zone:(UTC-06:00) Central Time (US & Canada)

-----Original Appointment-----

From: (b)(6);(b)(7)(C)

Sent: 8/25/2017 9:06:19 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6) (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: CBP Meeting with BNSF - El Paso Fence Replacement
Where: (b)(6);(b)(7)(C) (b) (7)(E)

~~*~*~*~*~*~*~*

(b) (7)(E) Project Agenda - BNSF.docx (b) (7)(E) Project Meeting - BNSF 08282017.pptx

From:

(b)(6);(b)(7)(C)

To:

[Redacted]

(b)(6);(b)(7)(C)

Cc:
Bcc:
Subject: 8/24/17 (b) (7)(E) IPT - Minutes
Date: Thu Aug 31 2017 08:34:44 EDT
Attachments: (b) (7)(E) IPT Minutes 082417.docx
CWEmbed1.doc

All,

Attached are the notes/minutes from the 8/24/2017 (b) (7)(E) IPT meeting.

<(b) (7)(E) IPT Minutes 082417.docx>>

V/r,

(b)(6);(b)(7)(C) PMP

(Contractor, ManTech Team)

Program Analyst

(b) (7)(E)

U.S. Customs and Border Protection

.....
Office: (b)(6);(b)(7)(C)

-----Original Appointment-----

From: (b)(6);(b)(7)(C)

Sent: Thursday, August 17, 2017 3:37 PM

To:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: (b)(7)(E) IPT

When: Thursday, August 24, 2017 2:00 PM-3:00 PM (UTC-05:00) Eastern Time (US & Canada).

Where: Call in: (b)(6);(b)(7)(C) Pin: (b)(7)(E)

Purpose: To discuss current status, upcoming event/milestones, and update action items occurring on the (b)(7)(E) Program

(Previously named (b)(7)(E))

Occurrence: Monthly; Every 4 weeks

Time: 2:00pm – 3:00pm (Eastern)

Room: Crystal City, 1901 S. Bell Street Room (b)(7)(E)

Agenda: To be sent out before each meeting

Contact Information: (b)(6);(b)(7)(C) Program Manager, (b)(7)(E) (b)(6);(b)(7)(C)

**Please do not forward this invite. If you need to be removed from this invite or would like to add someone, please contact (b)(6);(b)(7)(C)

**(b)(7)(E) Program
IPT Agenda – 24 August 2017**



U.S. Customs and
Border Protection

(b) (5)

- b. El Centro **(b)(7)(E)** Miles
 - i. All specs submitted at this time from USBP PMO / S&T to BPAM
 - ii. RFP nearly complete
 - iii. A "hut" near the PoE will be constructed
- c. San Diego **(b)(7)(E)** Miles
 - i. All specs submitted at this time from USBP PMO / S&T to BPAM
- d. El Paso **(b)(7)(E)** Miles
 - i. All specs submitted at this time from USBP PMO / S&T to BPAM
- e. TBD Remaining FR Miles
- 3. The Border Wall Deployments
 - a. RGV Levee – **(b)(7)(E)** Miles [change from **(b)(7)(E)** to **(b)(7)(E)** mi]
 - b. RGV Primary Wall – **(b)(7)(E)** Miles
 - c. **(b) (5)** The only activity funded is AE for Levee
- 4. Stand Alone Deployments
 - a. Laredo – **(b)(7)(E)**
- ii. Program Management
 - 1. Program Name Change Approved to **(b)(7)(E)**
 - 2. Program Acquisition Documentation
- DALS Process
 - a. DALS Artifacts (being approved by others)
 - i. CAR – Delivered to CRD 7/3/17
 - ii. MNS – Adjudicating comments (received very late comments)
 - iii. Top Level CONOPS – Adjudicating comments (received very late comments)
 - iv. ORDs – 3 ORDs to be delivered after CAR validation and CONOPS comments have been adjudicated
 - b. Operational Procurement Packages
 - i. Direction Memo – Signature routing to resume week of 8/28/17
 - 1. KPPs
 - 2. COIs/MOEs/MOPs – ACTION: Set up meeting to discuss
 - ii. Alternatives Analysis (AA)
 - 1. To be awarded by September
 - 2. **(b)(7)(E)** stated can do 1-day demos to compare vendor products
 - iii. Acquisition Plan
 - iv. Acq. Program Baseline
 - v. LCCE
 - vi. Capability Based ORD
 - vii. Capability Based CONOPS
 - c. Functional Requirement

(b)(7)(E) Program
IPT Agenda – 24 August 2017



U.S. Customs and
Border Protection

i. Being developed by SE- has not had official kick off. Waiting for the AA to be completed

d. IPT Charter

i. Ready to be sent out for signature

e. Risk Management Plan

f. TEMP

g. ILSP – FAA to assist

h. CEBD

i. Configuration Management Plan

j. SELC Tailoring Plan

k. Project Management Plan (PMP)

iii. Pilots / Demonstration

1. Future Vendor Demonstrations: RFI and Demonstration (to feed into AA; NLT October 2017)
2. Optasense deployed in July 2017 in San Diego – no cost demonstration; need to work with the field for a test plan as needed.
3. Updates to Army DoD (b) (7)(E) – Due to the fence replacement project, (b)(7)(E) system in San Diego and El Centro will be impacted.

iv. Facility Laydown Plan and Specs for "Brain Box"

1. USBP is working on gather all OFO and USBP facilities available. Work with (b)(6);(b)(7)(C) regarding laydown. A facility plan for (b)(7)(E) is needed (cost, specs, power, etc.)
2. (b)(7)(E)
3. (b)(7)(E) does not have power. (b)(7)(E) stated (b)(7)(E) will go to export vehicle building at (b)(7)(E)

v. Future Sustainment

(b) (5), (b) (7)(E)

c. Upcoming Briefs / Travel

3. Border Patrol Updates / Concern (b)(6); (b)(7)(C)

a. Updates

4. Schedule (b)(6); (b)(7)(C) w]

- a. IMS / Major Upcoming Milestones – Draft IMS is available and under review with PM PMC/Scheduler need to meet
 - i. S&T Pilot Schedule
 - ii. Fence Replacement Schedule needs from (b)(7)(E)

(b)(7)(E) Program IPT Agenda – 24 August 2017



U.S. Customs and
Border Protection

iii. The Border Wall Schedule needs from (b)(7)(E)

iv. Overall Planning for Facility ("Brain Box") Schedule

- b. Coordination Meeting between S&T Lead (b)(6); (b)(7)(C) and (b)(7)(E) Program Scheduler/Program Manager – TBD

5. Budget / Execution Plan / Cost Estimates (b)(6); (b)(7)(C) n]

- a. CPE Development – Initial meeting held 8/23/2017
- b. Border Wall CEBD drafted.
- c. (b) (5)

6. Contractin (b)(6);(b)(7)(C) s]

- a. S&T IAA with USBP (executing S&T Pilot Projects)
 - i. Contract Extension Needed by 8/31/2017. S&T has IAA paperwork for signature
- b. RFI for future Demonstrations and AA Data Collection
 - i. Getting NTT Data on contract
- c. Future Contract needs (?)

7. Systems Engineerin (b)(6);(b)(7)(C) ?]

- a. SELC Tailoring Plan

8. OFAM Updates

9. New Business / Open Forum [All]

10. Action Items (b)(6); (b)(7)(C) o]

From:

(b)(6);(b)(7)(C)

To:

(b) (6)
(b) (6) (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C) (b) (6)
(b) (6)
(b)(6);(b)(7)(C)
(b) (6) (b) (6)
(b) (6) (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc:

(b) (6) (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
(b) (6)
(b) (6) (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Bcc:

Subject: RE: CBP Meeting with Union Pacific - El Paso Replacement Fence
Date: Wed Aug 30 2017 15:43:14 EDT
Attachments:

Hey folks,

Apologies on not calling in on the meeting. We have some coming coordination between the USACE real estate folks and UP. The site location and project plan were clarified. I'll get notes out later today when i am back at a computer.

Thanks!

All times listed are in the following time zone:(UTC-06:00) Central Time (US & Canada)

-----Original Appointment-----

From: (b)(6);(b)(7)(C)

Sent: 8/28/2017 2:34:55 PM

To: (b)(6);(b)(7)(C) (b) (6)
(b)(6);(b)(7)(C) (b) (6)

(b) (6)
(b)(6);(b)(7)(C)

(b) (6)

(b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

Subject: CBP Meeting with Union Pacific - El Paso Replacement Fence
Where: 1500 East Overland, El Paso, TX - (b)(6);(b)(7)(C) / (b) (7)(E)

~~*~*~*~*~*~*~*

(b) (7)(E) Project Meeting - UPRR 08282017.pptx

Team – The meeting will be a short meeting in the Union Pacific Office, then we will drive out to the project site to get eyes on the planned location.

Thanks!

From:

To:

Cc:

(b) (6)
(b)(6);(b)(7)(C)

(b) (6)
(b)(6);(b)(7)(C)
(b)(6);(b)(7)(C) (b) (6)
(b) (6)

Bcc:

Subject: RE: [EXTERNAL] ELP (b) (7)(E) 30% Final RFP review

Date: Wed Aug 30 2017 13:19:07 EDT

Attachments:

(b) (6)

In (b)(6);(b)(7)(C) absence, please socialize (b)(6);(b)(7)(C) comments (below) with the PDT to ascertain any conflicts-- want to try to incorporate these in the final RFP package.

Thank you,

(b) (6)

(b) (6) PMP
Deputy for Programs
USACE - Border Infrastructure PMO
(b) (6)
BB: (b) (6)

NOTICE: ~~Do not release~~ under the Freedom of Information Act, 5 U.S.C. § 552 (FOIA). This message [or document] contains personal and confidential information for the intended recipients and contains pre-decisional advice or information which is protected from disclosure under FOIA. Do not copy or release without prior authorization from the originator. Any review or distribution without consent is strictly prohibited. If you have received this information in error, please notify the sender immediately.

> On Aug 30, 2017, at 9:57 AM, (b) (6)

(b) (6) wrote:

>
> (b)(6);(b)(7)(C) your lead

>
> (b) (6) PMP
> Deputy for Programs
> USACE - Border Infrastructure PMO
> (b) (6)
> BB: (b) (6)
>

> NOTICE: Do not release under the Freedom of Information Act, 5 U.S.C. § 552 (FOIA). This message [or document] contains personal and confidential information for the intended recipients and contains pre-decisional advice or information which is protected from disclosure under FOIA. Do not copy or release without prior authorization from the originator. Any review or distribution without consent is strictly prohibited. If you have received this information in error, please notify the sender immediately.

>
>
> -----Original Message-----

> From: (b)(6);(b)(7)(C)
> Sent: Wednesday, August 30, 2017 10:55 AM
> To: (b) (6)
(b)(6);(b)(7)(C)
(b)(6);(b)(7)(C) (b) (6)
(b) (6)

> Cc: (b) (6)
(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)
> Subject: RE: [EXTERNAL] ELP (b)(7)(E) 30% Final RFP review

>
> As far as I am concerned they can be shared with the team

>
> (b)(6);(b)(7)(C) PE
> LMI
> BPAM Chief Engineer
> (b)(6);(b)(7)(C)

> Sent from Samsung Galaxy

>
> From: (b) (6)
> Sent: Tuesday, August 29, 2017 9:08:55 PM
> To: (b)(6);(b)(7)(C) (b) (6)

(b) (6)
> Cc: (b) (6) (b)(6);(b)(7)(C)

> Subject: Re: [EXTERNAL] ELP (b)(7)(E) 30% Final RFP review

>
> Do any of these merit team discussion, or can we share with team by email to determine if there are any counterpoints?

>
>
>
> From: (b)(6);(b)(7)(C)
> Date: August 29, 2017 at 5:54:17 PM CDT

> To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C) (b) (6)

(b) (6)
(b) (6)
> Cc: (b)(6);(b)(7)(C) (b) (6)
(b)(6);(b)(7)(C) (b) (6)

> Subject: [EXTERNAL] ELP (b) (7)(E) 30% Final RFP review

>

> (b)(6);(b)(7)(C)

>

> Today I conducted a "plans-in-hand" review of the final RFP for the (b) (7)(E) project. Overall the plans look very good. My observations are as follows:

>

>

(b) (5), (b) (7)(E)

>

> (b)(6);(b)(7)(C) P.E., PMP, Chief Engineer

> Border Patrol & Air and Marine (BPAM) PMO

> LMI

> Mobile: (b)(6);(b)(7)(C)

> (b)(6);(b)(7)(C)

>

>

>

>

From:

To:

Cc:

(b) (6)

(b)(6);(b)(7)(C)

(b) (6) (b) (6) (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

Bcc:

Subject:

Re: [EXTERNAL] ELP (b)(7)(C) 30% Final RFP review

Date:

Wed Aug 30 2017 12:02:10 EDT

Attachments:

Adding (b) (6) and (b) (6) to distribution

Sent from my iPhone

> On Aug 30, 2017, at 9:57 AM, (b) (6)

(b) (6) wrote:

>

> (b)(6);(b)(7)(C) your lead

>

> (b) (6) PMP

> Deputy for Programs

> USACE - Border Infrastructure PMO

> (b) (6)

> BB: (b) (6)

>

> NOTICE: Do not release under the Freedom of Information Act, 5 U.S.C. § 552 (FOIA). This message [or document] contains personal and confidential information for the intended recipients and contains pre-decisional advice or information which is protected from disclosure under FOIA. Do not copy or release without prior authorization from the originator. Any review or distribution without consent is strictly prohibited. If you have received this information in error, please notify the sender immediately.

>

>

> -----Original Message-----

> From: (b)(6);(b)(7)(C)

> Sent: Wednesday, August 30, 2017 10:55 AM

> To:

(b) (6)
(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

> Cc:

(b) (6)
(b)(6);(b)(7)(C)

> Subject: RE: [EXTERNAL] ELP (b)(7)(E) 30% Final RFP review

>

> As far as I am concerned they can be shared with the team

>

> (b)(6);(b)(7)(C) PE

> LMI

> BPAM Chief Engineer

> (b)(6);(b)(7)(C)

> Sent from Samsung Galaxy

>

> From: (b) (6)

> Sent: Tuesday, August 29, 2017 9:08:55 PM

> To: (b)(6);(b)(7)(C); (b) (6)

(b) (6)

> Cc: (b) (6); (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

> Subject: Re: [EXTERNAL] ELP (b)(7)(E) 30% Final RFP review

>

> Do any of these merit team discussion, or can we share with team by email to determine if there are any counterpoints?

>

>

> From: (b)(6);(b)(7)(C)

> Date: August 29, 2017 at 5:54:17 PM CDT

> To: (b)(6);(b)(7)(C); (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

> Cc: (b)(6);(b)(7)(C); (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

> Subject: [EXTERNAL] ELP (b)(7)(E) 30% Final RFP review

>

> (b)(6);(b)(7)(C)

>

> Today I conducted a "plans-in-hand" review of the final RFP for the (b)(7)(E) project. Overall the plans look very good. My observations are as follows:

>

>

(b) (5), (b) (7)(E)

(b) (5), (b) (7)(E)

>
> (b)(6);(b)(7)(C) P.E., PMP, Chief Engineer
> Border Patrol & Air and Marine (BPAM) PMO
> LMI
> Mobile: (b)(6);(b)(7)(C)
> (b)(6);(b)(7)(C)
>
>
>
>

From:

(b) (6)

To:

(b)(6);(b)(7)(C)

Cc:

(b) (6)

(b)(6);(b)(7)(C)

Bcc:

Subject: RE: [EXTERNAL] ELP (b)(7)(E) 30% Final RFP review

Date: Wed Aug 30 2017 11:57:00 EDT

Attachments:

(b)(6);(b)(7)(C) your lead

(b) (6)

PMP

Deputy for Programs

USACE - Border Infrastructure PMO

(b) (6)

BB: (b) (6)

NOTICE: Do not release under the Freedom of Information Act, 5 U.S.C. § 552 (FOIA). This message [or document] contains personal and confidential information for the intended recipients and contains pre-decisional advice or information which is protected from disclosure under FOIA. Do not copy or release without prior authorization from the originator. Any review or distribution without consent is strictly prohibited. If you have received this information in error, please notify the sender immediately.

-----Original Message-----

From: (b)(6);(b)(7)(C)

Sent: Wednesday, August 30, 2017 10:55 AM

To:

(b) (6)
(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

Cc:

(b) (6)

(b)(6);(b)(7)(C)

Subject: RE: [EXTERNAL] ELP (b)(7)(E) 30% Final RFP review

As far as I am concerned they can be shared with the team

(b)(6);(b)(7)(C) PE

LMI

BPAM Chief Engineer

(b)(6);(b)(7)(C)

Sent from Samsung Galaxy

From: (b) (6)

Sent: Tuesday, August 29, 2017 9:08:55 PM

To: (b)(6);(b)(7)(C)

(b) (6)

(b) (6)

Cc: (b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Re: [EXTERNAL] ELP (b)(7)(E) 30% Final RFP review

Do any of these merit team discussion, or can we share with team by email to determine if there are any counterpoints?

From: (b)(6);(b)(7)(C)

Date: August 29, 2017 at 5:54:17 PM CDT

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

Subject: [EXTERNAL] ELP (b)(7)(E) 30% Final RFP review

(b)(6);(b)(7)(C)

Today I conducted a "plans-in-hand" review of the final RFP for the (b)(7)(E) project. Overall the plans look very good. My observations are as follows:

(b) (5), (b) (7)(E)

(b) (5), (b) (7)(E)

(b)(6);(b)(7)(C) P.E., PMP, Chief Engineer
Border Patrol & Air and Marine (BPAM) PMO
LMI

Mobile: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From:

(b)(6);(b)(7)(C)

To:

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc:

Bcc:

Subject: RE: EPT (b) (7)(E) RF - El Paso Fence Replacement Project

Date: Tue Aug 29 2017 12:58:14 EDT

Attachments: image001.png

Thanks,

(b)(6);(b)(7)(C)

V/R,

(b)(6);(b)(7)(C)

Operations Officer

El Paso Sector | Program Management Office

Office: (b)(6);(b)(7)(C)

iPhone: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, August 29, 2017 10:54 AM

To:

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

Cc:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: EPT (b)(7)(E) RF - El Paso Fence Replacement Project

Good morning,

(b) (7)(E) Station has provided comments in red below. Please let me know if there are any questions.

Thank you,

From: (b)(6);(b)(7)(C)

Sent: Tuesday, August 29, 2017 5:49 AM

To:

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

Subject: RE: EPT (b)(7)(E) RF - El Paso Fence Replacement Project

All

Yesterday (b)(6) and myself conducted a comprehensive "plans-in-hand" review of the latest version of the 30% design. Our comments were annotated on drawings that we will distribute shortly (need to convert them to pdf). In the meantime, provided below is a summary of our observations. Baker is planning to update the drawings before they are released for bid later this week.

(b) (7) (E)

(b) (5)

We can discuss the above on Thursday's call but we'd like feedback from Border Patrol on item #1 soonest.

Best,

(b)(6);(b)(7)(C)

-----Original Message-----

From: (b) (6)

(b) (6)

Sent: Tuesday, August 22, 2017 12:23 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: FW: EPT (b)(7)(E) RF - El Paso Fence Replacement Project Corrected Final Submittal (UNCLASSIFIED)

CLASSIFICATION: UNCLASSIFIED

All,

Once you have reviewed the Corrected Final RFP from Michael Baker Corporation for the El Paso Replacement Fence Project please let me know what comments I can close out for you in the Draft 35% review and which have not been addressed and need to remain open.

Thanks,

(b) (6) PMP

Military and Operations Project Manager

USACE-ABQ District

4101 Jefferson Plaza

Albuquerque, NM 87109

Desk: (b) (6)

BB: (b) (6)

E-mail: (b) (6)

-----Original Message-----

From: (b) (6)

Sent: Tuesday, August 22, 2017 12:18 AM

To: (b)(6);(b)(7)(C); (b) (6)

(b) (6) (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) (b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b) (6)

(b) (6)

Subject: [Non-DoD Source] EPT (b) (7)(E) RF - El Paso Fence Replacement Project Corrected Final Submittal

All,

The Corrected Final RFP submittal for EPT (b) (7)(E) RF - El Paso Fence Replacement RFP is available. You can download the RFP document and HEC-RAS models and by clicking the links below.

RFP Document (includes plans, geotechnical and drainage reports):

(b)(7)(E)

HEC-RAS models:

(b)(7)(E)

Flowmaster Files:

(b)(7)(E)

Let me know if you have any questions or problems accessing the submittal.

Thank you,

(b) (6)

(b) (6) P.E., LEED-AP | Senior Associate | Michael Baker International

2929 N. Central Avenue, Suite 800 | Phoenix, AZ 85012 | d: (b) (6) | c: (b) (6)
(b) (6) | Blockedwww.mbakintl.com
<Blockedhttp://www.mbakintl.com/>

(b)(7)(E)

CLASSIFICATION: UNCLASSIFIED

From:

(b)(6);(b)(7)(C)

To:

Cc:

(b) (6)

(b) (6)

Bcc:

Subject: RE: USACE Security On Replacement Projects

Date: Tue Aug 29 2017 12:29:37 EDT

Attachments:

Thanks (b)(6);(b)(7)(C) We will get the el paso poc for this asap.

From (b)(6);(b)(7)(C)

Sent: Thursday, August 24, 2017 11:43:26 AM

To: (b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C) (b) (6)

(b) (6)

Subject: USACE Security On Replacement Projects

(b)(6);(b)(7)(C) and (b)(6);(b)(7)(C) I wanted to give you update. I had the call with (b) (6) and (b) (6) USACE is reviewing/revising their approach on security for BP projects. Based on higher concerns/publicity, each district is likely going to have a higher security involvement and review the RFP for security procedures. They don't see a necessary large change in the expectation of contractor providing security but better interaction/coordination of planning (b)(7)(E)

I discussed the San Diego Unified Resolve planning and will forward them a copy of the draft. They are going to use (b)(6);(b)(7)(C) as their coordinating point to me for future coordination. I expect they will want each project to have a BP POC for their security rep to engage as needed in planning. I see this as a simple expansion of what we did with SD as a contingency planning requirement and think that as long as the PMs are involved and USACE understands that PMs need to be in the loop this is a good

approach. They also recognize that each project has different concerns/levels of likelihood of protests/violence so each project will have varying level of interaction. While I'll act as the POC for (b)(6);(b)(7)(C) and their security efforts, I expect each PM will need to work with the respective sectors to identify a POC within their strategic planning group as SDC did in preparation for prototype.

I'm working on getting to DFW for meeting with (b)(6);(b)(7)(C) on one of my next passes through DFW

(b)(6);(b)(7)(C)

LMI
7940 Jones Branch Drive
Tysons, VA 22102
Cell: (b)(6);(b)(7)(C)

Complex Problems. Practical Solutions.
www.lmi.org<<http://www.lmi.org/>>

From:

(b)(6);(b)(7)(C)

To:

(b)(6);(b)(7)(C)

(b)(6)

(b)(6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6)

(b)(6)

(b)(6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc:

Bcc:

Subject:

RE: EPT (b)(7)(E) RF - El Paso Fence Replacement Project

Date:

Tue Aug 29 2017 12:13:07 EDT

Attachments:

(b)(6);(b)(7)(C)

Sector PMO is in the process of reviewing your comments. We will seek comments/concurrence from (b)(7)(E) Station , and advise soonest.

V/R,

(b)(6);(b)(7)(C)

Operations Officer

El Paso Sector | Program Management Office

Office: (b)(6);(b)(7)(C)

iPhone: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, August 29, 2017 5:49 AM

To: (b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

Subject: RE: EPT (b)(7)(E) RF - El Paso Fence Replacement Project

All

Yesterday (b) (6) and myself conducted a comprehensive "plans-in-hand" review of the latest version of the 30% design. Our comments were annotated on drawings that we will distribute shortly (need to convert them to pdf). In the meantime, provided below is a summary of our observations. Baker is planning to update the drawings before they are released for bid later this week.

(b) (5), (b) (7)(E)

(b) (5), (b) (7)(E)

We can discuss the above on Thursday's call but we'd like feedback from Border Patrol on item #1 soonest.

Best,

(b)(6);(b)(7)(C)

-----Original Message-----

From: (b) (6)

(b) (6)

Sent: Tuesday, August 22, 2017 12:23 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: FW: EPT (b) (7)(E) RF - El Paso Fence Replacement Project Corrected Final Submittal (UNCLASSIFIED)

CLASSIFICATION: UNCLASSIFIED

All,

Once you have reviewed the Corrected Final RFP from Michael Baker Corporation for the El Paso Replacement Fence Project please let me know what comments I can close out for you in the Draft

35% review and which have not been addressed and need to remain open.

Thanks,

(b) (6) PMP

Military and Operations Project Manager

USACE-ABQ District

4101 Jefferson Plaza

Albuquerque, NM 87109

Desk: (b) (6)

BB: (b) (6)

E-mail: (b) (6)

—Original Message—

From: (b) (6)

Sent: Tuesday, August 22, 2017 12:18 AM

To:

(b)(6);(b)(7)(C)

(b) (6)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b) (6)

(b) (6)

Subject: [Non-DoD Source] EPT (b)(7)(E) RF - El Paso Fence Replacement Project Corrected Final

Submittal

All,

The Corrected Final RFP submittal for EPT (b)(7)(E) RF - El Paso Fence Replacement RFP is available. You can download the RFP document and HEC-RAS models and by clicking the links below.

RFP Document (includes plans, geotechnical and drainage reports):

(b)(7)(E)

HEC-RAS models:

(b)(7)(E)

(b)(7)(E)

Let me know if you have any questions or problems accessing the submittal.

Thank you,

(b) (6)

(b) (6)

P.E., LEED-AP | Senior Associate | Michael Baker International

2929 N. Central Avenue, Suite 800 | Phoenix, AZ 85012 | d: (b) (6) | c: (b) (6)

(b) (6) | Blockedwww.mbakintl.com
<Blockedhttp://www.mbakintl.com/>

(b)(7)(E)

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: Still at home by chance?

Date: Mon Aug 28 2017 08:12:03 EDT

Attachments:

Hi (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) flight was at noon on Friday so he wouldn't have seen this. He will be back in the office the week of 11 September.

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:13 PM

To: (b)(6);(b)(7)(C)

Subject: Still at home by chance?

Importance: High

(b)(6);(b)(7)(C) – If you are by any chance still at home and willing to accept a “drive-by,” I just received a ROW Grant from BLM that needs your signature and would be happy to drop on my way home this aft (or even this weekend) to have you sign it. No notary needed, just your signature. It's for (b)(7)(E) miles of CTIMR roads in NM.

No worries if you have already headed elsewhere.

Thanks. -- (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Real Estate Specialist; Real Estate, Environmental and Leasing Division

LMI Government Consulting

Border Patrol & Air and Marine Program Management Office (BPAM PMO)

Facilities Management & Engineering

Cell: **(b)(6);(b)(7)(C)**

Email: **(b)(6);(b)(7)(C)**

From:

(b)(6);(b)(7)(C)

To:

Cc:

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: Daily Reports

Date: Fri Aug 25 2017 18:09:27 EDT

Attachments: image001.jpg

(b)(6);(b)(7)(C) is right. This is what will separate us from amateurs.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 5:50:16 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

To best describe the day's activities, each report is going to have to use at least one of these words: "magnificent", "great", "tremendous", "really good", "huge", "winning", "weak", "loser", or "bad hombre"

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 1:27 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

We should probably include our financial burn rate as well. That will fulfill our stewardship obligation to taxpayers.

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 4:19 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Thanks (b)(6);(b)(7)(C) And here is the other one we discussed for consideration. We will just need to add a photo, which can change with the progress of the work.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 4:16 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Re: Daily Reports

I went ahead and got a twitter address name: (b) (6)

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 4:02:39 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [EXTERNAL] RE: Daily Reports

Talk to you all in 15.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 4:01 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Agree. Thanks (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 4:01 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Thanks (b)(6);(b)(7)(C) That will be helpful.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:59 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Let me know if you need me to draft concise/140 character updates.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:57 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: Re: Daily Reports

(b) (5)

We have 140 characters to be specific

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:48:05 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: [EXTERNAL] RE: Daily Reports

I'm actually with you. I know it isn't traditional, but yes – let's make it happen.

(b)(6);(b)(7)(C) – If you are ok with it, I can get a call set up for 4 pm with your guys to make it happen. OR is 4:15 better?

Adding (b)(6);(b)(7)(C) for awareness.

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:41 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Re: Daily Reports

This would be a great way to quickly distribute information to all the interested stakeholders

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:35:50 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [EXTERNAL] Daily Reports

I was thinking about reporting today, and made a decision. What (b)(6);(b)(7)(C) and myself will do is Tweet nightly our daily reports. We will set up an account this weekend and let you know our handle. That way it will be transmitted for your use, as well as many others, immediately.

Respectfully,

(b)(6);(b)(7)(C)

Eastern Corridors Division Director

Border Patrol and Air Marine Operations Program Management Office

Facilities Management and Engineering

Mobile: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

image001.jpg for Printed Item: 3035 (Attachment 1 of 1)

(b) (6)

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: Daily Reports

Date: Fri Aug 25 2017 16:31:22 EDT

Attachments: image001.jpg

We can include the handle to follow on the FOIA reading room. We probably need a working group to start working on hashtags.

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 4:29 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Re: Daily Reports

And will save on FOIA costs since everything will already be in public domain

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 4:27:48 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [EXTERNAL] RE: Daily Reports

Transparency. My middle name.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 4:27 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

We should probably include our financial burn rate as well. That will fulfill our stewardship obligation to taxpayers.

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 4:19 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Thanks (b)(6);(b)(7)(C) And here is the other one we discussed for consideration. We will just need to add a photo, which can change with the progress of the work.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 4:16 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Re: Daily Reports

I went ahead and got a twitter address name: (b) (6)

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 4:02:39 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [EXTERNAL] RE: Daily Reports

Talk to you all in 15.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 4:01 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Agree. Thanks (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 4:01 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Thanks (b)(6);(b)(7)(C) That will be helpful.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:59 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Let me know if you need me to draft concise/140 character updates.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:57 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: Re: Daily Reports

(b) (5)

We have 140 characters to be specific

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:48:05 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: [EXTERNAL] RE: Daily Reports

I'm actually with you. I know it isn't traditional, but yes – let's make it happen.

(b)(6);(b)(7)(C) – If you are ok with it, I can get a call set up for 4 pm with your guys to make it happen. OR is 4:15 better?

Adding (b)(6);(b)(7)(C) for awareness.

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:41 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Re: Daily Reports

This would be a great way to quickly distribute information to all the interested stakeholders

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:35:50 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [EXTERNAL] Daily Reports

I was thinking about reporting today, and made a decision. What (b)(6);(b)(7)(C) and myself will do is Tweet nightly our daily reports. We will set up an account this weekend and let you know our handle. That way it will be transmitted for your use, as well as many others, immediately.

Respectfully,

(b)(6);(b)(7)(C)

Eastern Corridors Division Director

Border Patrol and Air Marine Operations Program Management Office

Facilities Management and Engineering

Mobile: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

image001.jpg for Printed Item: 3039 (Attachment 1 of 1)

(b) (6)

From:
To:

(b)(6);(b)(7)(C)

Cc:
Bcc:
Subject: Re: Daily Reports
Date: Fri Aug 25 2017 16:27:46 EDT
Attachments: image001.jpg

Will also add in protester arrested tally

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 4:26:58 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [EXTERNAL] RE: Daily Reports

We should probably include our financial burn rate as well. That will fulfill our stewardship obligation to taxpayers.

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 4:19 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Thanks (b)(6);(b)(7)(C) And here is the other one we discussed for consideration. We will just need to add a photo, which can change with the progress of the work.

From: (b)(6);(b)(7)(C)
Sent: Friday, August 25, 2017 4:16 PM
To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Re: Daily Reports

I went ahead and got a twitter address name: (b) (6)

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)
Sent: Friday, August 25, 2017 4:02:39 PM
To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Subject: [EXTERNAL] RE: Daily Reports

Talk to you all in 15.

From: (b)(6);(b)(7)(C)
Sent: Friday, August 25, 2017 4:01 PM
To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Agree. Thanks (b)(6); (b)(7)(C)

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 4:01 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Thanks (b)(6);(b)(7)(C) That will be helpful.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:59 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Let me know if you need me to draft concise/140 character updates.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:57 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: Re: Daily Reports

(b) (5)

We have 140 characters to be specific

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:48:05 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: [EXTERNAL] RE: Daily Reports

I'm actually with you. I know it isn't traditional, but yes – let's make it happen.

(b)(6);(b)(7)(C) – If you are ok with it, I can get a call set up for 4 pm with your guys to make it happen. OR is 4:15 better?

Adding (b)(6);(b)(7)(C) for awareness.

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:41 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Re: Daily Reports

This would be a great way to quickly distribute information to all the interested stakeholders

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:35:50 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [EXTERNAL] Daily Reports

I was thinking about reporting today, and made a decision. What (b)(6);(b)(7)(C) and myself will do is Tweet nightly our daily reports. We will set up an account this weekend and let you know our handle. That way it will be transmitted for your use, as well as many others, immediately.

Respectfully,

(b)(6);(b)(7)(C)

Eastern Corridors Division Director

Border Patrol and Air Marine Operations Program Management Office

Facilities Management and Engineering

Mobile: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

image001.jpg for Printed Item: 3045 (Attachment 1 of 1)

(b) (6)

From:
To:

(b)(6);(b)(7)(C)

Cc:
Bcc:
Subject: Re: Daily Reports
Date: Fri Aug 25 2017 16:15:51 EDT
Attachments: Photo 1.jpg

I went ahead and got a twitter address name: (b) (6)

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)
Sent: Friday, August 25, 2017 4:02:39 PM
To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Subject: [EXTERNAL] RE: Daily Reports

Talk to you all in 15.

From: (b)(6);(b)(7)(C)
Sent: Friday, August 25, 2017 4:01 PM
To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Agree. Thanks (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 4:01 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Thanks (b)(6);(b)(7)(C) That will be helpful.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:59 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Let me know if you need me to draft concise/140 character updates.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:57 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: Re: Daily Reports

(b) (5)

We have 140 characters to be specific

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)
Sent: Friday, August 25, 2017 3:48:05 PM
To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Cc: (b)(6);(b)(7)(C)
Subject: [EXTERNAL] RE: Daily Reports

I'm actually with you. I know it isn't traditional, but yes – let's make it happen.

(b)(6);(b)(7)(C) – If you are ok with it, I can get a call set up for 4 pm with your guys to make it happen. OR is 4:15 better?

Adding (b)(6);(b)(7)(C) for awareness.

(b)(6);(b)(7)(C)

Director, Business Operations Division
Border Patrol & Air and Marine Program Management Office
Facilities Management and Engineering
Office of Facilities and Asset Management
Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Friday, August 25, 2017 3:41 PM
To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Subject: Re: Daily Reports

This would be a great way to quickly distribute information to all the interested stakeholders

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)
Sent: Friday, August 25, 2017 3:35:50 PM
To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Subject: [EXTERNAL] Daily Reports

I was thinking about reporting today, and made a decision. What (b)(6); (b)(7)(C) and myself will do is Tweet nightly our daily reports. We will set up an account this weekend and let you know our handle. That way it will be transmitted for your use, as well as many others, immediately.

Respectfully,

(b)(6);(b)(7)(C)

Eastern Corridors Division Director


Border Patrol and Air Marine Operations Program Management Office

Facilities Management and Engineering

Mobile: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

(b) (6)



From:
To:

(b)(6);(b)(7)(C)

Cc:
Bcc:
Subject: Re: Daily Reports
Date: Fri Aug 25 2017 16:09:01 EDT
Attachments:

Works for me. I'm in an alternate work location. It's after 4

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)
Sent: Friday, August 25, 2017 4:04:05 PM
To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Subject: [EXTERNAL] RE: Daily Reports

I'm going to call in from the car if that's ok!

(b)(6);(b)(7)(C)

Director, Business Operations Division
Border Patrol & Air and Marine Program Management Office
Facilities Management and Engineering
Office of Facilities and Asset Management
Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Friday, August 25, 2017 4:03 PM
To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Talk to you all in 15.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 4:01 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Agree. Thanks (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 4:01 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Thanks (b)(6);(b)(7)(C) That will be helpful.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:59 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Let me know if you need me to draft concise/140 character updates.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:57 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: Re: Daily Reports

(b) (5)

(b) (5)

We have 140 characters to be specific

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:48:05 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: [EXTERNAL] RE: Daily Reports

I'm actually with you. I know it isn't traditional, but yes – let's make it happen.

(b)(6);(b)(7)(C) – If you are ok with it, I can get a call set up for 4 pm with your guys to make it happen. OR is 4:15 better?

Adding (b)(6);(b)(7)(C) for awareness.

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:41 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Re: Daily Reports

This would be a great way to quickly distribute information to all the interested stakeholders

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:35:50 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [EXTERNAL] Daily Reports

I was thinking about reporting today, and made a decision. What (b)(6);(b)(7)(C) and myself will do is Tweet nightly our daily reports. We will set up an account this weekend and let you know our handle. That way it will be transmitted for your use, as well as many others, immediately.

Respectfully,

(b)(6);(b)(7)(C)

Eastern Corridors Division Director

Border Patrol and Air Marine Operations Program Management Office

Facilities Management and Engineering

Mobile: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

From:

To:

Cc:

Bcc:

Subject:

RE: Daily Reports

Date:

Fri Aug 25 2017 16:02:45 EDT

Attachments:

Happy to be of service to such a fine group of public servants.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 4:01 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Thanks (b)(6);(b)(7)(C) That will be helpful.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:59 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Daily Reports

Let me know if you need me to draft concise/140 character updates.

From: (b)(6);(b)(7)(C)
Sent: Friday, August 25, 2017 3:57 PM
To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Cc: (b)(6);(b)(7)(C)
Subject: Re: Daily Reports

(b) (5)
We have 140 characters to be specific

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)
Sent: Friday, August 25, 2017 3:48:05 PM
To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Cc: (b)(6);(b)(7)(C)
Subject: [EXTERNAL] RE: Daily Reports

I'm actually with you. I know it isn't traditional, but yes – let's make it happen.

(b)(6);(b)(7)(C) – If you are ok with it, I can get a call set up for 4 pm with your guys to make it happen. OR is 4:15 better?

Adding (b)(6);(b)(7)(C) for awareness.

(b)(6);(b)(7)(C)

Director, Business Operations Division
Border Patrol & Air and Marine Program Management Office
Facilities Management and Engineering
Office of Facilities and Asset Management
Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Friday, August 25, 2017 3:41 PM
To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Re: Daily Reports

This would be a great way to quickly distribute information to all the interested stakeholders

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:35:50 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [EXTERNAL] Daily Reports

I was thinking about reporting today, and made a decision. What (b)(6);(b)(7)(C) and myself will do is Tweet nightly our daily reports. We will set up an account this weekend and let you know our handle. That way it will be transmitted for your use, as well as many others, immediately.

Respectfully,

(b)(6);(b)(7)(C)

Eastern Corridors Division Director

Border Patrol and Air Marine Operations Program Management Office

Facilities Management and Engineering

Mobile: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

From:
To:

(b)(6);(b)(7)(C)

Cc:
Bcc:
Subject: Re: Daily Reports
Date: Fri Aug 25 2017 16:00:42 EDT
Attachments:

We'll need to agree on abbreviations to save characters like ADM is all deliveries made or CFP is concrete footer poured. All of them will have consistent activities we can designate in advance

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:58:44 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [EXTERNAL] RE: Daily Reports

Let me know if you need me to draft concise/140 character updates.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:57 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: Re: Daily Reports

(b) (5)

We have 140 characters to be specific

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)
Sent: Friday, August 25, 2017 3:48:05 PM

To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Cc: (b)(6);(b)(7)(C)
Subject: [EXTERNAL] RE: Daily Reports

I'm actually with you. I know it isn't traditional, but yes – let's make it happen.

(b)(6);(b)(7)(C) – If you are ok with it, I can get a call set up for 4 pm with your guys to make it happen. OR is 4:15 better?

Adding (b)(6);(b)(7)(C) for awareness.

(b)(6);(b)(7)(C)

Director, Business Operations Division
Border Patrol & Air and Marine Program Management Office
Facilities Management and Engineering
Office of Facilities and Asset Management
Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Friday, August 25, 2017 3:41 PM
To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Re: Daily Reports

This would be a great way to quickly distribute information to all the interested stakeholders

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)
Sent: Friday, August 25, 2017 3:35:50 PM

To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

Subject: [EXTERNAL] Daily Reports

I was thinking about reporting today, and made a decision. What (b)(6);(b)(7)(C) and myself will do is Tweet nightly our daily reports. We will set up an account this weekend and let you know our handle. That way it will be transmitted for your use, as well as many others, immediately.

Respectfully,

(b)(6);(b)(7)(C)

Eastern Corridors Division Director

Border Patrol and Air Marine Operations Program Management Office

Facilities Management and Engineering

Mobile: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: Daily Reports

Date: Fri Aug 25 2017 16:00:16 EDT

Attachments:

I see what you are saying. We will just need to check with OCC if we can put their name in the Tweet handle.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:57 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: Re: Daily Reports

(b) (5)

(b) (5)

We have 140 characters to be specific

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:48:05 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: [EXTERNAL] RE: Daily Reports

I'm actually with you. I know it isn't traditional, but yes – let's make it happen.

(b)(6);(b)(7)(C) - If you are ok with it, I can get a call set up for 4 pm with your guys to make it happen. OR is 4:15 better?

Adding (b)(6);(b)(7)(C) for awareness.

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:41 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Re: Daily Reports

This would be a great way to quickly distribute information to all the interested stakeholders

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:35:50 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [EXTERNAL] Daily Reports

I was thinking about reporting today, and made a decision. What (b)(6);(b)(7)(C) and myself will do is Tweet nightly our daily reports. We will set up an account this weekend and let you know our handle. That way it will be transmitted for your use, as well as many others, immediately.

Respectfully,

(b)(6);(b)(7)(C)

Eastern Corridors Division Director

Border Patrol and Air Marine Operations Program Management Office

Facilities Management and Engineering

Mobile: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: Daily Reports

Date: Fri Aug 25 2017 15:47:04 EDT

Attachments:

Absolutely (b)(6);(b)(7)(C) We can do separate Tweets (140 character limit) for each portion of the Daily Report, such as schedule progress, man power, security issues (save those that are OPSEC), etc.

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:41 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Re: Daily Reports

This would be a great way to quickly distribute information to all the interested stakeholders

Sent using OWA for iPhone

From: (b)(6);(b)(7)(C)

Sent: Friday, August 25, 2017 3:35:50 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [EXTERNAL] Daily Reports

I was thinking about reporting today, and made a decision. What (b)(6);(b)(7)(C) and myself will do is Tweet nightly our daily reports. We will set up an account this weekend and let you know our handle. That way it will be transmitted for your use, as well as many others, immediately.

Respectfully,

(b)(6);(b)(7)(C)

Eastern Corridors Division Director

Border Patrol and Air Marine Operations Program Management Office

Facilities Management and Engineering

Mobile: **(b)(6);(b)(7)(C)**

Email: **(b)(6);(b)(7)(C)**

From:

To:

Cc:

Bcc:

Subject:

RE: RGV Outreach

Date:

Thu Aug 24 2017 15:21:43 EDT

Attachments:

Hi

(b)(6);(b)(7)(C)

(b) (5)

(b)(6);(b)(7)(C)

Senior Attorney (Trade & Finance)

Office of Chief Counsel

U.S. Customs and Border Protection

1300 Pennsylvania Avenue, NW Room 4.4B

Washington, DC 20229

Tel: (b)(6);(b)(7)(C)

Fax: (b)(6);(b)(7)(C)

Email (b)(6);(b)(7)(C)

~~ATTORNEY-CLIENT PRIVILEGED/ATTORNEY WORK PRODUCT~~

~~This communication might contain communications between attorney and client, communications that are part of the agency deliberative process, or attorney work product, all of which are privileged and not subject to disclosure outside the agency or to the public. Please consult with the Office of Chief Counsel, U.S. Customs and Border Protection before disclosing any information contained in this email.~~

From: (b)(6);(b)(7)(C)

Sent: Thursday, August 24, 2017 3:15 PM

To: (b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: RE: RGV Outreach

Hi (b)(6);(b)(7)(C) – Is OCC still interested in meeting with Chief Padilla ahead of this meeting?

(b)(6);(b)(7)(C)

Director, Business Operations Division

Border Patrol & Air and Marine Program Management Office

Facilities Management and Engineering

Office of Facilities and Asset Management

Mobile: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, August 24, 2017 8:13 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: FW: RGV Outreach

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Wednesday, August 23, 2017 6:39 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RGV Outreach

ALCON,

I spoke with Chief Padilla here at the conference and spoke with Mr. (b)(6);(b)(7)(C) in RGV. Most of the concerns that came up at today's meeting were misunderstandings.

RGV is going send me what they have planned for September 14th. As soon as I receive it, I will pass it along.

(b)(6);(b)(7)(C)

Assistant Chief

ORMD

U.S. Border Patrol Headquarters

iPhone: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Bcc:

Subject: RE: RGV Wall & Gates Stakeholder Engagement/Meeting Planning

Date: Thu Aug 24 2017 14:27:26 EDT

Attachments:

Good afternoon -

Please find a proposed agenda below for our discussion this afternoon. Please let me know if you have other items to include.

- * September 12 - CBP/USACE/DOJ Meeting – Final Agenda
- * September 14 – Tier 2/3 Stakeholder Meeting Update
- o Format
- o Participants
- o Materials
- o Logistics
- * Follow-up stakeholder engagement meetings

-----Original Appointment-----

From: (b)(6);(b)(7)(C)

Sent: Tuesday, July 11, 2017 12:57 PM

To:

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C);

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

Cc: (b)(6);(b)(7)(C)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)
(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

Subject: RGV Wall & Gates Stakeholder Engagement/Meeting Planning

When: Thursday, August 24, 2017 3:00 PM-4:00 PM (UTC-05:00) Eastern Time (US & Canada)

Where: (b)(6);(b)(7)(C) PIN: (b) (7)(E)

From:

(b)(6);(b)(7)(C)

To:

(b) (6)

(b) (6)

Cc:

(b)(6);(b)(7)(C)

(b) (6)

(b) (6);

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C);

(b) (6)

(b) (6)

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Bcc:

Subject: RE: Systems Engineering

Date: Thu Aug 24 2017 10:41:34 EDT

Attachments: Boder Barrier PgMP 071117 Signed.pdf
Border Barrier System Risk Management Plan Signed.pdf
CBP_Wall_CDP_USMSigned.pdf
Impedence_and_Denial_MNS_20170317_Approved.pdf
Integrated_Logistics_Support_Plan_BPAM.PDF

All-

Highlighted below is what we have attached;

- Acquisition Program Artifacts
 - Mission Needs Statement (MNS)- attached
 - Capability Development Plan (CDP)- attached
 - Concept of Operations (CONOPS)- currently in signature cycle
 - Operational Requirements Document (ORD)- currently in development
 - Analysis of Alternatives (AoA)/Alternatives Analysis (AA) - currently in development
 - Other trade studies or analysis performed
 - Systems Engineering Life Cycle (SELC) Tailoring Plan for ADE 2B - currently in development
 - Life Cycle Cost Estimate (LCCE)- pending ICE finalization
 - Integrated Logistics Support Plan (ILSP)- attached and in signature cycle
-
- Program Management Artifacts
 - Risk Register- attached
 - High Level Architecture- do not have this document
 - Interface descriptions- do not have this document
 - Technology Capability Development Roadmap- do not have this document
 - Draft Security Plan-do not have this document
 - Draft Program Management Plan- attached

Thanks,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Border Patrol & Air and Marine Program Management Office (BPAM PMO)
Facilities Management & Engineering

Office: (b)(6);(b)(7)(C)

Cell: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

[Click Here to view the FMB team listed with areas of responsibility.](#)

[Click Here to view the PRR tracker.](#)

[Click Here to view the IAA Tracker](#)

From: (b)(6);(b)(7)(C)

Sent: Thursday, August 24, 2017 9:49 AM

To: (b) (6)
(b) (6)
Cc: (b)(6);(b)(7)(C) (b) (6)
(b) (6)
(b) (6) (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
(b)(6);(b)(7)(C) (b) (6)
(b) (6) (b)(6);(b)(7)(C)
Subject: RE: Systems Engineering

Please forward the list of required documents discussed during today's call and we will provide the most recent version for your use. Your POC for this action will be (b)(6);(b)(7)(C).

Respectfully,

(b)(6);(b)(7)(C) P.E. LEED AP BD+C
Program Manager
Border Patrol & Air and Marine Program Management Office (BPAM PMO)
Facilities Management & Engineering
Mobile: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

-----Original Appointment-----

From: (b)(6);(b)(7)(C)
Sent: Tuesday, August 22, 2017 3:12 PM
To: (b)(6);(b)(7)(C) (b) (6)
(b) (6); (b)(6);(b)(7)(C)
Cc: (b)(6);(b)(7)(C) (b) (6)
Subject: Systems Engineering
When: Thursday, August 24, 2017 9:00 AM-9:30 AM (UTC-05:00) Eastern Time (US & Canada).
Where: (b) (7)(E) Phone: (b) (7)(E) Pin: (b) (7)(E)

This is a priority meeting that (b)(6);(b)(7)(C) would like to occur before he is out of the office on Friday. Please let me know if you cannot attend.

(b) (7)(E)

1331 Pennsylvania Ave NW
Suite 755N
Washington DC 20004

Entrance is on F street, between 13th and 14th street next to Dress Barn. Proceed in the building to the back elevators, take them to the 7th Floor, and please call (b)(6);(b)(7)(C) at (b)(6);(b)(7)(C) to gain access to the suite.

JA 10/07/17



U.S. Customs and
Border Protection

Comprehensive Immigration Reform New Border Wall System Program Management Plan

Version 1.0

i

Approvals

By signing below, all parties agree to the terms and conditions described in this document.

Service Provider:

Facilities Management & Engineering (FM&E) Division,
Border Patrol & Air and Marine Program Management Office
(BPAM PMO)

(b)(6);(b)(7)(C)

10 JULY 17
Date

Director, Border Patrol & Air and Marine Program Management Office
Facilities Management & Engineering Division

(b) (5)

~~For Official Use Only Updated 6/19/17~~

(b) (5)

~~For Official Use Only Updated 6/19/17~~

1. Introduction

(b) (5)

(b) (5)

~~For Official Use Only~~

BW23 FOIA CBP 012257

Page 1277 of 1880

(b) (5)

(b) (5)

(b) (5)

~~For Official Use Only~~

BW23 FOIA CBP 012260

Page 1280 of 1880

(b) (5)

(b) (5)

~~For Official Use Only~~

(b) (5)

~~For Official Use Only~~

BW23 FOIA CBP 012263

Page 1283 of 1880

(b) (5)

~~For Official Use Only~~

BW23 FOIA CBP 012264

Page 1284 of 1880

(b) (5)

~~For Official Use Only~~

BW23 FOIA CBP 012265

Page 1285 of 1880

(b) (5)

(b) (5)

~~For Official Use Only~~

BW23 FOIA CBP 012267

Page 1287 of 1880

(b) (5)

~~For Official Use Only~~

BW23 FOIA CBP 012268

Page 1288 of 1880

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

~~For Official Use Only~~

BW23 FOIA CBP 012275

Page 1295 of 1880

(b) (5)

(b) (5)

~~For Official Use Only~~

BW23 FOIA CBP 012277

Page 1297 of 1880

(b) (5)

~~For Official Use Only~~

BW23 FOIA CBP 012278

Page 1298 of 1880

(b) (5)

~~For Official Use Only~~

(b) (5)

~~For Official Use Only~~

BW23 FOIA CBP 012280


Page 1300 of 1880

(b) (5)

(b) (5)

(b) (5)

18. Appendix
18.1 Org Chart

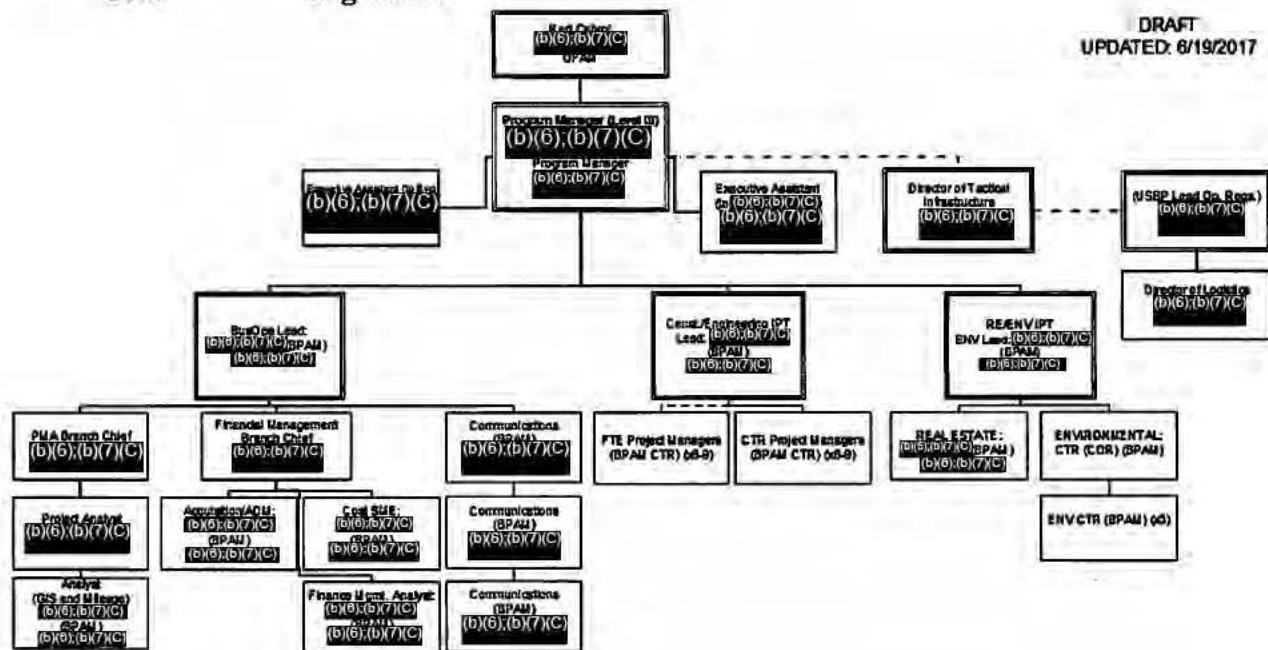

(b)(6); (b)(7)(C)



U.S. Customs and Border Protection

Facilities Management & Engineering Border Patrol and Air & Marine Program Management Office Border Barrier System Risk Management Plan

22 June, 2016

This document was prepared for authorized distribution only.
It has not been approved for public release.

Approvals

By signing below, all parties agree to the terms and conditions described in this document.

Service Provider:

Facilities Management & Engineering (FM&E) Division,
Border Patrol & Air and Marine Program Management Office
(BPAM PMO)

(b)(6);(b)(7)(C)

10 July 17
Date

Director, Border Patrol & Air and Marine Program Management Office
Facilities Management & Engineering Division


(b) (5)

(b) (5)


(b) (5)

(b) (5)


(b) (5), (b) (7)(E)




(b) (5), (b) (7)(E)




(b) (5), (b) (7)(E)




(b) (5), (b) (7)(E)



(b) (5), (b) (7)(E)




(b) (5), (b) (7)(E)




(b) (5), (b)(6);(b)(7)(C), (b) (7)(E)



(b) (5), (b) (7)(E)



(b) (5), (b) (7)(E)



1300 Pennsylvania Avenue NW
Washington, DC 20229

(b) (7)(E)

MAR. 11 10 2017



U.S. Customs and
Border Protection

Handwritten signature and date: 3/13/17

MEMORANDUM FOR: Robert Perez
Component Requirements Executive
U.S. Customs and Border Protection
FROM: Ronald D. Vitiello (b)(6);(b)(7)(C)
Chief
U.S. Border Patrol
SUBJECT: U.S. Border Patrol Capability and Mission Need Documentation
for Impedance and Denial

At the request of the Department of Homeland Security (DHS) and U.S. Customs and Border Protection, the U.S. Border Patrol expedited the necessary requirements documentation to align with DHS Acquisition Management Directive DHS 102-01 and DHS Joint Requirements Integration and Management System Directive 107-01 to support the Executive Order 13767, *Border Security and Immigration Enforcement Improvements*.

Specifically, this request pertains to capability requirements documents supporting the "Wall" Integrated Planning Team activities. To achieve this direction, the U.S. Border Patrol formally requests that the DHS Joint Requirements Council accommodate a tailored and expedited review of Impedance and Denial capability documentation.

Attached for your review is a Capability Analysis Report and Mission Need Statement for the required capability of Impedance and Denial. These documents formalize the initial capability assessment and the critical departmental mission need to impede and deny illegal activity along the Southwest Border of the United States.

Staff may direct questions regarding the Impedance and Denial requirements development effort to Assistant Chief (b)(6);(b)(7)(C) at (b)(6);(b)(7)(C) or (b)(6);(b)(7)(C) at (b)(6);(b)(7)(C)

Attachment

U.S. Customs and Border Protection

U.S. Border Patrol

Impedance and Denial Mission Need Statement



U.S. Customs and Border Protection

March 9, 2017

Sponsoring Organization: Customs and Border Protection (CBP), U.S. Border Patrol (USBP)

Page i

~~FOR OFFICIAL USE ONLY/LAW ENFORCEMENT SENSITIVE~~

~~FOUO/LES~~

Validation Page

This document (version 1.11) has not yet been validated, and is not considered to be an authoritative source for the content herein. This document may be considered authoritative only when this page has been replaced by a signed validation memorandum from the appropriate validation authority.

Submitted by:	(b)(6);(b)(7)(C) Chief, United States Border Patrol	3-10-17 Date
Endorsed by:	(b)(6);(b)(7)(C) Components Requirements Executive Customs and Border Protection	3/13/17 Date
Validated by:	(b)(6);(b)(7)(C) Director, DHS Joint Requirements Council (JRC)	3/16/17 Date
Endorsed By:	(b)(6);(b)(7)(C) Chairman, DHS Joint Requirements Council (JRC)	3/16/17 Date
Approved By:	(b)(6);(b)(7)(C) DHS Acting Under Secretary for Management	3/17/17 Date

Mission Need Statement, Version 1.0

(b) (5)

(b) (5)

Mission Need Statement, Version 1.0

Section B. Revision Summary

The following table indicates the changes that were made to the document since its last release.

Date	Version #	Description of Changes
3/9/2017	1 through 2	Initial Draft

Mission Need Statement, Version 1.0

(b) (5)

~~FOR OFFICIAL USE ONLY - LAW ENFORCEMENT SENSITIVE~~

4

Mission Need Statement, Version 1.0



(b)(7)(E)

Mission Need Statement, Version 1.0

(b)(7)(E)



~~FOR OFFICIAL USE ONLY - LAW ENFORCEMENT SENSITIVE~~

Mission Need Statement, Version 1.0

(b)(7)(E)



~~FOR OFFICIAL USE ONLY / LAW ENFORCEMENT SENSITIVE~~

7

Mission Need Statement, Version 1.0

(b)(7)(E)

~~FOR OFFICIAL USE ONLY - LAW ENFORCEMENT SENSITIVE~~

8

Mission Need Statement, Version 1.0

(b)(7)(E)



~~FOR OFFICIAL USE ONLY - LAW ENFORCEMENT SENSITIVE~~

9

Mission Need Statement, Version 1.0

(b)(7)(E)

~~FOR OFFICIAL USE ONLY / LAW ENFORCEMENT SENSITIVE~~

10

BW23 FOIA CBP 012312

Page 1337 of 1880

Mission Need Statement, Version 1.0

(b)(7)(E)



~~FOR OFFICIAL USE ONLY / LAW ENFORCEMENT SENSITIVE~~

11

Mission Need Statement, Version 1.0

(b)(7)(E)



~~FOR OFFICIAL USE ONLY - LAW ENFORCEMENT SENSITIVE~~

12

Mission Need Statement, Version 1.0

(b)(7)(E)



~~FOR OFFICIAL USE ONLY - LAW ENFORCEMENT SENSITIVE~~

13

Mission Need Statement, Version 1.0

(b)(7)(E)



~~FOR OFFICIAL USE ONLY - LAW ENFORCEMENT SENSITIVE~~

14

Mission Need Statement, Version 1.0

(b)(7)(E)



~~FOR OFFICIAL USE ONLY - LAW ENFORCEMENT SENSITIVE~~

15

Mission Need Statement, Version 1.0

Enclosure 2: Threat Characteristics

Table summarizes threat attributes and characteristics at a high level. Collectively, these adversary attributes increase the risk not only to the border security mission, but the agents that execute that mission. The impact of threat TTPs and characteristics in the various terrain types on CBP ability to execute the tasks and on agent safety is summarized in table 4.

(b)(7)(E)

Table Error! No text of specified style in document.-I. Impact of Threat Characteristics in the Different Terrain Types on CBP Ability to Execute the METS and on Agent Safety

(b)(7)(E)

(b) (7)(E)



Integrated Logistics Support Plan For Border Patrol Tactical Infrastructure Program

**DHS Systems Engineering
Life Cycle**

**OFFICE OF FACILITIES AND ASSET
MANAGEMENT
BORDER PATROL AND AIR AND MARINE
PROGRAM MANAGEMENT OFFICE**

Integrated Logistics Support Plan*for**Border Patrol Tactical Infrastructure*

Submitted by:

(b)(6);(b)(7)(C) Program ManagerDate

Endorsed by:

Component Acquisition Executive
(Developing Component)Date

Endorsed by:

Component Head
(Developing Component)Date

Endorsed by:

Component Acquisition Executive
(Operating Component)Date

Approved by:

Component Head
(Operating Component)Date

Reviewed by:

Director, APMDDate

Approved by:

Acquisition Decision AuthorityDate

(b) (5)

Revision Summary (If Applicable)

Provide a bulleted high-level description of what changes have occurred and why in the current submission. Provide the date of the revisions. See format below.


DOCUMENT CHANGE HISTORY

Version Number	Date	Description

(b) (5)

(b) (5)


(b) (5), (b) (7)(E)



(b) (5)

(b) (5)

(b) (5), (b) (7)(E)



(b) (5), (b) (7)(E)




Table 4 – LCCE Summary Table (Current Year)

(b) (5)

(b) (5), (b) (7) (E)

(b) (5)

(b) (5)

(b) (5)

(b) (5)

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: Alignment question

Date: Thu Aug 24 2017 07:16:51 EDT

Attachments:

(b)(6);(b)(7)(C) has been working with the division chief at sdc and paic- I would like him come back with the sdc leadership's requirements and position -

From: (b)(6);(b)(7)(C)

Sent: Thursday, August 24, 2017 6:30:34 AM

To: (b)(6);(b)(7)(C)

Subject: RE: Alignment question

(b) (5), (b) (7)(E)

(b)(6);(b)(7)(C) PE

LMI

BPAM Chief Engineer

(b)(6);(b)(7)(C)

Sent from Samsung Galaxy

From: (b)(6);(b)(7)(C)

Sent: Wednesday, August 23, 2017 4:54:27 PM

To: (b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: RE: Alignment question

Understand – (b) (5)

(b)(6); (b)(7)(C); (b)(7)(E)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Wednesday, August 23, 2017 4:50 PM
To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Subject: RE: Alignment question

(b) (5), (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

LMI
7940 Jones Branch Drive
Tysons, VA 22102
Cell: (b)(6);(b)(7)(C)

Complex Problems. Practical Solutions.
www.lmi.org<<http://www.lmi.org>>

From: (b)(6);(b)(7)(C)
Sent: Wednesday, August 23, 2017 4:48 PM
To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Subject: [EXTERNAL] RE: Alignment question

(b) (5), (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Wednesday, August 23, 2017 4:46 PM
To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Subject: RE: Alignment question

Thanks (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) see the traffic below. (b) (5)

From: (b)(6);(b)(7)(C)
Sent: Wednesday, August 23, 2017 4:40:23 PM
To: (b)(6);(b)(7)(C)
Subject: FW: Alignment question
FYI

(b)(6);(b)(7)(C)

LMI
7940 Jones Branch Drive
Tysons, VA 22102
Cell: (b)(6);(b)(7)(C)

Complex Problems. Practical Solutions.
www.lmi.org<<http://www.lmi.org>>

From: (b)(6);(b)(7)(C)
Sent: Sunday, August 13, 2017 12:29 AM
To: (b)(6);(b)(7)(C)
Subject: [EXTERNAL] RE: Alignment question

Yes (b) (5)

From: (b)(6);(b)(7)(C)
Sent: Saturday, August 12, 2017 3:39:59 PM
To: (b)(6);(b)(7)(C)
Subject: Alignment question

(b)(6);(b)(7)(C): a question came up this week regarding the alignment between the two POEs. I remember on several visits sector saying they wanted to keep the current alignment (b)(7)(E)

(b) (5)

Thanks

Sent using OWA for iPhone

From:

To:

(b)(6);(b)(7)(C)

Cc:

Bcc:

Subject: RE: Geotech Analysis Prototype (UNCLASSIFIED)

Date: Thu Aug 24 2017 06:50:39 EDT

Attachments:

Good info-should mitigate our "unknowns" risk substantively

(b)(6);(b)(7)(C) PE

LMI

BPAM Chief Engineer

(b)(6);(b)(7)(C)

Sent from Samsung Galaxy

From: (b)(6);(b)(7)(C)

Sent: Wednesday, August 23, 2017 2:33:39 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: Geotech Analysis Prototype (UNCLASSIFIED)

FYI

As some of you know I had USACE conduct a Geotechnical evaluation of the Prototype area. I wanted this completed regardless of that due to the schedule it wouldn't be available for Prototype RFPs. I wanted to make sure the Government knew what sub-surface risks existed. The results are in and positive (b) (5)

Respectfully,

(b)(6);(b)(7)(C)

Eastern Corridors Division Director

Border Patrol and Air Marine Operations Program Management Office

Facilities Management and Engineering

Mobile: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

From:

(b) (6)

To:

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc:

(b) (6)

Bcc:

Subject:

RE: [Non-DoD Source] RE: BIPMO security POC

Date:

Thu Aug 24 2017 06:36:47 EDT

Attachments:

(b) (7)(E)

ANNEX P CCIR CLEAN 14 Aug

17.pdf

PS. Attached is the CCIR (Commanders Critical Information Requirements) where are referred to in the Security Annex

-----Original Message-----

From:

(b) (6)

Sent: Wednesday, August 23, 2017 8:24 PM

To:

(b) (6)

(b)(6); (b)(7)(C)

Cc:

(b) (6)

Subject: RE: [Non-DoD Source] RE: BIPMO security POC

Here is the security annex

Here is the security annex. Talk to you all tomorrow.

(b) (6)

I will send out a call in number in the morning.

(b) (6)

-----Original Message-----

From:

(b) (6)

Sent: Wednesday, August 23, 2017 11:43 AM

To:

(b)(6); (b)(7)(C)

Cc:

(b) (6)

Subject: RE: [Non-DoD Source] RE: BIPMO security POC

Let's do 930 (b) (6) and I will be in person. Let us know if I need to send out a call in

From: (b)(6);(b)(7)(C)
Date: August 23, 2017 at 11:39:23 AM CDT
To: (b)(6);(b)(7)(C) (b) (6)
(b) (6) (b)(6);(b)(7)(C)
Cc: (b) (6)
Subject: RE: [Non-DoD Source] RE: BIPMO security POC

Trip got cancelled. Free 9:30-11:30 tomorrow morning

(b)(6);(b)(7)(C)

LMI
7940 Jones Branch Drive
Tysons, VA 22102
Cell: (b)(6);(b)(7)(C)

Complex Problems. Practical Solutions.
Blockedwww.lmi.org

From: (b) (6)
Sent: Wednesday, August 23, 2017 11:48 AM
To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Cc: (b) (6)
Subject: [EXTERNAL] Re: [Non-DoD Source] RE: BIPMO security POC

(b) (6) and (b)(6);(b)(7)(C)

Do you have a time tomorrow we can discuss this? I know (b)(6);(b)(7)(C) is in Ca but maybe before he goes to field. Probably need about 30 minutes.

9 or 10 eastern? (b)(6);(b)(7)(C) I am not a morning person so I will wait to hear back from you

(b) (6)

From: (b)(6);(b)(7)(C)

Date: August 18, 2017 at 5:46:08 AM CDT

To: (b)(6)

(b)(6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6)

(b)(6)

Subject: [Non-DoD Source] RE: BIPMO security POC

(b)(6)

Please include me on the email traffic and meetings.

Thanks,

(b)(6)

-----Original Message-----

From: (b)(6)

Sent: Thursday, August 17, 2017 1:23 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6)

(b)(6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: BIPMO security POC

Thanks (b)(6) We will let you know a time. We will be in DC so don't want to make it too early for you!!

-----Original Message-----

From: (b)(6);(b)(7)(C)

Sent: Thursday, August 17, 2017 11:42 AM

To: (b)(6)

(b)(6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6)

(b)(6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [Non-DoD Source] Re: BIPMO security POC

I'll be in San Diego then but should be able to call in around unified resolve planning meeting

Sent using OWA for iPhone

From: (b)(6)

(b)(6)

Sent: Thursday, August 17, 2017 12:31:36 PM

To: (b)(6);(b)(7)(C)

Cc: (b)(6)

(b)(6);(b)(7)(C)

Subject: [EXTERNAL] RE: BIPMO security POC

Thanks (b)(6);(b)(7)(C)

(b) (6) is ours. Thought maybe we could discuss amongst us on the morning of the 24th if (b)(6);(b)(7)(C) is in the office. Then we can connect the two up.

Thanks

(b) (6)

-----Original Message-----

From: (b)(6);(b)(7)(C)

Sent: Thursday, August 17, 2017 11:28 AM

To: (b) (6)

(b) (6)

Cc:

(b) (6)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [Non-DoD Source] BIPMO security POC

(b)(6); (b)(7)(C) (b)(6);(b)(7)(C) will be CBP POC for the San Diego Wall/Fence projects -


(b)(6);(b)(7)(C)

Director, BPAM PMO

(b)(6);(b)(7)(C)(desk)

(b)(6);(b)(7)(C)(mobile)

(b) (5), (b) (7)(E)



~~For Official Use Only~~

BW23 FOIA CBP 012347

Page 1374 of 1880

(b) (5), (b) (7)(E)



(b) (7)(E)

ANNEX P CCIR CLEAN 14 Aug 17.pdf for Printed Item: 3118 (Attachment 1 of 1)

(b) (7)(E)

Annex P CCIR ~~For Official Use Only~~

~~For Official Use Only~~

BW23 FOIA CBP 012349

Page 1376 of 1880

From:

(b) (6)

To:

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc:

(b) (6)

Bcc:

Subject: RE: [Non-DoD Source] RE: BIPMO security POC

Date: Wed Aug 23 2017 21:23:46 EDT

Attachments: (b) (7)(E) ANNEX Q Security CLEAN 14 Aug 1....pdf

Here is the security annex

Here is the security annex. Talk to you all tomorrow.

(b)(6);(b)(7)(C)

I will send out a call in number in the morning.

(b)(6);(b)(7)(C)

-----Original Message-----

From: (b) (6)

Sent: Wednesday, August 23, 2017 11:43 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b) (6)

Subject: RE: [Non-DoD Source] RE: BIPMO security POC

Let's do 930 (b) (6) and I will be in person. Let us know if I need to send out a call in

From: (b)(6);(b)(7)(C)

Date: August 23, 2017 at 11:39:23 AM CDT

To: (b)(6);(b)(7)(C)

(b) (6)

(b)(6);(b)(7)(C)

(b) (6)

Cc: (b) (6)

Subject: RE: [Non-DoD Source] RE: BIPMO security POC

Trip got cancelled. Free 9:30-11:30 tomorrow morning

(b)(6);(b)(7)(C)

LMI
7940 Jones Branch Drive
Tysons, VA 22102
Cell: (b)(6);(b)(7)(C)

Complex Problems. Practical Solutions.
Blockedwww.lmi.org

From: (b) (6)
Sent: Wednesday, August 23, 2017 11:48 AM
To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Cc: (b) (6)
Subject: [EXTERNAL] Re: [Non-DoD Source] RE: BIPMO security POC

(b)(6);(b)(7)(C)

Do you have a time tomorrow we can discuss this? I know (b)(6);(b)(7)(C) is in Ca but maybe before he goes to field. Probably need about 30 minutes.

9 or 10 eastern? (b)(6);(b)(7)(C) I am not a morning person so I will wait to hear back from you

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Date: August 18, 2017 at 5:46:08 AM CDT
To: (b) (6) (b) (6) (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Cc: (b) (6)
(b) (6)
Subject: [Non-DoD Source] RE: BIPMO security POC

(b)(6);(b)(7)(C)

Please include me on the email traffic and meetings.

Thanks,

(b)(6);(b)(7)(C)

-----Original Message-----

From: (b) (6)

Sent: Thursday, August 17, 2017 1:23 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b) (6)

(b) (6) (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: BIPMO security POC

Thanks (b)(6);(b)(7)(C) We will let you know a time. We will be in DC so don't want to make it too early for you!!

-----Original Message-----

From: (b)(6);(b)(7)(C)

Sent: Thursday, August 17, 2017 11:42 AM

To: (b) (6)

(b) (6) (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b) (6)

(b) (6) (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [Non-DoD Source] Re: BIPMO security POC

I'll be in San Diego then but should be able to call in around unified resolve planning meeting

Sent using OWA for iPhone

From: (b) (6)

(b) (6)

Sent: Thursday, August 17, 2017 12:31:36 PM

To: (b)(6);(b)(7)(C)

Cc: (b) (6)

(b)(6);(b)(7)(C)

Subject: [EXTERNAL] RE: BIPMO security POC

Thanks (b)(6);(b)(7)(C)

(b) (6) is ours. Thought maybe we could discuss amongst us on the morning of the 24th if (b)(6);(b)(7)(C) is in the office. Then we can connect the two up.

Thanks

(b)(6);(b)(7)(C)

-----Original Message-----

From: (b)(6);(b)(7)(C)

Sent: Thursday, August 17, 2017 11:28 AM

To: [REDACTED] (b) (6)

[REDACTED] (b) (6)

Cc: [REDACTED] (b) (6)

[REDACTED] (b) (6) [REDACTED] (b)(6);(b)(7)(C)

[REDACTED] (b)(6);(b)(7)(C)

Subject: [Non-DoD Source] BIPMO security POC

(b)(6); (b)(7)(C) [REDACTED] (b)(6);(b)(7)(C) will be CBP POC for the San Diego Wall/Fence projects -

[REDACTED] (b)(6);(b)(7)(C)

Director, BPAM PMO

[REDACTED] (b)(6);(b)(7)(C) (desk)

[REDACTED] (b)(6);(b)(7)(C) (mobile)

~~For Official Use Only~~**OPERATIONS ORDER: (b) (7)(E)****Annex Q – Security****1. Situation.**

(a) General. This annex provides policy and guidance, and outlines the operational requirements, procedures, and standards for executing the USACE Security management program described in (b) (7)(E).

(b) Policy and Guidance Requirements.

(1) USACE will provide guidance and direction related to security for program and project activities required to address both USACE and contractor, personnel and equipment. A USACE Regional Protection Working Group (RPWG), will be established with representatives designated by the Commanders of both Southwestern Division and South Pacific Division. The primary responsibility of the RPWG is to synchronize security plans, policies, and guidance for the program and to monitor the execution of security activities to ensure consistent execution across all districts and divisions. The RPWG will closely coordinate its activities with the Project Management Office - Border Infrastructure (PMO-BI) and report directly to the Commanders of Southwestern and South Pacific Divisions.

(2) The USACE TF Southwest Border PMO and the RPWG recognize that the possibility exists that normally accepted DA and USACE security regulations and requirements may not address the full spectrum of security concerns associated with this program and associated projects. The RPWG will leverage previous security best practices appropriate with this operating environment. In addition, the RPWG will closely coordinate with appropriate members of the Intelligence Community (IC) and Customs and Border Protection (CBP) to perform a continuous security risk assessment and develop recommendations and counter measures to assist in mitigating new or evolving risks associated with this project.

(3) The overall purpose of Operation Security (OPSEC) is to strengthen our traditional security procedures by identifying existing vulnerabilities or weaknesses and applying measures to protect sensitive technologies. The goal is to deny our adversaries access to any critical information. Critical information is technologies and information desired by an adversary that is sensitive and its disclosure could seriously impact the program. The technologies and information does not have to be classified to be of value to an adversary. An adversary can learn a lot about our programs by piecing together

~~For Official Use Only~~

~~For Official Use Only~~

obtainable unclassified information. In our attempt to shield our activities, it is not only important to follow normal security practices but also to implement OPSEC measures as needed. Operation Security should be integrated into every phase of the operation. CBP will be the lead on releasing public information pertaining to the projects. Release of information will be control by CBP and all information pertaining to the project will be protected from public disclosure until it is approved for released by CBP.

(4) The protection of information and information systems against unauthorized access or modification of information, whether in storage, processing, or transit, and against denial of service to authorized users. Information security includes those measures necessary to detect, document, and counter such threats. Information security is composed of computer security and communications security, also called Information Security (INFOSEC). Information about the project should be keep to the unclassified level when possible. If classified information is deemed necessary it will be protected per AR 380-5. A significant amount of program management information will be ~~For Official Use Only (FOUO)~~ and will be protected accordingly.

(5) Contractor and sub-contractor vetting will be accomplished IAW the contract with the National Crime Information Center Interstate Identification Index (NCIC-III) and the Terrorist Screening Database (TSDB) on non-DoD affiliated personnel 18 years of age and older to determine if the person presents a potential threat to the good order, discipline, or health and safety on the project. Contracting officers or their representatives will conduct a compliance review of existing services contracts and all new service contracts to ensure those that exceed the simplified acquisition threshold and do not meet one of the exceptions specified in Federal Acquisition Regulation (FAR) 22.1803 will include FAR 52.222-54 that requires the contractor to enroll in the E-Verify program within thirty (30) calendar days of contract award.

2. Assumptions.

(a) Customs and Border Protection (CBP) is the lead federal agency responsible for the security and operation of our nation's borders. As the customer, CBP maintains overall responsibility for the TF Southwest Border program.

(b) USACE through TF Southwest Border is providing interagency support to CBP IAW the Economy Act to deliver tactical infrastructure to enhance the ability of Border Patrol to execute its mission on the southwest border. USACE is responsible for the security of USACE personnel, assets, and facilities directly owned by USACE in support of this project

~~For Official Use Only~~

~~For Official Use Only~~

(c) Contractors, in accordance with contract language, shall be fully responsible for ensuring the security of contract personnel, contractor operations, contractor owned assets, contractor owned facilities, and project construction sites.

3. Mission

(a) To continuously execute a comprehensive security program which is capable of detecting, deterring, defending against, and/or mitigating both non-specific and specific threats against personnel, assets, infrastructure, and facilities. The TF Southwest Border Project security program will rely on three broad scope foundational pillars.

- Oversight of security measures by a USACE multi-division/multi-district Regional Protection Working Group framework.
- Integration of an intelligence centric security integration into Command and program management, planning and direction. Leveraging multi-agency/multi-jurisdictional intelligence sources to collect, analyze, assess and conduct predictive analysis of relevant threat information.
- Integration of a comprehensive risk management process to accurately assess threat, criticality, vulnerability, measurement, and management of risk.

(b) The intent is to ensure that timely and accurate information is available to senior leadership to allow for the development of well-informed and educated security mitigation decisions. Understanding that USACE program and project activities may be conducted within a non-standard working environment, all USACE staff will work to ensure that security is considered at all levels and phases of work.

4. Execution

Commander's Intent. To ensure the security and protection of all USACE personnel, assets, facilities and infrastructure during all phases of the TF Southwestern Border Project, the following security measures will be implemented.

- Develop a security annex which establishes the framework for an comprehensive integrated security management program for execution of the TF Southwestern Border projects.
- Initiate a Regional Protection Working Group responsible for synchronizing security management activities for the program and projects.
- Initiate a risk management process and ensure necessary assessments and analysis are conducted.
- Ensure project security measures and practices are clearly communicated and executed consistently across all USACE Divisions and Districts.

~~For Official Use Only~~

~~For Official Use Only~~

- Develop security Commander's Critical Information Requirements (CCIRs) as well as security Priority Intelligence Requirements (PIRs)
- Ensure that security reporting requirements are clearly defined and understood.
- Ensure information and intelligence sharing relationships are established with partner agencies, law enforcement, and the intelligence community (IC) to ensure timely receipt of threat information.

~~For Official Use Only~~

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: FW: CBP Meeting with EPWID#1

Date: Wed Aug 23 2017 20:55:43 EDT

Attachments:

FYSA (b)(6);(b)(7)(C) and (b)(6);(b)(7)(C) meeting with water District next week. I can't participate -recommended to (b)(6);(b)(7)(C) she have baker on the phone in case design questions come up.

(b)(6);(b)(7)(C) PE

LMI

BPAM Chief Engineer

(b)(6);(b)(7)(C)

Sent from Samsung Galaxy

From: (b)(6);(b)(7)(C)

Sent: Wednesday, August 23, 2017 1:25:45 PM

To: (b) (6)

Cc: (b)(6);(b)(7)(C) (b) (6)

(b)(6);(b)(7)(C) (b) (6)

(b) (6)

Subject: RE: CBP Meeting with EPWID#1

Sounds great! Can you please send me your address and I can add the meeting to the calendar? Thx!

(b)(6);(b)(7)(C)

Chief, Portfolio Management and Analysis (PMA) Branch

Border Patrol & Air and Marine Program Management Office

Mobile: (b)(6);(b)(7)(C)

Office (b)(6);(b)(7)(C)

PMA Sharepoint Site: (b) (7)(E)

(b) (7)(E)

From: (b) (6)

Sent: Wednesday, August 23, 2017 10:51 AM

To: (b)(6);(b)(7)(C)

Cc: (b) (6)

(b) (6) (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) (b) (6)

(b) (6)

(b) (6)

Subject: Re: CBP Meeting with EPWID#1

(b)(6);(b)(7)(C)

Good morning, thanks for the email. Yes, 8/30/2017 during morning hours will work.

How does 10:00 am at the District sound?

Thanks,

(b) (6)

On Aug 23, 2017, at 8:01 AM, (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) wrote:

Good Morning (b) (6)

Would Wednesday, August 30th in the morning work for you? (b) (6) and I will be able to attend in person.

Thanks,

(b)(6);(b)(7)(C)

Chief, Portfolio Management and Analysis (PMA) Branch
Border Patrol & Air and Marine Program Management Office

Mobile: (b)(6);(b)(7)(C)

Office: (b)(6);(b)(7)(C)

PMA Sharepoint Site: (b) (7)(E)

(b) (7)(E)

From: (b) (6)

Sent: Tuesday, August 22, 2017 2:21 PM

To: (b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C) ; (b) (6)

(b) (6) (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) ; (b) (6)

(b) (6)

Subject: RE: CBP Meeting with EPWID#1

Good afternoon, the week of the 28th will work for us here at the district. We can meet here at our office in Clint if that works for you all, Tuesday through Thursday.

Regards,

(b) (6) PE

EPCWID1 I (b) (6)

(b) (6)

PO Box 749 | 13247 Alameda Ave. | Clint, TX 79836-0749

(p) (b) (6) | (f) (b) (6) | (c) (b) (6)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, August 22, 2017 8:42 AM

To: (b) (6)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C) ; (b) (6)

(b) (6)
(b) (6) (b)(6):(b)(7)(C)
(b)(6):(b)(7)(C)

Subject: CBP Meeting with EPWID#1

Good Morning,

As you are probably aware, CBP is working on a project in El Paso to replace existing fence along the IBWC levee. We would like to coordinate a meeting with you all to discuss coordination and logistics associated with the replacement adjacent to the canal and construction of gates (b) (7)(E). If possible, I'd like to coordinate a meeting with you in person either next week (week of the 28th) or the following week (week of the 5th). Please let me know your availability and I look forward to working with you.

Thank you,

(b)(6):(b)(7)(C)
Chief, Portfolio Management and Analysis (PMA) Branch
Border Patrol & Air and Marine Program Management Office
Facilities Management and Engineering
Office of Facilities and Asset Management
Mobile: (b)(6):(b)(7)(C)
Office: (b)(6):(b)(7)(C)

PMA Sharepoint Site: (b) (7)(E)
(b) (7)(E)

From:

To:

Cc:

Bcc:

Subject: RE: Fence Replacement Final RFP Preparation

Date: Wed Aug 23 2017 19:28:25 EDT

Attachments:

Thanks for the update (b)(6);(b)(7)(C)

Best,

(b)(6);(b)(7)(C)

Senior Attorney

Office of Assistant Chief Counsel-Indianapolis

U.S. Customs and Border Protection

6650 Telecom Drive, Suite 100

Indianapolis, Indiana 46278

Direct Line: (b)(6);(b)(7)(C)

Fax: (b)(6);(b)(7)(C)

E-mail: (b)(6);(b)(7)(C)

This document/electronic communication contains communications between attorney and client, communications that are part of the agency deliberative process, or attorney work-product, and as such, it is privileged and confidential. It is intended only for the confidential use of the designated recipient(s) and any U.S. Customs and Border Protection (CBP) Officials who have an official "need to know."

Absent the express prior approval of the Assistant Chief Counsel - Indianapolis, (b)(6);(b)(7)(C) it is not available for release, disclosure, or use by anyone within or outside of CBP other than the aforementioned officials.

-----Original Message-----

From: (b)(6);(b)(7)(C)

Sent: Wednesday, August 23, 2017 7:13 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Fence Replacement Final RFP Preparation

(b) (5)

From: (b)(6);(b)(7)(C)

Sent: Tuesday, August 22, 2017 5:07:31 PM

To: (b)(6);(b)(7)(C)

Cc:

Subject: RE: Fence Replacement Final RFP Preparation

All –

(b) (5)

Thanks!

Best,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Senior Attorney

Office of Assistant Chief Counsel-Indianapolis U.S. Customs and Border Protection

6650 Telecom Drive, Suite 100

Indianapolis, Indiana 46278

Direct Line: (b)(6);(b)(7)(C)

Fax: (b)(6);(b)(7)(C)

E-mail: (b)(6);(b)(7)(C)

This document/electronic communication contains communications between attorney and client, communications that are part of the agency deliberative process, or attorney work-product, and as such, it is privileged and confidential. It is intended only for the confidential use of the designated recipient(s) and any U.S. Customs and Border Protection (CBP) Officials who have an official "need to know."

Absent the express prior approval of the Assistant Chief Counsel - Indianapolis, (b)(6);(b)(7)(C) it is not available for release, disclosure, or use by anyone within or outside of CBP other than the aforementioned officials.

From: (b)(6);(b)(7)(C)

Sent: Monday, August 07, 2017 3:03 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: RE: Fence Replacement Final RFP Preparation

(b)(6);(b)(7)(C)

Speaking with USACE this afternoon, the Decision Point dates below are when we need to have the information for the USACE RFP. Providing it after that date but before RTA might require USACE CT to extend their review time, after RTA would require an Amendment and more time, and after award, well...

So as we get close to the dates we will be sure to coordinate with you and (b)(6);(b)(7)(C)

Thank you,

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, August 07, 2017 1:50 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Fence Replacement Final RFP Preparation

I appreciate it (b)(6);(b)(7)(C) Communication is going to be key!

Best,

(b)(6);(b)(7)(C)

Senior Attorney

Office of Assistant Chief Counsel-Indianapolis U.S. Customs and Border Protection

6650 Telecom Drive, Suite 100

Indianapolis, Indiana 46278

Direct Line: (b)(6);(b)(7)(C)

Fax: (b)(6);(b)(7)(C)

E-mail:

(b)(6);(b)(7)(C)

This document/electronic communication contains communications between attorney and client, communications that are part of the agency deliberative process, or attorney work-product, and as such, it is privileged and confidential. It is intended only for the confidential use of the designated recipient(s) and any U.S. Customs and Border Protection (CBP) Officials who have an official "need to know."

Absent the express prior approval of the Assistant Chief Counsel - Indianapolis, (b)(6);(b)(7)(C) it is not available for release, disclosure, or use by anyone within or outside of CBP other than the aforementioned officials.

From: (b)(6);(b)(7)(C)

Sent: Monday, August 07, 2017 1:49 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Fence Replacement Final RFP Preparation

(b)(6);(b)(7)(C)

The dates below (see table at bottom of this email) provide the dates by project when the RFPs will be developed. That being said there is typically a week or more from the Decision Point to Ready To Advertise (RTA).

I will reach back to USACE and find out the absolute drop dead date for introducing new language to their RFPs relating to the TAA / BAA prior to RTA date. I will get back with you soonest.

Respectfully,

(b)(6);(b)(7)(C)

Eastern Corridors Division Director

Border Patrol and Air Marine Operations Program Management Office Facilities Management and Engineering

Mobile: (b)(6);(b)(7)(C)

Email: (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Monday, August 07, 2017 1:25 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: FW: Fence Replacement Final RFP Preparation

All –

(b) (5), (b)(6); (b)(7)(C)

Best,

(b)(6);(b)(7)(C)

Senior Attorney

Office of Assistant Chief Counsel-Indianapolis U.S. Customs and Border Protection

6650 Telecom Drive, Suite 100

Indianapolis, Indiana 46278

Direct Line: (b)(6);(b)(7)(C)

Fax: (b)(6);(b)(7)(C)

E-mail: (b)(6);(b)(7)(C)

This document/electronic communication contains communications between attorney and client, communications that are part of the agency deliberative process, or attorney work-product, and as such, it is privileged and confidential. It is intended only for the confidential use of the designated recipient(s) and any U.S. Customs and Border Protection (CBP) Officials who have an official "need to know."

Absent the express prior approval of the Assistant Chief Counsel - Indianapolis, (b)(6);(b)(7)(C) it is not available for release, disclosure, or use by anyone within or outside of CBP other than the aforementioned officials.

From: (b)(6);(b)(7)(C)

Sent: Monday, August 07, 2017 8:57 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: FW: Fence Replacement Final RFP Preparation

FYI.

(b)(6);(b)(7)(C)

Senior Attorney

Office of Assistant Chief Counsel, Indianapolis Customs and Border Protection ph. (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

This communication might contain communications between attorney and client, communications that are part of the agency deliberative process, or attorney-work product, all of which are privileged and not subject to disclosure outside the agency or to the public. Please consult with the Office of Assistant Chief Counsel-Indianapolis, U.S. Customs and Border Protection before disclosing any information contained in this email.

From: (b)(6);(b)(7)(C)

Sent: Monday, August 07, 2017 8:55 AM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: FW: Fence Replacement Final RFP Preparation

See below when we need buy American decisions for the FY 17 fence replacement

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Thursday, August 03, 2017 11:29 AM

To: (b)(6);(b)(7)(C)

(b) (6)

(b) (6)

(b) (6) (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b) (6)

Subject: Fence Replacement Final RFP Preparation
Importance: High

Hello PMs,

(b) (5), (b)(6); (b)(7)(C)

Project

Final RFP Prep Activity

Buy American Act Decision

(b) (7)(E)

9 AUG 17 - 18 AUG 17

18 AUG 17

SDC

8 AUG 17 - 29 AUG 17

29 AUG 17

(b) (7)(E)

2 AUG 17 - 13 AUG 17

13 AUG 17

(b)(7)(E)

1 AUG 17 - 12 AUG 17

12 AUG 17

Respectfully,

(b)(6);(b)(7)(C)

Eastern Corridors Division Director
Border Patrol and Air Marine Operations Program Management Office Facilities Management and
Engineering

Mobile: **(b)(6);(b)(7)(C)**

Email **(b)(6);(b)(7)(C)**

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject:

FW: (b) (7)(E) IPT

Date:

Wed Aug 23 2017 19:14:20 EDT

Attachments:

Fya

All times listed are in the following time zone:(UTC-05:00) Eastern Time (US & Canada)

From: (b)(6);(b)(7)(C)

Sent: Thursday, August 17, 2017 3:37:05 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

(b) (6)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: (b) (7)(E) IPT

When: Thursday, August 24, 2017 2:00 PM-3:00 PM.

Where: Call in: (b)(6);(b)(7)(C) Pin: (b) (7)(E)/ Room (b) (7)(E)

Purpose: To discuss current status, upcoming event/milestones, and update action items occurring on the (b) (7)(E) Program

(Previously named (b) (7)(E))

Occurrence: Monthly; Every 4 weeks

Time: 2:00pm – 3:00pm (Eastern)

Room: (b) (7)(E) 1901 S. Bell Street Room (b) (7)(E)

Agenda: To be sent out before each meeting

Contact Information: (b)(6);(b)(7)(C) (Program Manager, (b)(7)(E); (b)(6);(b)(7)(C))

**Please do not forward this invite. If you need to be removed from this invite or would like to add someone, please contact (b)(6);(b)(7)(C).

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: FW: Alignment question

Date: Wed Aug 23 2017 19:10:42 EDT

Attachments:

We can discuss your thoughts tomorrow nite

From: (b)(6);(b)(7)(C)

Sent: Wednesday, August 23, 2017 5:09:59 PM

To: (b)(6);(b)(7)(C)

Cc:

Subject: RE: Alignment question

I'll reach out to (b)(6);(b)(7)(C) who replaced (b)(6);(b)(7)(C) as well as try to get (b)(6);(b)(7)(C) to address.

(b)(6);(b)(7)(C)

LMI

7940 Jones Branch Drive

Tysons, VA 22102

Cell: (b)(6);(b)(7)(C)

Complex Problems. Practical Solutions.

www.lmi.org<<http://www.lmi.org>>

From: (b)(6);(b)(7)(C)

Sent: Wednesday, August 23, 2017 5:04 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Cc: (b)(6);(b)(7)(C)

Subject: [EXTERNAL] RE: Alignment question

(b)(6);(b)(7)(C)

I would like to get this resolved before the 90% review period is up.

Would (b)(6);(b)(7)(C) be a good person to run that up? Who is (b)(6);(b)(7)(C) Replacement? (b)(6);(b)(7)(C)?

I think sector needs to have this discussion and include their HQs so we can put this to bed.

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Wednesday, August 23, 2017 4:54:27 PM

To: (b)(6);(b)(7)(C)

Cc:

Subject: RE: Alignment question

Understand – (b) (5), (b)(6); (b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Wednesday, August 23, 2017 4:50 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Alignment question

(b) (5), (b)(6); (b)(7)(C)

(b)(6);(b)(7)(C)

LMI

7940 Jones Branch Drive

Tysons, VA 22102

Cell: (b)(6);(b)(7)(C)

Complex Problems. Practical Solutions.

www.lmi.org<<http://www.lmi.org>>

From: (b)(6);(b)(7)(C)

Sent: Wednesday, August 23, 2017 4:48 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [EXTERNAL] RE: Alignment question

(b) (5), (b)(6); (b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Wednesday, August 23, 2017 4:46 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Alignment question

Thanks (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

see the traffic below.

(b)(7)(E)

(b)(7)(E)

From: (b)(6);(b)(7)(C)
Sent: Wednesday, August 23, 2017 4:40:23 PM
To: (b)(6);(b)(7)(C)
Subject: FW: Alignment question
FYI

(b)(6);(b)(7)(C)

LMI
7940 Jones Branch Drive
Tysons, VA 22102
Cell: (b)(6);(b)(7)(C)

Complex Problems. Practical Solutions.
www.lmi.org<<http://www.lmi.org>>

From: (b)(6);(b)(7)(C)
Sent: Sunday, August 13, 2017 12:29 AM
To: (b)(6);(b)(7)(C)
Subject: [EXTERNAL] RE: Alignment question

Yes. (b) (5)

(b) (5), (b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Saturday, August 12, 2017 3:39:59 PM
To: (b)(6);(b)(7)(C)
Subject: Alignment questiin

(b)(6);(b)(7)(C) a question came up this week regarding the alignment between the two POEs. I remember on several visits sector saying they wanted to keep the current alignment (b)(7)(E)
(b) (5)

Thanks

Sent using OWA for iPhone

From:

(b)(6);(b)(7)(C)

To:

Cc:

Bcc:

Subject: RE: Alignment question

Date: Wed Aug 23 2017 17:22:48 EDT

Attachments:

Thank you sir.

From: (b)(6);(b)(7)(C)

Sent: Wednesday, August 23, 2017 5:09:59 PM

To: (b)(6);(b)(7)(C)

Cc:

Subject: RE: Alignment question

I'll reach out to (b)(6);(b)(7)(C) who replaced (b)(6);(b)(7)(C) as well as try to get (b)(6);(b)(7)(C) to address.

(b)(6);(b)(7)(C)

LMI

7940 Jones Branch Drive

Tysons, VA 22102

Cell: 703-409-4241

Complex Problems. Practical Solutions.

www.lmi.org

From: (b)(6);(b)(7)(C)

Sent: Wednesday, August 23, 2017 5:04 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)
Cc: (b)(6);(b)(7)(C)
Subject: [EXTERNAL] RE: Alignment question

(b)(6);(b)(7)(C)

I would like to get this resolved before the 90% review period is up.

Would (b)(6);(b)(7)(C) be a good person to run that up? Who is (b)(6);(b)(7)(C) Replacement? (b)(6);(b)(7)(C)?

I think sector needs to have this discussion and include their HQs so we can put this to bed.

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Wednesday, August 23, 2017 4:54:27 PM
To: (b)(6);(b)(7)(C)
Cc: (b)(6);(b)(7)(C)
Subject: RE: Alignment question

Understand – (b) (5), (b)(6); (b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)
Sent: Wednesday, August 23, 2017 4:50 PM
To: (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
Subject: RE: Alignment question

(b) (5)

(b)(6);(b)(7)(C)

LMI
7940 Jones Branch Drive
Tysons, VA 22102
Cell: (b)(6);(b)(7)(C)

Complex Problems. Practical Solutions.
www.lmi.org

From: (b)(6);(b)(7)(C)

Sent: Wednesday, August 23, 2017 4:48 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: [EXTERNAL] RE: Alignment question

(b)(5), (b)(6); (b)(7)(C)

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

From: (b)(6);(b)(7)(C)

Sent: Wednesday, August 23, 2017 4:46 PM

To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: RE: Alignment question

Thanks (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

see the traffic below.

(b)(7)(E)

From: (b)(6);(b)(7)(C)

Sent: Wednesday, August 23, 2017 4:40:23 PM

To: (b)(6);(b)(7)(C)

Subject: FW: Alignment question

FYI

(b)(6);(b)(7)(C)

LMI
7940 Jones Branch Drive
Tysons, VA 22102
Cell: (b)(6); (b)(7)(C)

Complex Problems. Practical Solutions.
www.lmi.org

From: (b)(6);(b)(7)(C)
Sent: Sunday, August 13, 2017 12:29 AM
To: (b)(6);(b)(7)(C)
Subject: [EXTERNAL] RE: Alignment question

Yes. (b) (5), (b) (7)(E)

From: (b)(6);(b)(7)(C)
Sent: Saturday, August 12, 2017 3:39:59 PM
To: (b)(6);(b)(7)(C)
Subject: Alignment questiin

(b)(6);(b)(7)(C) a question came up this week regarding the alignment between the two POEs. I remember on several visits sector saying they wanted to keep the current alignment (b) (5), (b) (7)(E)

Thanks

Sent using OWA for iPhone
